



I-294 AT I-290/I-88 INTERCHANGE

Jeff Allen, *Deputy Chief of Program Implementation*

October 2025

CENTRAL TRI-STATE TOLLWAY (I-294) PROJECT

2025 *Current Status*



97%

Design complete

87%


Construction complete

164 contracts
awarded

- 72 active contracts
- 92 contracts closed out



I-294 AT I-290/I-88 INTERCHANGE OVERVIEW

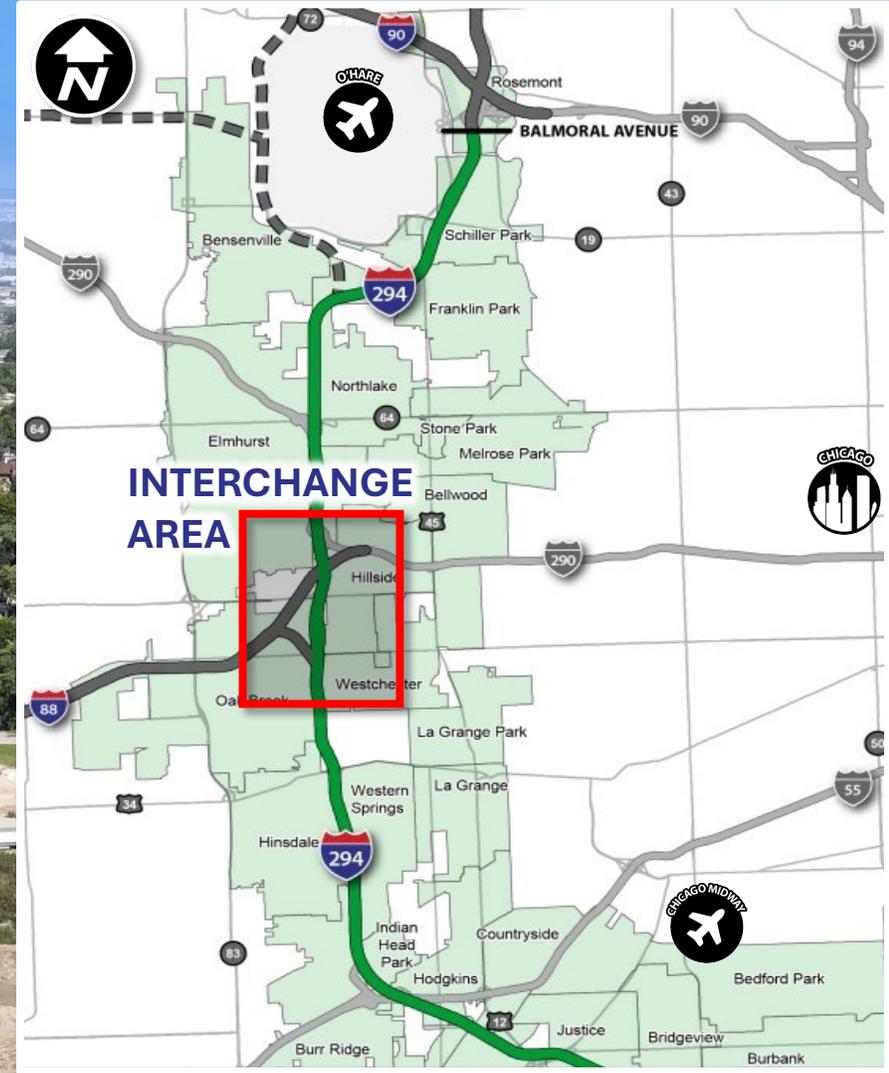

\$700 million project to provide congestion relief and operational improvements

I-294 AT I-290/I-88 INTERCHANGE

Project Complexities



#1

**congested
interchange**
on Tollway system

300,000

daily vehicles
(18% trucks)

15+

**local municipalities
and agencies**


WORK TO DATE

Five contracts worth approximately \$652 million awarded to date

\$147.7 million paid to DBE firms

\$4.9 million paid to veteran-owned firms

130 unique firms involved in project




PROJECT BEGAN IN 2020,
TWO YEARS AHEAD OF SCHEDULE

CONSTRUCTION PROGRESS



**ComEd
Relocation**

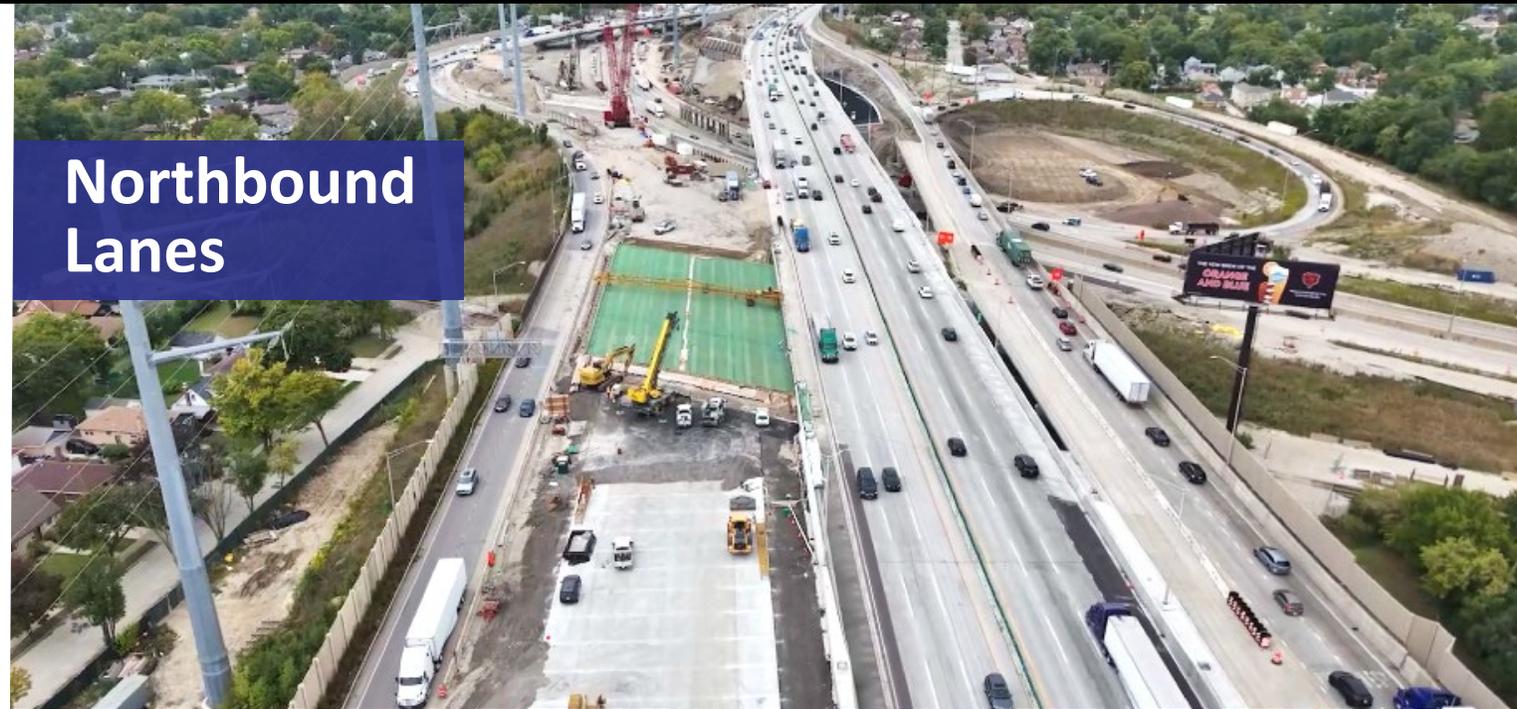

**Northbound
Lanes**



**Auxiliary
Lanes**

CURRENT CONSTRUCTION

Southbound lanes

Untangling the weave from EB I-290 to SB I-294/WB I-88

NB I-294 to WB I-290 fly-under ramp




EB I-290 to SB I-294/WB I-88

NB I-294 to WB I-290



CURRENT CONSTRUCTION

Untangling the weave: EB I-290 to SB I-294/WB I-88

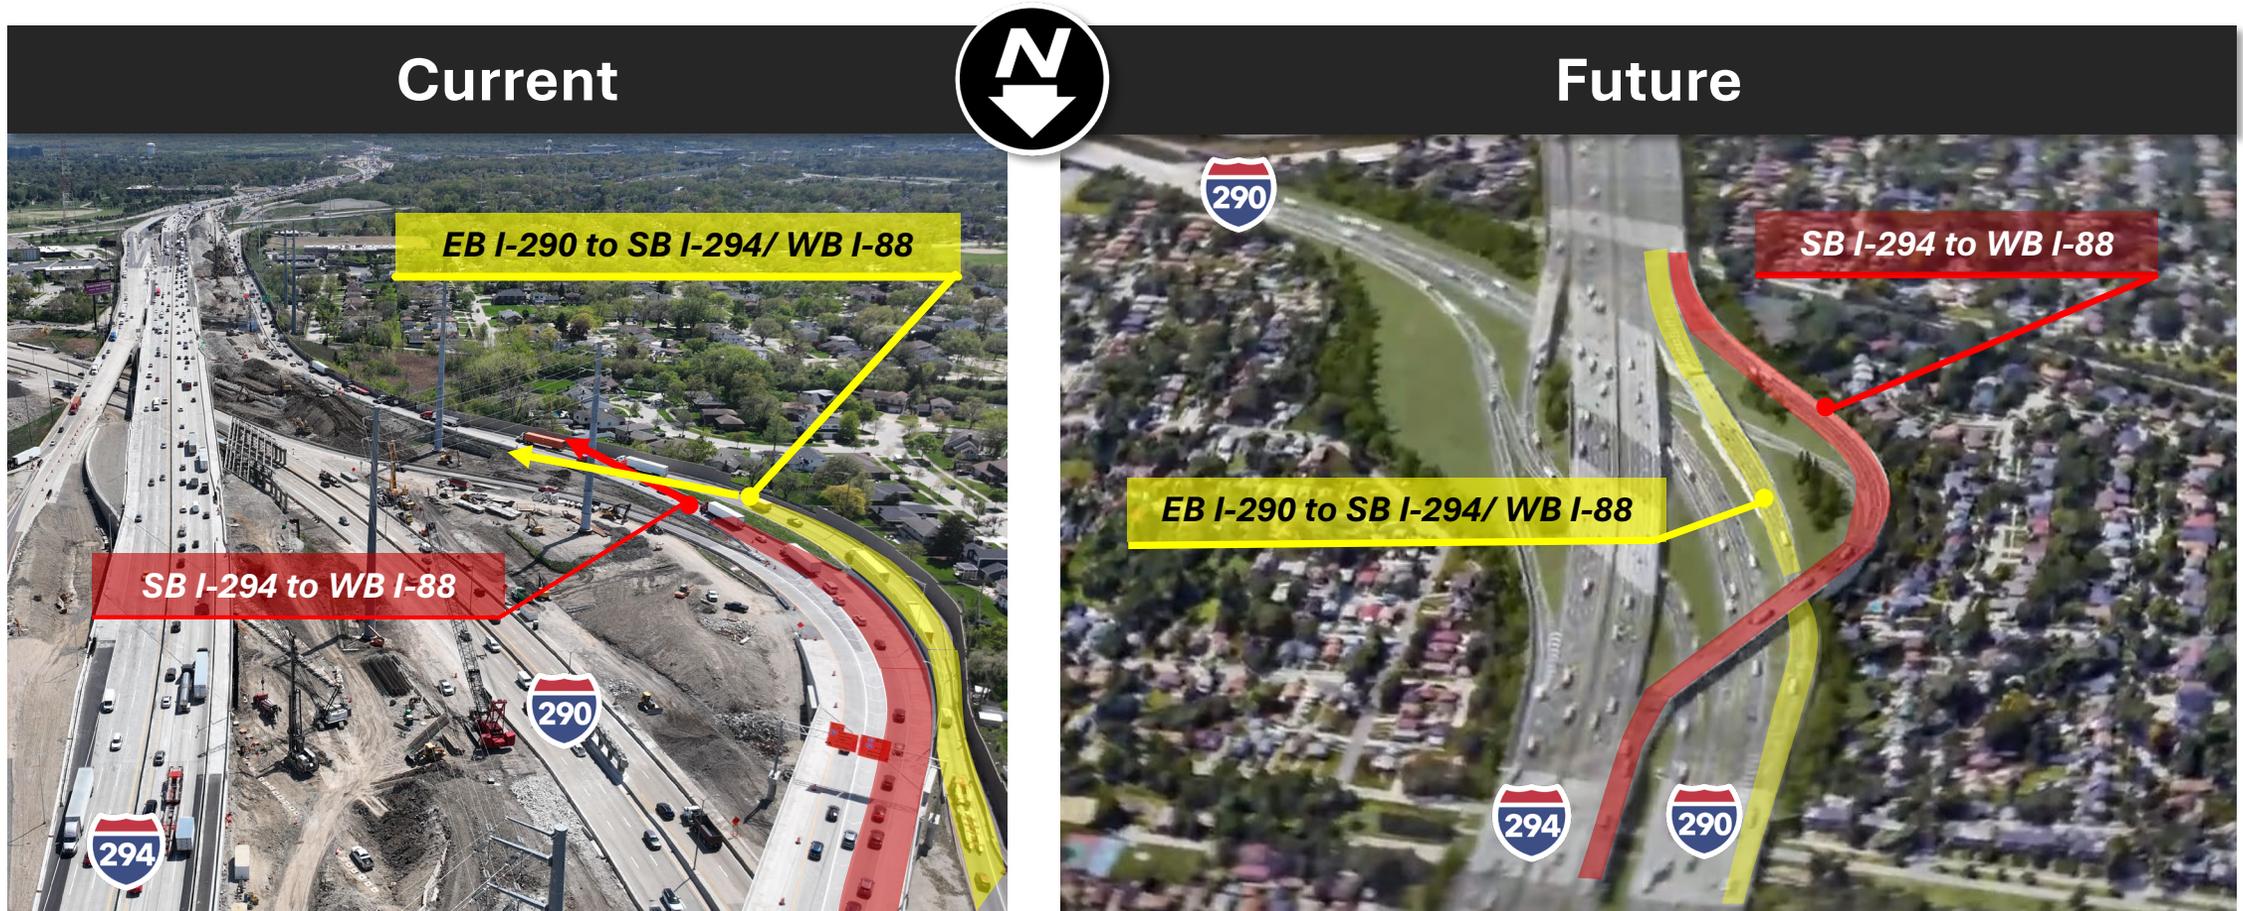

CURRENT CONSTRUCTION

NB I-294 to WB I-290 fly-under ramp



I-290/I-88 INTERCHANGE DRONE VIDEO PLACEHOLDER
Roosevelt Road to I-290



THANK YOU
