



CENTRAL TRI-STATE TOLLWAY (I-294) CONSTRUCTION UPDATE

Manar Nashif, *Chief Engineering Officer*
September 2024

CENTRAL TRI-STATE TOLLWAY PROJECT STATUS



\$3.2 billion

spent

\$4 billion project budget

165

contracts awarded

70 contracts closed out

95


active contracts

Design, construction, inspection, other*





MAJOR HIGHLIGHTS

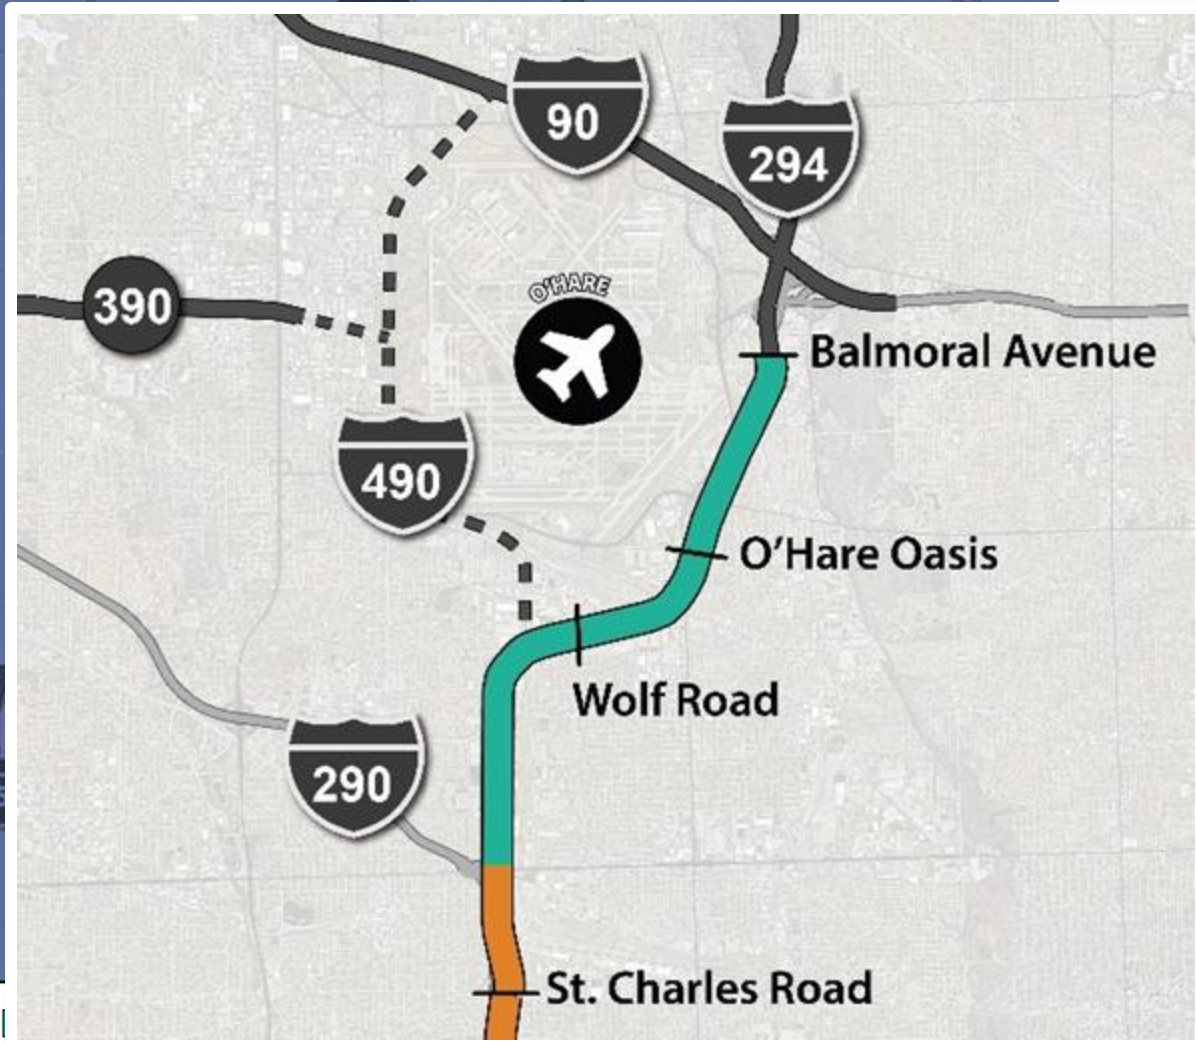

Construction

North section



WORK COMPLETED

Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



ACTIVE TRAFFIC MANAGEMENT


14

SmartRoad gantries installed between Rosemont and Elmhurst




I-90 SmartRoad



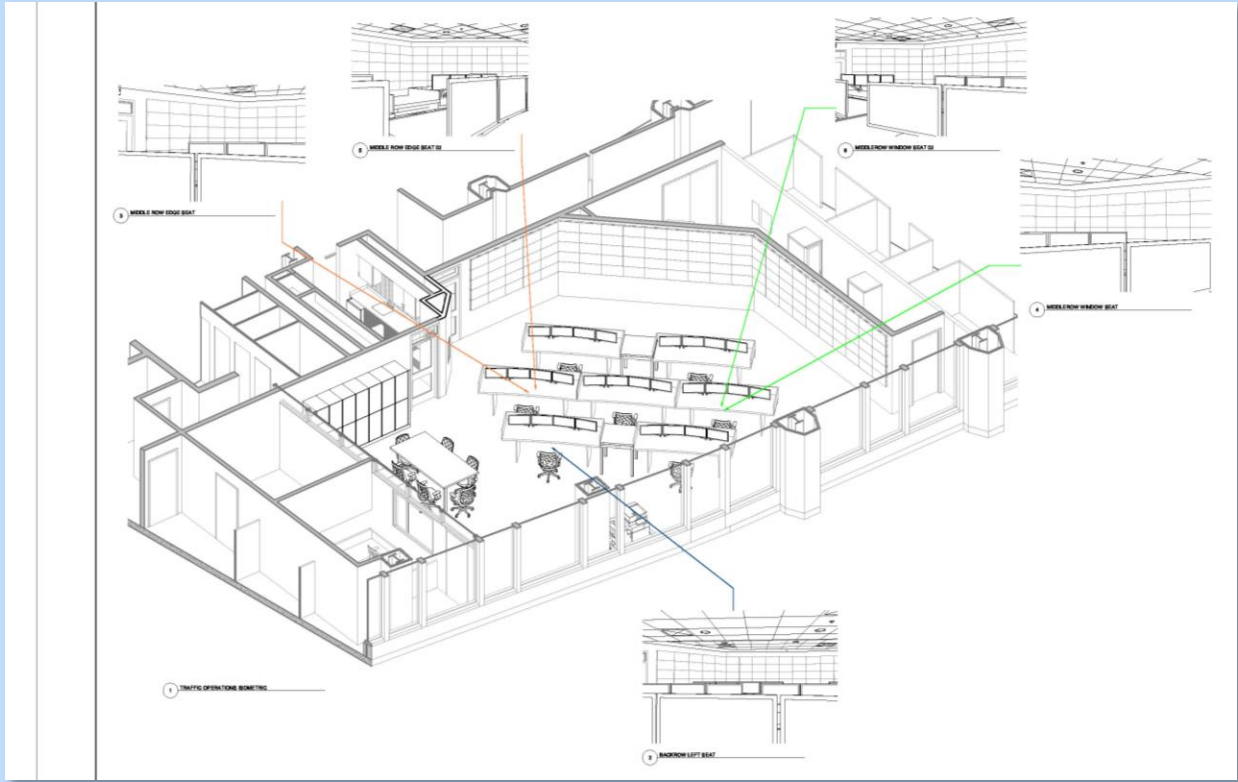

TRAFFIC OPERATIONS CENTER/ DISPATCH IMPROVEMENTS

I-490/I-294 INTERCHANGE PROJECT

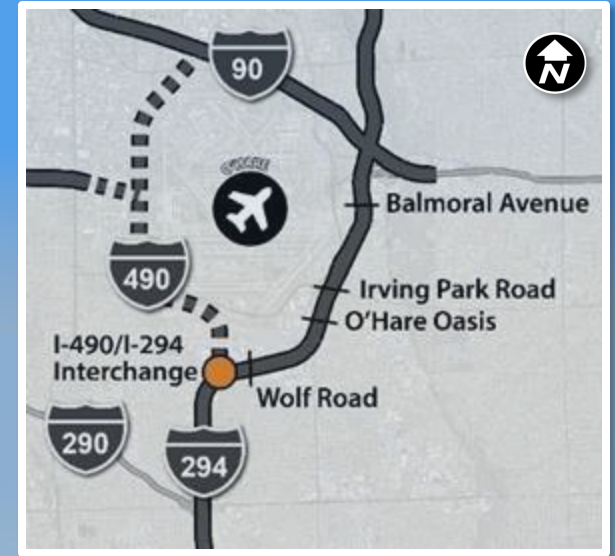

33

miles of lane paving

Nearly 15 million

pounds of structural steel

Nearly 500,000

cubic yards of grading



I-490/I-294 INTERCHANGE PROJECT



ECONOMIC DEVELOPMENT

City of Northlake

- New development along Northwest Avenue

City of Elmhurst

- New development along County Line Road

North Avenue Interchange

- Partnership with Cook County and Cities of Elmhurst and Northlake
- County Line Road ramp opening 2025





THANK YOU

Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290



Fifth lane open on SB I-294 between Irving Park Road and WB I-290





CONSTRUCTION UPDATES

