PROFESSIONAL SERVICES BULLETIN 26-4

ADDENDUM No. 2

ADDENDUM No. 2 does not change the due date or time

STATEMENTS OF INTEREST (SOIs) are due by 4:30:00 p.m. (Central Time)

Due Date: October 30, 2026

Successful Firm(s) will be notified.

Overall results will be posted on the Illinois Chief Procurement Officer's eProcurement System at: https://www.bidbuy.illinois.gov/

Professional Services Bulletin

No. 26-4 Addendum No. 2 October 19, 2026

ILLINOIS TOLLWAY website: www.illinoistollway.com

Illinois Tollway
2700 Ogden Avenue, Downers Grove, IL 60515

ADDENDUM No. 2
REVISION DATE: October 19, 2026
PROFESSIONAL SERVICES BULLETIN
No. 26-4

Addendum No. 2 does not change the due date or time that Statements of Interest are due. Statements of Interest are due via the Trimble Unity Construct process: https://app.e-builder.net/ to the Illinois State Toll Highway Authority by 4:30:00 PM Central Time, October 30, 2026.

The following revisions are being made via Addendum No.2 to Professional Services Bulletin (PSB) No. 26-4. The bulletin is being reissued in its entirety with changes noted and shall supersede all prior versions. If you downloaded the bulletin prior to the noted Addendum/Revision Date, you should incorporate the revisions or download and use a new copy of the bulletin. The revisions being made through this addendum include the following:

- The item description for Item 2 has been updated to correct Keslinger Road.
- The scope and pre-qualifications for Item 3 have been revised to address plaza design.
- The scope for Item 6 has been revised to remove structural design and clarify maintenance of traffic.
- The scope and pre-qualifications for Item 7 have been revised to clarify the westbound roadway and include structural pre-qualification.
- The item title, pre-qualifications and goals for Item 12 have been revised.
- The Pre-Proposal Meeting Presentation and Attendee List are included. A recording of the Pre-Proposal Meeting is available at https://www.bidbuy.illinois.gov/.

QUESTIONS: The Tollway has received the following questions pertaining to PSB 26-4 via the SOI Mailbox. The Tollway offers the following responses:

Question 1: For Item 13 (I-26-40002), Tri-State Tollway (I-94), Active Traffic Management System Installation, Phase II Engineering Services, the scope of work references “geotechnical services as required to support the above items.” However, geotechnical services are not listed as a required prequalification. Will the Tollway be providing geotechnical services for this contract, or should firms include geotechnical services as part of their proposed team?

Answer: Geotechnical services are required as part of the scope for this item and will not be provided separately.

Question 2: For Items 7, 8, 9, and 10, topographic survey is not identified in the scope of work and is not listed as a required prequalification. Is topographic survey anticipated to be part of the required scope for these items?
Answer: Survey is required as part of the scope for these items and will not be provided separately.

Question 3: Section 3.3.2.3, Item 1.G requires a current certification letter demonstrating that each proposed DBE/VOSB firm is certified in the scope(s) of work stated in the SOI and LOI, and notes that IDOT prequalification in the respective scope will satisfy this requirement. Section 3.4.4 separately

requires DBE/VOSB certification letters to be submitted as DBE_VOSB_Certs.pdf. Please clarify where firms should submit documentation demonstrating certification or prequalification in the assigned scope of work, including any applicable IDOT prequalification documentation.
Answer: Please use the Documents tab to attach any additional documentation. See the Trimble Unity Construct Web-Based Project Management System User Manual for instructions on how to attach files.

Question 4: If we propose a two-firm team, can the non-managing partner (non-DBE firm) serve as the mentor to the managing partner/team lead (DBE firm) under a Reverse P4G, or must the mentor be a subconsultant rather than a prime partner?
Answer: Yes, the non-lead Team member may mentor the lead Team member as long as the Protégé is a M/W/DBE or VOSB certified firm.

Question 5: Please indicate if any of the items shall include survey under the Phase II Engineering services.

Answer: Survey is required as part of the scope for these items and will not be provided separately.

Question 6: In addition to the key personnel specifically identified in the item ad, are consultants permitted to include resumes for other relevant staff?

Answer: Please see section 3.3.2.1 regarding Exhibit A. Include resumes of item specific key personnel.

Question 7: Regarding Item 5, since this project could potentially take place on both IDOT and Tollway property, which standards for soil classification, handling, and disposal will be used and where?

Answer: Excavation is not planned to be completed on IDOT property.

NEW TO THIS PSB

An optional In-Person Networking and Pre-Proposal Meeting (with a virtual option) will be held on Thursday October 15, 2026 at the following times and location:

Networking: 2:30 pm – 3:15 pm (CT)
Pre-Proposal Meeting: 3:15 pm (CT)
Marriott Chicago Naperville
1801 N. Naper Blvd.
Naperville, IL 60563

Register here: PSB 26-4 Pre-Proposal Meeting

Please note that registration for this event is required and can be completed using the link above.

e-Builder is now Trimble Unity Construct. If you are currently registered in e-Builder, your user ID will be active in Trimble Unity Construct.

TABLE OF CONTENTS

PART I: THE SCHEDULE

1.1	CONTACT INFORMATION	3
1.2	OFFICIAL NOTICE	3-4
1.3	ACCEPTANCE OF SCANNED SIGNATURES	4
1.4	PSB ITEM INDEX	5
1.5	PSB ITEM DETAILS	A-1 – A-26

PART II: CONTRACT CLAUSES AND REQUIREMENTS

2.1	CONSULTANT/SUBCONSULTANT CONFLICTS OF INTEREST WITHIN TOLLWAY PROJECTS	6
2.2	INSPECTOR GENERAL	7
2.3	FINANCIAL INFORMATION	7-8
2.4	ILLINOIS TOLLWAY'S CONTRACT PAYMENT POLICY	8
2.5	DISADVANTAGED BUSINESS ENTERPRISE (DBE) PARTICIPATION	8-10
2.6	PARTNERING FOR GROWTH PROGRAM GUIDELINES	10
2.7	STATE OF ILLINOIS VETERAN SMALL BUSINESS PARTICIPATION AND UTILIZATION PLAN	10-11
2.8	TEAMING AGREEMENT	11-12
2.9	MANUALS, PROCESSES AND GUIDELINES	12
2.10	PHASE II: DESIGN ENGINEERING SERVICES	12
2.11	PHASE III: CONSTRUCTION ENGINEERING SERVICES	12-13
2.12	CONSTRUCTION AND QUALITY ASSURANCE CONSULTANTS	13
2.13	QUALITY ASSURANCE PREQUALIFICATION CATEGORY	13
2.14	CLARIFICATION OF QUALITY CONTROL/QUALITY ASSURANCE REQUIREMENTS	13
2.15	CONSULTANT CONTRACT FORMS	14
2.16	SELF-PERFORMANCE	14

PART III: REPRESENTATIONS AND INSTRUCTIONS

3.1	SELECTION CRITERIA	14
3.2	SCHEDULE FOR CONSULTANT SELECTION	15
3.3	GUIDELINES FOR SUBMITTING SOI	15-17
3.4	SUBMITTAL INSTRUCTIONS	17-22
3.5	DISCLOSURES AND CERTIFICATIONS	23
3.6	PROTEST PROCEDURE	24
3.7	USEFUL LINKS	25
3.8	ILLINOIS EPROCUREMENT BIDBUY NOTICE	25
3.9	INFORMATION ON ACCESSING THE ILLINOIS TOLLWAY WEBSITE	26
3.10	FUTURE PROFESSIONAL SERVICES BULLETIN NOTIFICATIONS	27
3.11	RESERVED	27
3.12	EXCHANGES WITH FIRMS AFTER SOI SUBMISSION	28

PART I: THE SCHEDULE

1.1 CONTACT INFORMATION

Illinois State Toll Highway Authority (ISTHA)
2700 Ogden Avenue
Downers Grove, IL 60515

PSB 26-4 Coordinator: csstaff@getipass.com

PSB 26-4 Tech Support: support@wbpmsupport.zendesk.com

PSB 26-4 Trimble Unity Construct Training: PSB SOI Submission Training

1.2 26-4 OFFICIAL NOTICE

This Professional Services Bulletin 26-4 (PSB 26-4**)** is the official notice of needed professional services for the Illinois State Toll Highway Authority ("Illinois Tollway", "Tollway"), as authorized by the Architectural, Engineering, and Land Surveying Qualifications Based Selection Act, (30 ILCS 535/1, *et seq.*). This PSB contains information pertaining to the advertisement for Statements of Interest (SOI) and is part of the Chief Procurement Officer eProcurement System for the Illinois State Toll Highway Authority. PSB **26-4**, including all Exhibits and forms, is available on the Illinois Tollway's website at Illinois Tollway Professional Service Bulletin. Additional information is also posted on the Illinois Chief Procurement Officer's eProcurement System at: Illinois BidBuy. For instructions on accessing the Illinois Tollway website, PSB, and Exhibits please refer to the Table of Contents. Instructions on receiving procurement opportunities are included in the "Illinois eProcurement BidBuy Notice" section of this PSB.

1.2.1 PSB 26-4 SUMMARY

Information for the Trimble Unity Construct process for PSB **26-4** can be found in the Public Folder at: Statement of Interest (SOI) Training, FAQs, etc.

You will need the following before you can submit an SOI in Trimble Unity Construct:

- Trimble Unity Construct resources, including PSB SOI user manual, FAQ file, and videos (see Public Folder link above)
- Webinar Training (see Section 3.7 Useful Links for training webinar registration link)
- Trimble Unity Construct Login ID (see Section 3.4 Submittal Instructions)
- Firm Code Name (see Section 3.4 Submittal Instructions)

An optional In-Person Pre-Proposal Meeting (with a virtual option) will be held on Thursday October 15, 2026, at 3:15 p.m. (CT) at the following location:

Marriott Chicago Naperville
1801 N. Naper Blvd.
Naperville, IL 60563

Register here: PSB 26-4 Pre-Proposal Meeting

Please note that registration for this event is required and can be completed using the link above.

All questions related to this PSB must be submitted electronically through the Trimble Unity Construct SOI

Mailbox at **PSB_26-4_Questions_and_RFIs@docs.e-builder.net** no later than **October 21, 2026 at 4:30:00 pm** (**CT**). The subject line should read: PSB 26-4 Question. Answers will be addressed via an Addendum published on the Tollway website and the Illinois eProcurement site, BidBuy. For Trimble Unity Construct technical questions, please contact the Trimble Unity Construct PSB Tech Support: support@wbpmsupport.zendesk.com.

This is not an invitation for bids. Consultants properly prequalified for the projects listed herein may indicate their desire to be considered for selection by submitting an SOI to the Illinois Tollway via the Trimble Unity Construct PSB **26-4** SOI process.

The Illinois Tollway follows the Qualifications Based Selection (QBS) process mandated by Illinois statute (30 ILCS 535)**:** Architectural, Engineering, and Land Surveying Qualifications Based Selection Act for selecting qualified Consultants under this PSB.

1.3 ACCEPTANCE OF SCANNED SIGNATURES

Unless otherwise specified, the parties agree that proposals, contracts, certifications and disclosures, and other contract related documents to be entered into in connection with the resulting contract will be considered signed when the signature of a party is delivered by scanned image (e.g. .pdf or .tiff file extension name) as an attachment to the Trimble Unity Construct PSB SOI process. Such scanned signature will be treated in all respects as having the same effect as an original signature.

1.4 PROFESSIONAL SERVICES BULLETIN NO. 26-4 ITEM INDEX

No.	Project No. / County	Description	Page No.
1	I-26-20000 Ogle, DeKalb and Kane Counties	**Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, IL Route 251 to IL Route 56, Design Corridor Manager and Phase II Engineering Services**	A1-A2
2	I-26-20001 Kane and DeKalb Counties	**Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, Somonauk Road to Dauberman Road, Phase II Engineering Services**	A3-A4
3	I-26-20002 DeKalb County	**Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, Shabbona Road to Somonauk Road, Phase II Engineering Services**	A5-A6
4	I-26-20003 Ogle and DeKalb Counties	**Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, IL Route 251 to Shabbona Road, Phase II Engineering Services**	A7-A8
5	RR-26-30000 Cook County	**Tri-State Tollway (I-294), Roadway and Bridge Rehabilitation, 171st Street to 159th Street, Phase II Engineering Services**	A9-A10
6	RR-26-40000 Cook County	**Tri-State Tollway (I-94), Roadway Rehabilitation, I-294 to Edens Expressway, Phase II Engineering Services**	A11-A12
7	I-26-20004 DuPage County	**Reagan Memorial Tollway (I-88), Roadway Widening, Highland Avenue to IL Route 83, Phase II Engineering Services**	A13-A14
8	I-26-70000 Cook County	**Illinois Route 390 Tollway (IL 390), Bridge Reconstruction at Roselle Road, Phase II Engineering Services**	A15-A16
9	I-26-40001 Lake County	**Tri-State Tollway (I-94), Bridge Reconstruction at Atkinson Road and Everett Road, Phase II Engineering Services**	A17-A18
10	I-26-50000 Winnebago County	**Jane Addams Memorial Tollway (I-90), Bridge Reconstruction, Rockton Road to Rote Road, Phase II Engineering Services**	A19-A20
11	I-26-50001 Winnebago, Boone, McHenry and Kane Counties	**Jane Addams Memorial Tollway (I-90), Fiber Optic System Improvements, from Rockton Road to Plaza 9 (Elgin Plaza), Phase II Engineering Services**	A21
12	I-26-10000 DuPage County	**Veterans Memorial Tollway (I-355), Pre-Concept Design and Noise Abatement Wall Reconstruction, I-55 to Army Trail Road, Phase II Engineering Services**	A22-A23
13	I-26-40002 Lake County	**Tri-State Tollway (I-94), Active Traffic Management System Installation, Phase II Engineering Services**	A24
14	I-26-60000 Cook County	**Tri-State Tollway (I-294), Interchange Improvements at Irving Park Road, Phase II Engineering Services**	A25-A26

1.5 PSB ITEM DETAILS

1.5.1 Item 1: I-26-20000, Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, IL Route 251 to IL Route 56, Design Corridor Manager and Phase II Engineering Services.

This project has a 25% D/M/WBE participation goal and 3% VOSB participation goal.

Design Corridor Management (DCM) services are required for roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88) corridor from IL Route 251 to IL Route 56, MP 76.0 to MP 113.6, in Ogle, DeKalb and Kane Counties, Illinois. This project also includes phase II engineering services for the preparation of engineering studies, contract drawings, specifications and project related permits for roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88) from Dauberman Road to IL Route 56, MP 104.8 to MP 113.6, in Kane County, Illinois.

Design Corridor Management Services

The DCM will provide support and guidance to the corridor Design Section Engineers (DSE) and serve as the single point of contact for DSE contracts in the corridor. DCM services generally encompass the following tasks:

- Agency coordination – Coordinate with stakeholders, including IDOT, county and municipal agencies, as well as regulatory agencies, railroads and utilities as required to secure approvals, agreements and permits. The DCM shall also coordinate with these agencies as necessary where land acquisition is required.
- Design coordination – Provide design review and management support to the Tollway for overseeing DSE work. This includes reviewing DSE submittals for consistency with adjacent DSE sections and compliance with corridor-wide requirements. The DCM will coordinate the overall review process with the Tollway as well as all involved external reviewing agencies and stakeholders and facilitate issue resolution and comment disposition.
- Construction coordination – Work with the construction management teams to assist in resolution of construction issues, review proposed modifications during construction, obtain field condition information and review proposed construction staging and scheduling during the design phase.

Phase II Engineering Services

The work generally encompasses roadway reconstruction and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Signing and pavement marking design
- ITS design
- Roadway lighting design
- Geotechnical services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- I-88 over Blackberry Creek (2 structures)
- I-88 over Welch Creek (culvert)
- I-88 over Lake Run (culvert)
- IL Route 47 over I-88
- Bliss Road over I-88
- US 30 / IL Route 56 over I-88

Construction Estimate: Category F

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Typical)
Special Studies (Location Drainage)
Hydraulic Reports (Waterways: Typical)
Environmental Reports (Environmental Assessment)
Special Services (Surveying)

The Tollway will allow a Prime Consultant to meet the prequalification for Special Studies (Location Drainage), Hydraulic Reports (Waterways: Typical), Environmental Reports (Environmental Assessment) and Special Services (Surveying) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Drainage designer, who will be responsible for drainage design related issues (must be an Illinois Licensed Professional Engineer).
- The Environmental Lead (EL), who will be responsible for coordinating the DSE team's environmental studies.
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 42 months after authorization to proceed inclusive of completion of DCM and Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.2 Item 2: I-26-20001, Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, Somonauk Road to Dauberman Road, Phase II Engineering Services.

This project has a 25% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88) from Somonauk Road to Dauberman Road, MP 95.6 to MP 104.8, in Kane and DeKalb Counties, Illinois.

The work generally encompasses roadway reconstruction and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Signing and pavement marking design
- ITS design
- Geotechnical services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- Somonauk Road over I-88
- Hinckley Road over I-88
- Keslinger Road over I-88
- Watson Road over I-88
- I-88 over Young Creek (culvert)
- I-88 over Big Rock Creek (culvert)

Construction Estimate: Category F

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Typical)
Special Studies (Location Drainage)
Environmental Reports (Environmental Assessment)
Special Services (Surveying)

The Tollway will allow a Prime Consultant to meet the prequalification for Special Studies (Location Drainage), Environmental Reports (Environmental Assessment) and Special Services (Surveying) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).

- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Drainage designer, who will be responsible for drainage design related issues (must be an Illinois Licensed Professional Engineer).
- The Environmental Lead (EL), who will be responsible for coordinating the DSE team's environmental studies.
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 42 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.3 Item 3: I-26-20002, Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, Shabbona Road to Somonauk Road, Phase II Engineering Services.

This project has a 25% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88) from Shabbona Road to Somonauk Road, MP 85.4 to MP 95.6, in DeKalb County, Illinois.

The work generally encompasses roadway reconstruction and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Signing and pavement marking design
- ITS design
- Roadway lighting design
- Plaza design
- Geotechnical services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- I-88 over Kishwaukee River (2 structures)
- Walkway for Plaza 66 (DeKalb Plaza) over I-88 at MP 86.25
- I-88 over IL Route 23 (2 structures)
- I-88 over Union Pacific Railroad (2 structures)
- Shabbona Road over I-88
- University Road over I-88
- Annie Glidden Road over I-88
- South First Street over I-88
- DeKalb Oasis Ramp bridge over I-88
- Peace Road over I-88
- Culvert at MP 87.2
- Culvert at MP 89.3

The following plazas are anticipated to be included in this project:

- Peace Road Plaza 65
- DeKalb Plaza 66

Construction Estimate: Category F

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Typical)
Special Studies (Location Drainage)
Environmental Reports (Environmental Assessment)

Special Services (Surveying)
Special Services (Electrical Engineering)

The Tollway will allow a Prime Consultant to meet the prequalification for Special Studies (Location Drainage), Environmental Reports (Environmental Assessment), Special Services (Surveying) and Special Services (Electrical Engineering) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Drainage designer, who will be responsible for drainage design related issues (must be an Illinois Licensed Professional Engineer).
- The Environmental Lead (EL), who will be responsible for coordinating the DSE team's environmental studies.
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 42 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.4 Item 4: I-26-20003, Reagan Memorial Tollway (I-88), Roadway Reconstruction and Bridge Rehabilitation, IL Route 251 to Shabbona Road, Phase II Engineering Services.

This project has a 25% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88) from IL Route 251 to Shabbona Road, MP 76.0 to MP 85.4, in Ogle and DeKalb Counties, Illinois.

The work generally encompasses roadway reconstruction and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Signing and pavement marking design
- ITS design
- Roadway lighting design
- Geotechnical services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- I-88 over IL Route 251 (2 structures)
- I-88 over Burlington Northern Santa Fe Railroad (2 structures)
- Culvert at MP 76.0
- Culvert at MP 83.4
- Main Street over I-88
- Mulford Road over I-88
- Locust Road over I-88
- Woodlawn Road over I-88
- Tower Road over I-88
- Willrett Road over I-88

Construction Estimate: Category F

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Typical)
Special Studies (Location Drainage)
Environmental Reports (Environmental Assessment)
Special Services (Surveying)

The Tollway will allow a Prime Consultant to meet the prequalification for Special Studies (Location Drainage), Environmental Reports (Environmental Assessment) and Special Services (Surveying) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Drainage designer, who will be responsible for drainage design related issues (must be an Illinois Licensed Professional Engineer).
- The Environmental Lead (EL), who will be responsible for coordinating the DSE team's environmental studies.
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 42 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.5 Item 5: RR-26-30000, Tri-State Tollway (I-294), Roadway and Bridge Rehabilitation, 171st Street to 159th Street, Phase II Engineering Services.

This project has a 24% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for proposed roadway, bridge rehabilitation and plaza improvements on the Tri-State Tollway (I-294) from 171st Street to 159th Street, MP 4.9 to MP 6.2, in Cook County, Illinois.

The work generally encompasses roadway and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Interchange design
- Tolling and toll plaza design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- ITS design
- Signing and pavement marking design
- Geotechnical services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- I-294 over Prairie Creek/Calumet Ditch (culvert)
- Westbound I-80 Ramp over I-294
- 167th Street over I-294

The following plazas are anticipated to be included in this project:

- I-80 West Plaza 43
- I-80 East Plaza 45

Construction Estimate: Category B

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Advanced Typical)
Special Services (Electrical Engineering)
Special Services (Surveying)

The Tollway will allow a Prime Consultant to meet the prequalification for Structures (Highway: Advanced Typical), Special Services (Electrical Engineering) and Special Services (Surveying) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).

- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Electrical designer, who will be responsible for electrical design related issues (must be an Illinois Licensed Professional Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 36 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.6 Item 6: RR-26-40000, Tri-State Tollway (I-94), Roadway Rehabilitation, I-294 to Edens Expressway, Phase II Engineering Services.

This project has a 24% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for proposed roadway rehabilitation on the Tri-State Tollway (I-94) from I-294 to the Edens Expressway, MP 25.3 to MP 30.2, in Cook County, Illinois.

The work generally encompasses roadway and bridge rehabilitation and shall include, but not be limited to, the following items:

- Roadway design
- Tolling and toll plaza design
- Maintenance of traffic design
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- ITS design
- Signing and pavement marking design
- Geotechnical services
- Phase III support during construction

Improvements at Plaza 24 (Edens Spur Plaza) are also anticipated to be included in this project.

Construction Estimate: Category A

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Special Services (Electrical Engineering)
Special Services (Surveying)

The Tollway will allow a Prime Consultant to meet the prequalification for Special Services (Electrical Engineering) and Special Services (Surveying) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Electrical designer, who will be responsible for electrical design related issues (must be an Illinois Licensed Professional Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 36 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed

approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.7 Item 7: I-26-20004, Reagan Memorial Tollway (I-88), Roadway Widening, Highland Avenue to IL Route 83, Phase II Engineering Services.

This project has a 28% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for westbound roadway widening on the Reagan Memorial Tollway (I-88) from Highland Avenue to IL Route 83, MP 134.3 to MP 137.1, in DuPage County, Illinois.

The work generally encompasses roadway widening and shall include, but not be limited to, the following items:

- Roadway design
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- ITS design
- Signing and pavement marking design
- Geotechnical services
- Phase III support during construction

Construction Estimate: Category D

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Simple)

The Tollway will allow a Prime Consultant to meet the prequalification for Structures (Highway:Simple) through a subconsultant.

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 36 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 24 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available

on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.8 Item 8: I-26-70000, Illinois Route 390 Tollway (IL 390), Bridge Reconstruction at Roselle Road, Phase II Engineering Services.

This project has a 21% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for the reconstruction of the Roselle Road bridge over the Illinois Route 390 Tollway (IL 390) at MP 9.5, in Cook County, Illinois.

The work generally encompasses bridge reconstruction and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Bridge Type Studies
- Type, Size and Location (TS&L) plan preparation
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- Signing and pavement marking design
- Geotechnical services
- Environmental services
- Phase III support during construction

Construction Estimate: Category B

The Prime Consultant must be prequalified by IDOT in the following categories:

Structures (Highway: Typical)
Highways (Freeways)
Highways (Roads and Streets)

The Tollway will allow a prime consultant to meet the prequalification for Highways (Freeways) and Highways (Roads and Streets) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer or Structural Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 48 months after authorization to proceed inclusive of completion of Phase III

support services during construction. Phase II design services are anticipated to be completed approximately 24 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.9 Item 9: I-26-40001, Tri-State Tollway (I-94), Bridge Reconstruction at Atkinson Road and Everett Road, Phase II Engineering Services.

This project has a 21% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for the reconstruction of the Atkinson Road Bridge over the Tri-State Tollway (I-94) at MP 15.2, and the Everett Road Bridge over the Tri-State Tollway (I-94) at MP 20.3, in Lake County, Illinois.

The work generally encompasses bridge reconstruction and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Bridge Type Studies
- Type, Size and Location (TS&L) plan preparation
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- Signing and pavement marking design
- Geotechnical services
- Environmental services
- Phase III support during construction

Construction Estimate: Category A

The Prime Consultant must be prequalified by IDOT in the following categories:

Structures (Highway: Typical)
Highways (Freeways)
Highways (Roads and Streets)

The Tollway will allow a prime consultant to meet the prequalification for Highways (Freeways) and Highways (Roads and Streets) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer or Structural Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 36 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.10 Item 10: I-26-50000, Jane Addams Memorial Tollway (I-90), Bridge Reconstruction, Rockton Road to Rote Road, Phase II Engineering Services.

This project has a 21% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for bridge reconstruction on the Jane Addams Memorial Tollway (I-90) from Rockton Road to Rote Road, MP 2.7 to MP 14.5, in Winnebago County, Illinois.

The work generally encompasses bridge reconstruction and shall include, but not be limited to, the following items:

- Roadway design
- Structural design
- Bridge Type Studies
- Type, Size and Location (TS&L) plan preparation
- Maintenance of traffic design including that associated with local roadways
- Barrier warrant analysis
- Utility coordination for protection and/or relocation of utilities
- Drainage design for new system installation or modification of the existing drainage system
- Grading and earthwork design
- Landscaping and soil erosion/sedimentation control
- Roadway lighting design
- Signing and pavement marking design
- Geotechnical services
- Environmental services
- Phase III support during construction

The following structures are anticipated to be included in this project:

- Rockton Road over I-90
- Harlem Road over I-90
- Spring Creek Road over I-90
- Rote Road over I-90

Construction Estimate: Category B

The Prime Consultant must be prequalified by IDOT in the following categories:

Structures (Highway: Typical)
Highways (Freeways)
Highways (Roads and Streets)

The Tollway will allow a prime consultant to meet the prequalification for Highways (Freeways) and Highways (Roads and Streets) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer or Structural Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).

- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 36 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 18 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.11 Item 11:, Jane Addams Memorial Tollway (I-90), Fiber Optic System Improvements, Rockton Road to Plaza 9 (Elgin Plaza), Phase II Engineering Services.

This project has a 17% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for the expansion of the Fiber Optic System on the Jane Addams Memorial Tollway (I-90) from Rockton Road to Plaza 9 (Elgin Plaza), MP 2.2 to MP 53.8, in Winnebago, Boone, McHenry and Kane Counties, Illinois.

The work generally encompasses fiber optic improvements and shall include, but not be limited to, the following items:

- Design of new fiber optic cables and conduit
- Design of communications equipment and systems
- Landscaping and soil erosion/sedimentation control
- Phase III support during construction

Construction Estimate: Category D

The Prime Consultant must be prequalified by IDOT in the following categories:
Special Services (Electrical Engineering)

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Electrical designer, who will be responsible for electrical design related issues (must be an Illinois Licensed Professional Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 24 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 12 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.12 Item 12: I-26-10000, Veterans Memorial Tollway (I-355), Pre-Concept Design and Noise Abatement Wall Reconstruction, I-55 to Army Trail Road, Phase II Engineering Services.

This project has a 21% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for noise abatement wall reconstruction on the Veterans Memorial Tollway (I-355) from I-55 to Army Trail Road, MP 12.7 to MP 29.6, in DuPage County, Illinois. Engineering services from 63rd Street to Butterfield Road/Illinois Route 56, MP 17.2 to MP 22.6 will be omitted from this contract.

The work generally encompasses noise wall studies and design and shall include, but not be limited to, the following items:

- Noise study
- Design of noise walls
- Landscaping and soil erosion/sedimentation control
- Geotechnical services as required to support the above items

The consultant will also be required to provide pre-concept design services and prepare associated engineering plans, that include horizontal and vertical geometry information, to inform noise studies as well as ensure that proposed noise abatement walls are located such that they will not be impacted by future roadway reconstruction.

Construction Estimate: Category E

The Prime Consultant must be prequalified by IDOT in the following categories:

Structures (Highway: Typical)
Highways (Freeways)
Environmental Reports (Environmental Assessment)
Location Design Studies (Reconstruction/Major Rehabilitation)

The Tollway will allow a Prime Consultant to meet the prequalification for Highways (Freeways), Environmental Reports (Environmental Assessment) and Location Design Studies (Reconstruction/Major Rehabilitation) through a subconsultant.

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 42 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 24 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer

Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP) The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.13 Item 13: I-26-40002, Tri-State Tollway (I-94), Active Traffic Management System Installation, Phase II Engineering Services.

This project has a 18% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for the installation of an active traffic management system (ATMS) on the Tri-State Tollway (I-94) at Grand Avenue to O'Plaine Road, MP 8.5 to MP 12.0, in Lake County, Illinois.

The work generally encompasses intelligent transportation system (ITS) design and shall include, but not be limited to, the following items:

- ATMS and ITS system design
- Maintenance of traffic design including that associated with local roadways
- Signing and pavement marking design
- Landscaping and soil erosion/sedimentation control
- Geotechnical services as required to support the above items

Construction Estimate: Category A

The Prime Consultant must be prequalified by IDOT in the following categories:

Special Services (Electrical Engineering)
Highways (Freeways)

The Tollway will allow a Prime Consultant to meet the prequalification for Highways (Freeways) through a subconsultant.

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).
- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Electrical designer, who will be responsible for electrical design related issues (must be an Illinois Licensed Professional Engineer).
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 30 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 12 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system. The Consultant will be required to participate in these procedures and will receive training on the system. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

1.5.14 Item 14: I-26-60000, Tri-State Tollway (I-294) Interchange Improvements at Irving Park Road, Phase II Engineering Services

This project has a 21% D/M/WBE participation goal and 3% VOSB participation goal.

Phase II engineering services are required for the preparation of engineering studies, contract drawings, specifications and project related permits for interchange improvements on the Tri-State Tollway (I-294) at Irving Park Road, MP 38.3, in Cook County, Illinois.

The work generally encompasses roadway and interchange design and shall include, but not be limited to, the design for the following items:

- Construction of new ramps from Mannheim Road to I-294
- Traffic signal modification at the intersection of Mannheim Road and Seymour Avenue
- Widening of Mannheim Road
- Construction of a flyover ramp from northbound I-294 to Mannheim Road
- Retaining wall construction
- Toll plaza construction
- Grading and landscaping improvements
- Installation of a new drainage system and modification of the existing drainage system
- Roadway lighting installation
- Signing and pavement marking improvements
- Erosion and sediment control installation

The work shall also include the following:

- Geotechnical services
- Landscape design and evaluation of soil erosion and sedimentation control measures and earthwork as necessary in accordance with the Tollway's Environmental Studies manual.
- Barrier warrant analysis
- Preparing Maintenance of Traffic plans, including providing alternative concepts for traffic and construction staging as appropriate, for the toll highway ramps and local roadways
- Utility coordination for protection and/or relocation of utilities
- Phase III support during construction
- All other appurtenant and miscellaneous items

Construction Estimate: Category D

The Prime Consultant must be prequalified by IDOT in the following categories:

Highways (Freeways)
Structures (Highway: Complex)
Environmental Reports (Environmental Assessment)
Special Studies (Location Drainage)
Special Plans (Lighting: Typical)
Special Services (Surveying)
Special Plans (Traffic Signals)

The Tollway will allow a Prime Consultant to meet the prequalification for Structures (Highway: Complex), Environmental Reports (Environmental Assessment), Special Studies (Location Drainage), Special Plans (Lighting: Typical), Special Services (Surveying) and Special Plans (Traffic Signals) through a subconsultant(s).

Key personnel listed on Exhibit A for this project must include:

- Project Manager (must be an Illinois Licensed Professional Engineer).

- Project Engineer, who is directly involved in the development of the contract documents (must be an Illinois Licensed Professional Engineer).
- Roadway designer, who will be responsible for roadway design related issues (must be an Illinois Licensed Professional Engineer).
- Structural designer, who will be responsible for structural design related issues (must be an Illinois Licensed Structural Engineer).
- Drainage designer, who will be responsible for drainage design related issues (must be an Illinois Licensed Professional Engineer).
- The Environmental Lead (EL), who will be responsible for coordinating the DSE team's environmental studies.
- QC/QA reviewer of all milestone submittals, who must be an Illinois Licensed Professional Engineer for roadway elements, or an Illinois Licensed Structural Engineer for structural elements.

Schedule: This project is scheduled to start in 2027. The substantial completion date for this project will be approximately 48 months after authorization to proceed inclusive of completion of Phase III support services during construction. Phase II design services are anticipated to be completed approximately 24 months after authorization to proceed. Final schedule will be determined at the time of negotiation.

This project is intended to be designed with the CADD models included as part of the Contract documents. The Consultant must comply with the current editions of the Illinois Tollway's Computer Aided Design and Drafting (CADD) Standards Manual and BIM Implementation Manual, available on the Illinois Tollway's website. This project will be managed through the Tollway's web-based project management system (WBPM). The Consultant will receive WBPM system training and will be required to utilize the WBPM system as part of the delivery of services. The Tollway will furnish the Consultant with guidelines for the Consultant's Quality Program (CQP). The Consultant who is selected for this project will be notified and scheduled to attend a scope briefing with the Illinois Tollway.

PART II: CONTRACT CLAUSES AND REQUIREMENTS

2.1 CONSULTANT /SUBCONSULTANT CONFLICTS OF INTEREST WITHIN TOLLWAY PROJECTS

Professional engineering services performed under contracts with the Illinois Tollway shall be performed in accordance with the highest standards of professional behavior and highest principles of ethical conduct. Such services must be provided with honesty, impartiality, fairness and equity and must be dedicated to the protection of public health, safety and welfare.

Prime Consultants submitting a Statement of Interest (SOI) shall disclose any known or potential conflicts of interest the Prime Consultants may have.

The selected Prime Consultant shall be required to submit a Consultant Quality Program (CQP) to the Illinois Tollway, which shall be subject to approval by the Illinois Tollway. As part of the CQP, Prime Consultants shall identify any known or potential conflicts of interest, including any known or potential conflicts of interest identified by any of their Subconsultants. The CQP also shall outline the plan for monitoring known conflicts and identifying potential conflicts through the duration of the contract, as well as describe, in detail, procedures relative to ethical screens and other procedures for mitigating conflicts. If additional conflicts of interest or potential conflicts of interest are identified during the administration of the contract, the Prime Consultant will be required to submit an updated CQP.

Periodically, the Illinois Tollway solicits Professional Services for foundational contracts, which include the Program Management Office (PMO), Consulting Engineer (CE), and Traffic Engineer (TE) contracts. The overarching engineering services provided pursuant to foundational contracts involve all or the majority of all other Illinois Tollway Professional Services contracts, and the foregoing provisions of this Section 2.1 are fully applicable to the PMO, CE and TE contracts.

Foundational contracts prohibit the PMO, CE and TE from performing new services for the Illinois Tollway during the pendency of the respective PMO, CE, or TE contract (including extensions). “New services” as used herein includes, but is not limited to, work or services awarded to a person or entity not affiliated with the PMO, CE, or TE that, subsequent to the award of the PMO, CE, or TE contract, is acquired, becomes controlled by or otherwise becomes affiliated with the PMO, CE, or TE. The PMO, CE, and TE are required to notify the Illinois Tollway, in advance, of any such acquisition, assumption of control or affiliation.

Notwithstanding the provisions of the CQP or any other provisions of this Section 2.1, the Illinois Tollway reserves the right to assess and require appropriate corrective action, as determined by the Illinois Tollway, relative to any conflict or potential conflict issues involving a professional firm, professional individual, PMO, CE, or TE. Relative to conflicts and potential conflicts, Prime Consultants must be responsive to the Illinois Tollway so that appropriate steps can be taken to mitigate any such circumstances.

Consistent with the foregoing, professional firms should conduct their operations using common sense and professional judgment. Professional firms should not place their firms in inappropriate situations or create any unfair advantage for their firms.

This notice is not intended to address any potential conflicts of interest ruled upon by the Chief Procurement Officer and/or the Procurement Policy Board under the Illinois Procurement Code (30 ILCS 500/1, et seq.). Violations of this Section may result in termination of contracts for cause or the Illinois Tollway declining to award work, projects or contracts.

2.2 INSPECTOR GENERAL

The Vendor hereby acknowledges that pursuant to Section 8.5 of the Toll Highway Act (605 ILCS 10/8.5) the Inspector General of the Illinois State Toll Highway Authority ("OIG") has the authority to conduct investigations into certain matters including but not limited to allegations of fraud, waste and abuse, and to conduct reviews. The Vendor agrees that it will fully cooperate in any OIG investigation or review and shall not bill the Illinois Tollway for such time. Cooperation includes, but is not limited to, providing access to all information and documentation related to the goods/services described in any Agreement entered into in connection with this PSB, and disclosing and making available all personnel involved or connected with these goods/services or having knowledge of these goods/services. All Prime Consultants must inform Subconsultants of this provision and their duty to similarly comply and cooperate with any OIG investigation or review.

2.3 FINANCIAL INFORMATION

2.3.1 DIRECT LABOR MULTIPLIER

The Direct Labor Multiplier to be used on projects advertised in the PSB is as follows:

Phase I and II (Studies, Design, and Survey)	2.8
Phase III (Construction Management)	2.8
Project Staff at Illinois Tollway Facilities	2.5

- The 2.5 multiplier applies to contracts with personnel permanently assigned to an Illinois Tollway facility, such as the Central Administration Building (CA). The 2.5 multiplier does not pertain to personnel assigned to construction field offices for Phase III (Construction Management).

The Direct Labor Multiplier for specialty engineering services, such as Aerial Mapping and LiDAR, will be based upon the firm's current overhead determined during initial contract negotiations between Tollway and Consultant.

2.3.2 OTHER CONTRACTING METHODS

The Illinois Tollway, in its sole discretion, may consider, when it is in the best interest of the Illinois Tollway, other payment methodologies in lieu of the Direct Labor Multiplier. Other considerations include "flat rate" or "lump sum" methodology that would be further defined at the time of negotiations between Tollway and Consultant. Other payment methodologies could negate or alter section 2.3.1 Direct Labor Multiplier.

2.3.3 ESTIMATED CONSTRUCTION COST OF PROJECTS

The estimated construction cost of each project is presented in the following categories or may be specific to a project detail. This is to assist the Vendor in determining the relative size of the project. The construction cost category will be included in each Item. The categories are:

CATEGORY	ESTIMATED CONSTRUCTION COSTS
A	$0M - $ 25M
B	$ 25M - $ 50M
C	$ 50M - $ 75M
D	$ 75M - $ 100M
E	$ 100M - $150M
F	$150M-$200M
G	>$200M

2.3.4 ALLOWABLE DIRECT COSTS

The Allowable Direct Cost and Allowable Direct Cost –Construction Inspection lists are available on the Illinois Tollway's website at:
https://www.illinoistollway.com/doing-business/construction-engineering/forms

The Illinois Tollway will allow the Vendor to negotiate their Direct costs and bill as a lump sum on the contract.

2.4 ILLINOIS TOLLWAY'S CONTRACT PAYMENT POLICY

The Illinois Tollway will not issue payments under contracts for costs incurred during the preceding calendar year if any invoice for that work is received after February 28th of the subsequent fiscal year. This policy enables the Illinois Tollway to close its financial books both on time and accurately. To meet the requirements of Generally Accepted Accounting Principles and those of the Illinois Auditor General and external auditors, the Illinois Tollway must account for all of its expenditures for a given calendar year before the end of the subsequent February. This policy includes payment of any "re-bill" issues that may arise. The Illinois Tollway is unable to make any payments for work in a given calendar year if it has not been properly invoiced to the Illinois Tollway by February 28th of the following year.

2.5 DISADVANTAGED BUSINESS ENTERPRISE (DBE) PARTICIPATION

The Illinois Tollway hereby notifies all respondents that it will affirmatively ensure that in any contract entered into pursuant to this solicitation, disadvantaged, minority, women-owned business and Small Business Administration (SBA) 8(a) enterprises are encouraged to submit a SOI response to this invitation and/or to participate in the advertised Disadvantaged Business Enterprise (DBE) goal of the work to be performed under the contract as a Subconsultant. The Tollway's contracts are not USDOT-assisted projects. Accordingly, the Tollway's DBE Program standards and requirements are distinct from the federal USDOT DBE Program.

Any agreement between a Prime Consultant and a DBE or other Subconsultant in which the Prime Consultant requires that the Subconsultant not provide professional services proposals to other vendors is prohibited.

To qualify as an eligible DBE, the firm must be currently certified by one of the following agencies currently participating in either (A) the Illinois Unified Certification Program (IL UCP); (B) the City of Chicago, Illinois; or (C) the County of Cook, Illinois, as a Minority or Women-Owned Business ("M/WBE") pursuant to their M/WBE programs; or (D) it must be currently participating in the Small Business Administration SBA 8(a) Program. A DBE is considered to have current certification if the firm is listed in the directory database of the pertinent certifying agency:

- IL UCP - Illinois Department of Transportation (IDOT)
- IL UCP - Chicago Transit Authority (CTA)
- IL UCP - PACE
- IL UCP - METRA
- IL UCP - City of Chicago
- City of Chicago – M/WBE
- Cook County, Illinois – M/WBE
- Small Business Administration SBA 8(a)

Each DBE firm utilized must be listed in a certifying agency's database at the time of the expiration of the extended documentation period, if utilized, as described below to be considered acceptable. Please provide proof of certification (example: letter) with your SOITEAM submittal. Certification letters must be current, and DBE and VOSB vendor's scope(s) of work stated in the SOI and Letter of

Intent (LOI) must match the area(s) of specialty specified in the DBE's or VOSB's certification letter. Failure to provide the required DBE/VOSB participation/utilization information in the SOITEAM may result in the SOI being deemed non-responsive.

You can view/print and download the most current listing of DBE firms at:

- IDOT's web site: https://webapps1.dot.illinois.gov/UCP/ExternalSearch
- City of Chicago's web site: https://chicago.mwdbe.com/
- County of Cook, Illinois' web site: https://cookcounty.diversitycompliance.com/
- Small Business Administration's SBA 8(a) web site: https://dsbs.sba.gov/

If a Vendor cannot obtain sufficient DBE commitments to meet the contract goal, the Vendor must document its good faith efforts to meet the goal, including any DBE participation secured, and request a partial or full waiver of the contract goal. Demonstrating good faith efforts means that the Vendor must show that all necessary and reasonable steps were taken to achieve the contract goal, meaning those steps that could be reasonably expected to obtain sufficient DBE participation. Mere pro forma efforts are not good faith efforts, and the documentation must be supported by backup evidencing contact attempts and results made by the Vendor to DBE firms. Vendors should not submit pricing information received from DBE firms with the good faith efforts documentation.

Examples of good faith efforts and the contact log are available in the List of Documents, Exhibit F, Section 7.10 of the State of Illinois Veteran Small Business Participation and Utilization Plan and in Exhibit H, Section 6.5 of the Tollway DBE Participation, Utilization Plan and Letter of Intent for Professional Services.

Extended Documentation Period for Vendors with a Technical Issue as determined by the Illinois Tollway related to the DBE and VOSB Commitment Made on a SOI:

All required DBE/VOSB documentation must be completed to the fullest extent possible and submitted with the SOI, including the signed DBE/VOSB Letters of Intent (LOI) and SOITEAM. The SOITEAM data will take precedence.
NOTE: the percentage inserted in the SOITEAM will take precedence over any other percentage inserted in the LOI data in the event of a discrepancy.

Each Consultant submitting a SOI who has a DBE/VOSB commitment with a technical issue as determined by the Illinois Tollway related to DBE/VOSB participation that is identified during initial review of a SOI by the Illinois Tollway shall be allowed, upon an email notification from the Illinois Tollway, an extended documentation period which will extend until 5:00 pm CT on the second business day after the day the notification is sent (e.g. if a Consultant is notified on Monday, extended documentation period concludes on Wednesday at 5:00 pm).

The extended documentation period allows a Consultant solely to correct their initial SOITEAM data to add or adjust DBE/VOSB participation to:

- Meet or exceed the initial DBE/VOSB commitment stated in the SOI, if that initial commitment was above the advertised DBE/VOSB goal, or
- Meet or exceed the goal, if the initial DBE/VOSB commitment stated in the SOI was below the advertised DBE/VOSB goal.

The Consultant shall submit updated SOITEAM data and LOI if additional or adjusted DBE/VOSB participation is secured by the end of the extended documentation period.

Under no circumstances is a Consultant allowed to remove, replace or reduce the DBE/VOSB participation of a certified DBE/VOSB firm listed in the initial LOI and SOITEAM data without prior written consent of Illinois Tollway. Increases to DBEs/VOSBs listed in the initial LOI and SOITEAM data are allowed. Under no circumstances is the Consultant allowed to change any documentation unrelated to the correction of the technical issue identified. Any adjustment made to the DBE/VOSB portion of the LOI and SOITEAM data during the extended documentation period must include a brief statement describing the revision(s) with resubmittal of the LOI and SOITEAM data. Any other changes to the original SOI will not be accepted.

Illinois Tollway Disclaimer Statement: Illinois Unified Certification Program (ILUCP), Disadvantaged Business Enterprises (DBE) Directory, City of Chicago or Cook County, Illinois Minority and Women-Owned Business (M/WBE) Directories, or Small Business Administration SBA 8(a) Directory

Firms listed in either the Illinois Unified Certification Program (IL UCP) Disadvantaged Business Enterprises Directory or the City of Chicago Minority and Women-Owned Business Directory have been certified as a Disadvantaged Business Enterprise (DBE) by one of the IL UCP participating agencies (Illinois Department of Transportation, City of Chicago, Chicago Transit Authority, Metra and Pace) or by the City of Chicago. Firms listed in the County of Cook, Illinois M/WBE Directory have been certified as Minority or Women Owned Business Enterprises by the County of Cook, Illinois. Firms listed in the Small Business Administration SBA 8(a) Directory have been certified as SBA 8(a) business enterprises by the Small Business Administration.

The criteria, standards and procedures by which certification decisions are made can be obtained from any of the certifying agencies. These directories are to be used as an "informational source only" and the following must be considered:

- Certification does not mean that a firm is in any way prequalified to provide the products and/or services the firm claims it can provide. "Certification" means that the certifying agency has determined, on the basis of information provided and the representations therein, that a business is a bona fide DBE. The certifying agency does not, as a result of any listing, make any representation concerning the ability of any listed firm to perform work in the specialty listed;
- The Illinois Tollway does not, through its use of, and referral to, certification lists, make any representation concerning the ability of any listed firm to perform work in the specialty listed.
- The Illinois Tollway, in awarding a contract, has discretion in determining whether a DBE firm's listed work categories are eligible to be counted toward the fulfillment of DBE contract goals; and
- It is the responsibility of all vendors to:
    a) Conduct their own investigation to determine the capability and capacity of the DBE firm(s) to satisfactorily perform the proposed work; and
    b) Ensure the DBE firm(s) is currently certified. A DBE is considered to have current certification if the firm is listed in the directory database of the pertinent certifying agency.

These directories list the most current certified firms. If there are any questions concerning these directories, please contact the certifying agency.

For more details about DBE utilization/participation, good faith efforts and related documentation requirements, refer to Exhibit H.

2.6 PARTNERING FOR GROWTH PROGRAM GUIDELINES (formerly Partnership-Mentor/Protégé Program Guidelines)

The Partnering for Growth Program and Documents have been updated to include the Reverse DBE_VOSB P4G Exhibit E and the standard DBE_VOSB P4G Exhibit E.

The Partnering for Growth Program applies to both Disadvantaged Business Enterprises (DBE) and Veteran-Owned Small Businesses (VOSBs) firms. Separate Exhibit E's – Partnering for Growth Program and Reverse Partnering for Growth forms are available for use for either a DBE or VOSB. Vendors may have multiple Partnering for Growth agreements in either the DBE and/or VOSB category(ies) and may have partnerships with both. More information on the Partner for Growth Program can be found at https://www.illinoistollway.com/doing-business/diversity-development/programs/partnering-for-growth

2.7 STATE OF ILLINOIS VETERAN SMALL BUSINESS PARTICIPATION AND UTILIZATION PLAN

This solicitation includes specific Veteran Small Business participation goal(s) as specified in each Item detail based on the availability of CEI-certified veteran-owned (VOSB) vendors to perform or provide the anticipated

services required by this solicitation. The Veteran Small Business participation goal is applicable as specified in each Item detail. In addition to the other award criteria established for this solicitation, the Illinois Tollway will award contracts under this PSB to a Vendor that meets the goal or makes good faith efforts to meet the goal. Vendor must submit a Utilization Plan and Letter of Intent with its SOI. Refer to PART III, List of Documents, Exhibits, and Other Attachments, for submittal instructions. As stated in Exhibit F, to qualify as an eligible VOSB the firm must be currently certified, at the time of the Professional Services Bulletin due date, by the State of Illinois Commission on Equity and Inclusion. Registration is available at:

https://supplierdiversitymanagementportal.illinois.gov/home.aspx

2.8 TEAMING AGREEMENT

The action of joining forces with another vendor to submit on a Professional Services Bulletin (PSB) is called Teaming. All former policies and procedures referring to Joint Venture still apply, with Teaming as the name of the effort.

Team SOIs shall comply with the same requirements set forth for individual SOIs, including. but not limited to, the submittal (under the Team's SOI code name) of the SOI, SOITEAM data, Exhibits, and Disclosures. A Team SOI represents a unique submittal and shall not be combined with an individual SOI from the Team Lead or submittals from other, unique teams.

Team members and a Team Leader must clearly be identified with the SOI submittal, and Team Lead shall be considered the Prime Consultant upon selection. A Team Lead can only select one D/M/WBE category but may provide evidence of multiple certifications by attaching any supporting documentation in the attachments tab before submitting. The selection criteria for the Team will include the Team members' prequalification categories, and the sum of the individual firm's work capacity and evaluation history.

The Illinois Tollway requires the Team to **self-perform no less than 40%** of the work, meaning the Team cannot subcontract more than 60% of the project work. The scope of work to be performed by each Team member and its Subconsultants must be clearly defined and leave no room for interpretation in the SOI. Each Team member must make a substantial contribution to the performance of the work being completed by the Team. Factors that may be considered by the Illinois Tollway, in its sole discretion, in determining what constitutes a substantial contribution include, but are not limited to, the number of participants in the Team, the professional qualifications of each member, and the nature of the work being performed.

Team SOI submittal overview:

- Designate a single point of contact who shall serve as the Team's primary contact with the Illinois Tollway.
- Indicate the Team member responsible for each prequalification category.
- The Team Lead shall submit outstanding work obligations, and Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B) (as applicable) for each of the Team members.
- Identify the Team member responsible for invoicing.
- For Exhibit A, plus other required documents specified in the PSB, combine the information for all participating Team members.

A firm planning to submit a SOI as a Team is required to contact the Illinois Tollway for a Team SOI Firm Name Code. Contact CS staff via e-mail at csstaff@getipass.com. The Team SOI Firm Name Code as provided by the Illinois Tollway is required to identify and process the submittal as a Team proposal.

Only the Team Lead is required to fill out the SOITEAM data on behalf of the Team. It is imperative that the other Team members do NOT submit SOITEAM data if they are not the Team Lead. The Team Lead must clearly identify the Team members and Subconsultants doing work for or in conjunction with the Team within the Team SOITEAM data submittal.

Example of a Team (TM) submittal: Companies forming Team are:

- Company A
- Company B

- Company C
- Team Firm Name Code as provided by the Illinois Tollway is: ABC_TM

Team members naming parameters are:

- ABC_TM (Company A) “Managing Partner”
- ABC_TM (Company B)
- ABC_TM (Company C)
- Subconsultants to the Team Lead: J. Smith Consulting (Company B)
- F.J. Engineering (Company C)
- Subconsultants to the Team members: G. Engineering (Company A)
- Materials Inc. (Company A)
- Surveying Services (Company B) Jersey Consulting (Company B) KL Services (Company C)
- LMN Engineering (Company C)

ADDITIONAL TEAMING INFORMATION FOR SELECTED FIRMS

The Illinois Tollway **DOES NOT** have a form for Teaming Agreements. However, the firms submitting as a Team are required to obtain and submit their Teaming Agreement. A Teaming Agreement, signed by all members, **MUST** be submitted within ten (10) business days after contract negotiations and prior to Board award. The Teaming Agreement will clearly identify the Team members, their percentage interest / share, as well as respective rights and responsibilities. The Teaming Agreement shall further designate a Team Lead who will assume responsibility for invoicing. **The Team may have no more than three participants.**

Each Team member shall procure and maintain separate insurance policies that meet the Illinois Tollway’s insurance requirements. The Tollway’s standard insurance requirements are set forth in the Vendor Agreement boilerplates (See Illinois Tollway website: https://www.illinoistollway.com/doing-business/construction-engineering/forms under Doing Business> Construction and Engineering: Vendor Resources under Vendor Forms). Each Team member will procure and maintain policies that meet the Prime Consultant’s required level of coverage and shall indemnify the Team and the Tollway against claims arising from their performance under the Team, as well as agreeing to remain joint and severally liable upon termination of the Project and/or the Team. In the event of the termination of the Team, the insurance and indemnification rights of the Team must be assignable to the Illinois Tollway as a matter of law. Proof of compliance with these requirements must be submitted to the Illinois Tollway prior to issuance of the Illinois Tollway’s Notice to Proceed.

2.9 MANUALS, PROCESSES AND GUIDELINES

Manuals are available on the Tollway website to provide guidance on contract requirements, procedures and responsibilities.

https://www.illinoistollway.com/doing-business/construction-engineering/manuals-processes-guidelines#Construction%20and%20Materials

2.10 PHASE II: DESIGN ENGINEERING SERVICES

The scope of work will generally include certain Phase II engineering services to be provided during construction. Such services may include, but not be limited to, shop drawing review, value engineering proposal review, attending construction phase meetings and responding to requests for information related to design. The scope of such services will be determined after the Consultant is selected as appropriate.

2.11 PHASE III: CONSTRUCTION ENGINEERING SERVICES

The following applies to all Phase III Engineering service items.

After the Consultant has been selected, the Construction Manager (CM) shall provide the following to the Illinois Tollway:

The Consultant selected for the Construction Management (CM) Services shall submit for the Illinois Tollway's review and approval, a management plan for the specific Project(s) for which the Consultant is selected. This management plan shall include an outline of the full-time or part-time plant, on-site inspection services, sampling and laboratory testing the Consultant is providing for Quality Assurance. The selected CM's Consultant's Quality Program (CQP) shall include the identification and pre-qualifications of the Field Inspectors and Laboratory Technicians to be assigned to this project as employees of the Consultant or a qualified Subconsultant. The CQP shall include periodic verification by an independent qualified Subconsultant that the Quality Assurance operations are proceeding as specified using the proper methods of sampling and testing.

The name of any accredited material laboratory(ies) to be utilized for the quality assurance work must be provided with the CQP. The laboratory must be accredited under the AASHTO Accreditation Program (AAP) for all required test procedures specified in IDOT Bureau of Materials Policy Memorandum "Minimum Private Laboratory Requirements for Construction Materials Testing or Mix Design."

2.12 CONSTRUCTION AND QUALITY ASSURANCE CONSULTANTS

Personnel performing materials testing for aggregate, PCC, and HMA shall have completed the appropriate IDOT Quality Management Training Program classes. Personnel performing soils inspection and field tests shall have completed IDOT class S-33, Soils Field Testing and Inspection.

The Field Inspectors assigned to any project under this PSB for on-site Quality Assurance for earthwork quality control and for monitoring the on-site asphalt construction work must be prequalified by having passed the IDOT Nuclear Density training course. The Field Inspectors assigned to the on-site quality control of concrete placement shall be prequalified by having passed the IDOT/ACI Portland Cement Concrete Level I training course. Personnel performing soils field tests shall have completed IDOT class S-33, Soils Field Testing and Inspection.

The Vendor's Quality Assurance responsibilities at the material production plants shall be performed by a Field Inspector having passed IDOT Level I and Level II (HMA and PCC) training courses to perform the specified inspection of approved materials at the concrete and asphalt plants.

2.13 QUALITY ASSURANCE PREQUALIFICATION CATEGORY

The prequalification requirements for Quality Assurance Testing are required and will follow the guidelines set by IDOT in the Prequalification information "Description and Minimum Requirements for Prequalification" SPECIAL SERVICES - Quality Assurance Testing.

The information about the Quality Assurance Testing prequalification can be located on IDOT's website at: https://public.powerdms.com/IDOT/documents/3242864?utm.com

2.14 CLARIFICATION OF QUALITY CONTROL/QUALITY ASSURANCE REQUIREMENTS

The Quality Control/Quality Assurance personnel on Exhibit A shall not be the same personnel preparing the design documents. If the Prime Consultant does not have personnel to cover the QC/QA requirements, then a Subconsultant prequalified in the category may be used.

The following highlighted sections have been added to the Guidelines in the Professional Services Bulletin and the solicitations.

Complete **Exhibit A** as follows:

- List the required key personnel to match prequalification categories and any additional personnel requirements designated in the project solicitation. Include firm name if work is to be completed by a Subconsultant; and

- QC/QA personnel must be different individuals than those preparing the design documents.

2.15 CONSULTANT CONTRACT FORMS

Standard forms exhibits and associated instructions to be used by Construction Management (CM) and Design Section Engineering (DSE) Consultants in preparing proposals and agreements with the Illinois Tollway are located on the Illinois Tollway website. Contracts will be awarded based on the standard Agreement templates. Selected Consultants should be prepared to execute the appropriate Agreement template. Any exceptions shall be noted in the Consultant's SOI.
https://www.illinoistollway.com/doing-business/construction-engineering/forms

2.16 SELF-PERFORMANCE

The Illinois Tollway requires the Prime Consultant (non-team) to self-perform no less than 40% of the work.

PART III: REPRESENTATIONS AND INSTRUCTIONS

3.1 SELECTION CRITERIA

Members of the Vendor Selection Committee will not be available to discuss specifics of projects listed in this PSB between the date of the submittal and the Selection Committee meeting. Please do not send letters or e-mails expressing interest in specific projects to members of the Vendor Selection Committee.

Selection of professional Vendors by the Illinois Tollway is based on the firm's professional qualifications, related experience, expertise, and availability of key personnel to be assigned to the project, satisfaction of diversity goals and contract compliance and what is best for the Illinois Tollway. SOIs will be evaluated based on the following criteria:

- Specialized experience when required, technical competence of the personnel, and experience of the firms and/or Subconsultants proposed;
- Performance history and expertise of the firm and any proposed Subconsultants with the work described in the Item;
- Particular attention will be given to appropriate cost-saving measures and innovative ideas that will benefit the Illinois Tollway;
- Ability to complete the work in the time required and the firm's existing workload;
- Commitment and availability of Key Personnel during the term of the contract;
- Proposed method of accomplishing the project's objectives;
- Demonstrated understanding of an inclusive and substantive DBE/VOSB utilization plan; and
- Contract Compliance will evaluate submitted forms and documents, including but not limited to the SOI, LOI, and DBE/VOSB certification(s) for completeness, accuracy and verification that all requirements of the PSB have been met.

Consideration will also be given to the quality and scope of utilization plan which demonstrates an understanding of an inclusive and substantive DBE and VOSB U-Plan (Reference Section 2.5 and 2.7 for definition of "DBE" and "VOSB"), VOSB and Partnering for Growth (formerly Mentor Protégé proposals).

Consideration will also be given to the completeness and content of the compliance documentation submitted (SOI and LOI), whether the submitted documents show that at least the advertised diversity goal(s) has/have been met, and if the certification letters submitted are current and the area(s) of specialty as certified match with the scopes of work of the respective DBE/VOSB participants.

3.2 SCHEDULE FOR VENDOR SELECTION

The Illinois Tollway anticipates selecting Vendors based on the estimated schedule below:
Representatives from the Illinois Tollway will contact selected firms to schedule introductory meetings.

TASK	DATE DUE
Publish	October 8, 2026
Pre-proposal meeting 2:45:00 p.m. Central Time	October 15, 2026
Last Day for Questions no later than 4:30:00 pm Central Time	October 21, 2026
Complete SOIs are due no later than 4:30:00 pm Central Time on this date, including all required Attachments/Exhibits as specified in this PSB.	October 30, 2026
Selection Committee Meeting:	December 2026
Estimated Board Approval (earliest)	February 2027
Estimated Notice to Proceed (earliest)	April 2027

3.3 GUIDELINES FOR SUBMITTING STATEMENTS OF INTEREST (SOI)

The firm acting as the Prime Consultant must be prequalified in all of the prequalification categories requested in the project advertisement even if they plan to subcontract part of the project, except where noted in a specific project advertisement. Any Prime Consultant or Subconsultant must be prequalified by IDOT in the category of work they are performing or as stated in the item description, unless the Subconsultant is being mentored in the Partnering for Growth Program. **SEE NOTICE BELOW.**

3.3.1 REQUIRED FORMAT FOR SUBMITTING STATEMENTS OF INTEREST

3.3.2.1 THE FOLLOWING EXHIBITS AND DATA SHALL BE SUBMITTED IN ACCORDANCE WITH THE PSB SUBMITTAL INSTRUCTIONS **AND SHALL BE DOWNLOADED FROM THE ILLINOIS TOLLWAY WEBSITE.** ALL EXHIBITS SUBMITTED FOR THIS PSB MUST BE CURRENT. EXHIBITS FROM PREVIOUS PSBs WILL NOT BE ACCEPTED.

- Exhibit A: Proposed Staff
  - Submit as a separate pdf document.
  - Include resumes of item specific key personnel.
- Exhibit C: Instructions for Completing Exhibit C and Current Obligations form
  - Submit as a separate pdf document.
- Exhibit D: Availability of Key Project Personnel
  - Submit as a separate pdf document.
- Exhibit E-DBE/VOSB: Partnering for Growth Program
  - If proposing a mentor-protégé arrangement with a DBE or VOSB firm, submit this Exhibit.
  - Submit as a separate pdf document.
- Exhibit E- Reverse DBE/VOSB: Partnering for Growth Program
  - If proposing a mentor-protégé arrangement with a DBE or VOSB firm where the subconsultant is mentoring, submit this Exhibit.

- Submit as a separate pdf document.

- Exhibit F: Veteran Small Business Participation and Utilization Plan
  - If the item includes a Veteran Goal, submit this Exhibit.
  - Submit as a separate pdf document.
- Exhibit H: DBE Participation and Utilization Plan
  - If the item includes a DBE Goal, submit this Exhibit.
  - Submit as a separate pdf document.
- Illinois Tollway Standard Business Terms and Conditions
  - Submit as a separate pdf document.
- SOITEAM Data
  - Required, see Section 3.4.3 Instructions for Submitting the SOITEAM Data

3.3.2.2 PREQUALIFIED FIRMS MAY INDICATE THEIR DESIRE TO BE CONSIDERED FOR SELECTION ON ANY OF THE PROJECTS LISTED WITHIN THIS PSB BY SUBMITTING A SEPARATE SOI FOR EACH PROJECT.

3.3.2.3 EACH SOI MUST BE SUBMITTED USING THE FOLLOWING BASIC FORMAT:
Only pages within the stated page limits for each SOI section or attachment will be reviewed. Any pages exceeding these limits will be redacted and will not be considered. Embedded links within submittals will be disabled and will not be considered.

COVER SHEET

Include Full Legal Prime Consultant Name, PSB Number, Item Number, and **all** known Subconsultants (Full Legal Firm Names).

Section 1. Executive Summary (limit of 5 pages)

A. Legal Name of Prime Consultant, address, telephone number, e-mail address and contact person.
B. List all known Subconsultants, the work the firm(s) will be performing and a contact person for each. Identify any DBEs (Reference Section 2.5 for definitions) and VOSBs. Include Mentor and Protégé data if applicable.
C. Name of Project Manager.
D. Name of Project Engineer/Resident Engineer.
E. Project Understanding.
F. Project Approach (include brief statement of firm's unique qualifications and experience, approach to the project's specific challenges such as maintenance of traffic, environmental constraints, budget constraints, schedule constraints, design challenges, etc.).
G. Statement that firm will meet or exceed the DBE goal and VOSB goal as applicable for the item. Include the proposed percentage of work to be completed by proposed DBE and VOSB firms (Percentages shall match those submitted with the SOITEAM data). For each proposed DBE firm, include a current certification letter that shows that the DBE/VOSB firm is certified in its scope(s) of work stated in the SOI and its LOI. (IDOT Prequalification in the respective scope will meet this requirement.)

Section 2. Organization Chart

Include names and titles for all Key Project Personnel.

Section 3. Relevant Project Experience

Include a minimum of three (3) relevant projects of equal or greater complexity accomplished within the past five (5) years, demonstrating the firm's experience in the type of work required for this project. Color graphics and photographs may be sent with the files.

Include performance ratings for past work done for the Illinois Tollway, IDOT, or any other government agencies or public bodies, if applicable.

Section 4. Conflicts of Interest

Statement acknowledging any known or potential conflicts of interest the Prime Consultant may have.

NOTICE

Pursuant to Illinois Department of Transportation (IDOT) Prequalification rules and procedures, the Illinois Tollway will accept your firm's prequalification the same as IDOT, in that your firm is prequalified until (Fiscal Year + 1 year). As per IDOT, your firm will be given an additional six months from this date to submit the applicable portions of the "Statement of Experience and Financial Condition" (SEFC) to IDOT to remain prequalified.

The firm remains prequalified during this six (6) month grace period. Once the data is submitted to IDOT, either before or on the due date, the firm remains prequalified in the current categories until IDOT reviews a category and decides. If there is not a submittal by the due date, the firm is automatically listed as not approved.

IDOT provides a listing of prequalified consulting firms on the website:
IDOT Prequalified Consultants

This list is typically updated weekly and is based on the most recently approved SEFC application. Firms are encouraged to monitor their prequalification status in IDOT's EPAS system. This notice also applies when utilizing a Subconsultant to meet prequalification requirements on a project.

3.4 SUBMITTAL INSTRUCTIONS

All submittals for this PSB will be received through the Illinois Tollway's Trimble Unity Construct PSB SOI process at: https://app.e-builder.net/ Contact support@wbpmsupport.zendesk.com for training and login information.

Firms that are teaming and preparing an SOI must use the code name assigned for the team. When a firm is submitting on behalf of a team, a unique Trimble Unity Construct account and login ID are required. The team SOI submittal must be created and submitted by the Prime Consultant. (Important Reminder: if a Prime Consultant is submitting for themselves, that account and login ID will be different from the account and login ID that they will use to submit for a team).

The preparation of the SOI for submittal in Trimble Unity Construct must be done in one Trimble Unity Construct account, i.e., one account login ID. Each account/login has access only to the Trimble Unity Construct PSB SOI process instance that is being created in that account. Each Trimble Unity Construct PSB SOI process instance can only be seen from the login that created it.

One SOI is required for each PSB item. The subject line will be created in the Trimble Unity Construct PSB SOI process when you select the item number your firm will be submitting for from the pull-down menu. Complete Trimble Unity Construct instructions for the PSB SOI process can be found in the upper right-hand corner of the SOI instance.

This is not an invitation for bids. Firms properly prequalified for the projects listed herein may indicate their desire to be considered for selection by submitting an SOI to the Illinois Tollway via the Trimble Unity Construct PSB 26-4 SOI process.

The Illinois Tollway follows the Qualifications Based Selection (QBS) process mandated by Illinois statute (30 ILCS 535/1 et seq.)**:** Architectural, Engineering, and Land Surveying Qualifications Based Selection Act for selecting qualified Vendors under this PSB.

SOI Trimble Unity Construct submittals must be received by the due date and time as noted in this solicitation. Any submittals received after that time will be considered late and the user will receive a Trimble Unity

Construct notification stating that the PSB SOI date and time has expired. Late submittals will not be accepted by the Illinois Tollway. NOTE: You must set the Time Zone field on your Trimble Unity Construct account profile page to "(UTC-06:00) Central Time (US & Canada)" so that you can submit your SOIs up until the submittal deadline.

Please carefully read the instructions below BEFORE submitting your SOIs.

3.4.1 GENERAL INSTRUCTIONS

It is CRITICAL that submittal instructions be followed. All Forms must be submitted per the instructions provided. Failure to do so may result in an incomplete submittal resulting in your firm being disqualified. For further information on accessing the Illinois Tollway Website, PSB and Exhibits, please refer to the Table of Contents.

3.4.2 NAMING AND LABELING INSTRUCTIONS

- The Illinois Tollway requires electronic submittals for the Professional Services Bulletin's SOIs via the established Trimble Unity Construct PSB process. All respondents must utilize a unique 2 to 6-character SOI Firm Name Code assigned by the Illinois Tollway.
- To determine the designated SOI Firm Name Code go to the Illinois Tollway's website under Doing Business>Construction and Engineering - see Vendor Resources and click on the link to the Professional Services Bulletin page. The current SOI Firm Name Code List will be posted under the "Required Forms" section. If your firm is not included on the list, or your firm name has changed, please contact PSB Coordinator. csstaff@getipass.com, for an assigned SOI Firm Name Code.
- When submitting "Team" files please, use the **new** SOI Firm Name Code assigned by the Illinois Tollway to the Team. The SOI Firm Code Name is exclusive to the electronic submittal – meaning it does not establish the name of the Team. Please contact PSB Coordinator, csstaff@getipass.com, for an assigned SOI Firm Name Code.

3.4.3 INSTRUCTIONS FOR SUBMITTING THE SOITEAM DATA

The SOITEAM information is now input into the "SOITEAM data" section in Trimble Unity Construct. The following still apply to your submittal. Failure to provide the required information in the SOITEAM may result in the SOI being deemed non-responsive.

- Vendors are required to complete the SOITEAM data section for each Item, completing all columns shown for the Prime Consultant, and for every Subconsultant that is being proposed. ***Do not enter "TBD" or enter a range of percentages, and do not leave blank cells.*** Totals must equal 100%.

TEAM submittals:

- NOTE: If a firm is submitting as a Prime Consultant and also as a Team lead for one or more teams, a separate SOI and the SOITEAM data information must be submitted for each. DO NOT combine SOITEAM data information for unique SOI submittals.
- When entering Prime Consultant or Subconsultant information in the SOITEAM data section, please follow the below instructions:
    - Add new item for firm information for each team member
    - Under Team Member Role, select Prime (Lead Teaming Partner) or Prime (Non-Lead Teaming Partner)
    - Teams with three firms may enter an additional firm and select Prime (Non-Lead Teaming Partner)
    - Select Subconsultant for the Firm Role for any additional firms that are included in the SOI.
    - Below is a sample of how the Team members and Subconsultants are to be entered and submitted within the SOITEAM data section:

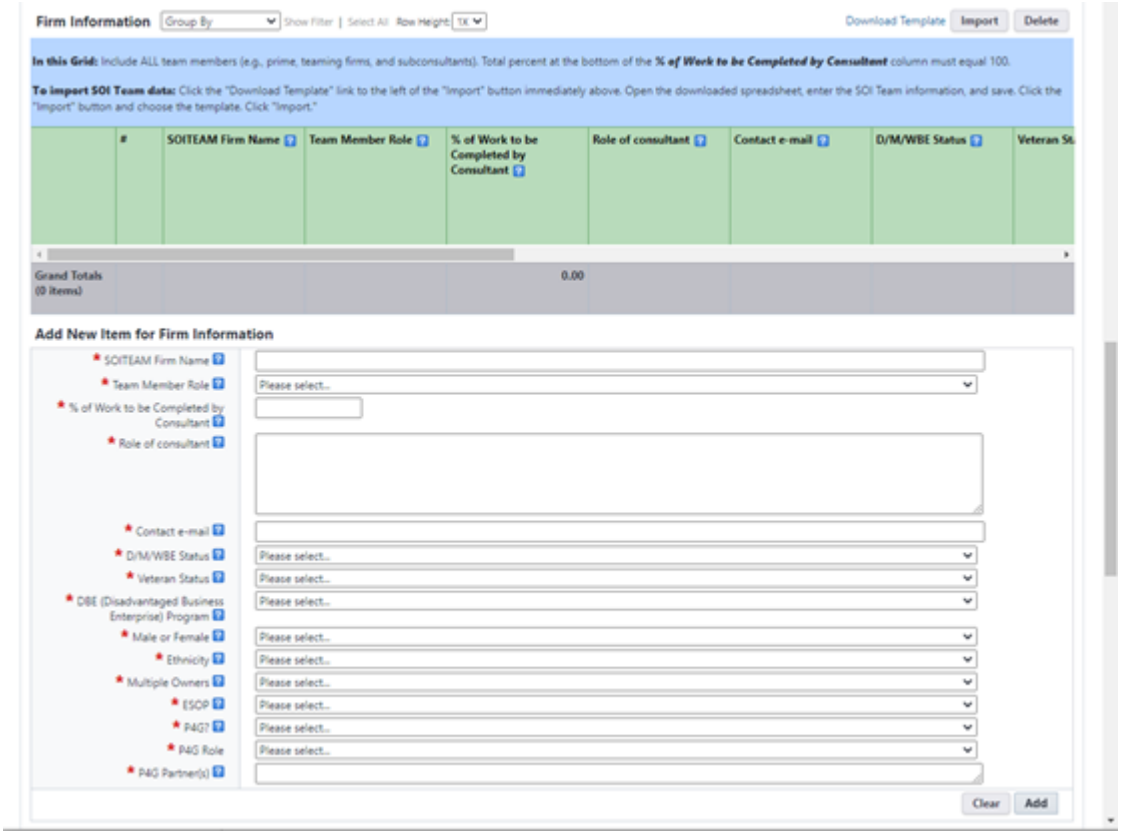

3.4.4 INSTRUCTIONS FOR Trimble Unity Construct SUBMITTAL

It is important that your Trimble Unity Construct submittal be prepared according to the following instructions:

A Statement of Interest file and required exhibit files must be attached to each SOI submission in Trimble Unity Construct. Files must a) be attached to the SOI process instance and b) be saved in the document folder corresponding to the item number. If a file will be used for more than one submission, a separate, unique file must be saved in the document folder for each item. Do not attach a file already saved in one item folder to an SOI submission for a different item.

The Word and/or PDF documents available (except for SOIs) on the Illinois Tollway website are labeled as follows:

FORM	FILE NAMING CONVENTION - EXAMPLE –	DIRECTIONS
SOI – Statement of Interest Includes cover sheet, executive summary, organizational chart and relevant project experience. For each Item submittal, use firm's 2-6-character SOI Firm Name Code (this example = ABC immediately followed by underscore SOI plus a 2-digit Item Number (i.e., SOI01 through SOI 99). See Section 3.3.2.3 SOI format Instructions.	ABC_SOI01.pdf	Submit as a separate document on Trimble Unity Construct

Teaming Submittal **SOI** use the team's unique 2-6-character SOI Team Name Code	ABCXYZ_SOI01_TM.pdf	Submit as a separate document on Trimble Unity Construct
Illinois Tollway Standard Business Terms and Conditions	ABC_TC.pdf	Submit as a separate document on Trimble Unity Construct
Teaming Agreement **Illinois Tollway Standard Business Terms and Conditions**	ABC_TC_TM.pdf DEF_TC_TM.pdf GHI_TC_TM.pdf	Submit as a separate document on Trimble Unity Construct for **each Team member**
Illinois Board of Elections Registration document	ABC_BOE.pdf	Submit as a separate document on Trimble Unity Construct
Teaming Agreement **Illinois Board of Elections Registration document**	ABC_BOE_TM.pdf DEF_BOE_TM.pdf GHI_iBOE_TM.pdf	Submit as a separate document on Trimble Unity Construct for **each Team member**
Vendor Disclosure (formerly Forms A) or IPG Active Registered Vendor Disclosure (formerly Forms B) (Disclosures) – are required. To submit use your 2-6-character SOI Firm Name Code followed by DS.	ABC_DS.pdf	Submit as a separate document on Trimble Unity Construct
Teaming Agreement **Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B) (Disclosures) – are required.** Use the unique 2-6-character SOI Firm Name Code for EACH individual Team firm name followed by _DS_TM	ABC_DS_TM.pdf DEF_DS_TM.pdf GHI_DS_TM.pdf	Submit as a separate document on Trimble Unity Construct for **each Team member**
<u>Exhibit A</u> – Proposed Staff – Key Project Personnel. a. Include resumes for Key Project Personnel proposed for the project (Prime Consultant and Subconsultants for those specific positions identified in the PSB item description). Resumes for each individual should not exceed two (2) pages and should include only relevant experience for the specific Item. b. List the Key Project Personnel to match the required prequalification categories and any additional personnel requirements designated in the Bulletin Items. (Include firm name if work is to be completed by a Subconsultant). c. QC/QA personnel must be different individuals than staff preparing the design documents. Construction Management Services require the names and resumes of Certified Record Documentation Reviewers and Inspectors that will be assigned to the project. Specific requirements are explained in the Phase	ABC_ExA.pdf	Submit as a separate document on Trimble Unity Construct

III Items.		
Exhibit C - Current Obligations, use your 2-6-character SOI Firm Name Code, followed by _WL One copy of the Current Obligations Form is required to be completed by the Prime Consultant. **Teaming Agreement** **Exhibit C -** use the unique 2-6-character SOI Team Name Code followed by _WL_TM	ABCWL.pdf ABCXYZ_WL_TM.pdf	Submit as a separate document on Trimble Unity Construct Submit as a separate document on Trimble Unity Construct. The document should include one form for each Team member.
Exhibit D – Availability of Key Project Personnel Firms must show the percentage of time identified Key Project Personnel will be available to work on the project described in each Item. We request a Word document saved in .pdf format to be completed with the relevant information.	ABC_ExD.pdf	Submit as a separate document on Trimble Unity Construct
Exhibit E – DBE/VOSB: Partnering for Growth Program - If proposing a mentor-protégé arrangement with a DBE or VOSB firm attach the required Exhibit E.	ABC_ExE_P4G.pdf	Submit as a separate document on Trimble Unity Construct
Exhibit E – Reverse DBE/VOSB: Partnering for Growth Program - If proposing a mentor-protégé arrangement with the **subconsultant mentoring** attach the required Exhibit E.	ABC_ExE_RevP4G.pdf	Submit as a separate document on Trimble Unity Construct
Exhibit F - Veteran Small Business Participation, Utilization Plan and Letter of Intent	ABC_ExF.pdf	Submit as a separate document on Trimble Unity Construct
Exhibit H - DBE Participation, Utilization Plan and Letter of Intent	ABC_ExH_DBE.pdf	Submit as a separate document on Trimble Unity Construct
Firm's Commitment and Signature Form.	ABC_FCS.pdf	Submit as a separate document on Trimble Unity Construct
DBE and VOSB Evidence (current certification letters)	DBE_VOSB_Certs.pdf	Submit as a separate document on Trimble Unity Construct

- Complete the Word documents and then convert them to Adobe.pdf for the submittal.
- Do not send zipped files. They will be rejected and cause the firm's submittal to be disqualified.
- Signatures must be scanned, then cut/copied and pasted into the appropriate signature blocks. The files must then be converted to a PDF.
- The time zone in your Trimble Unity Construct profile must be set to "(UTC-06:00) Central Time (US &

Canada)." The Time Zone field can be found on the Setup tab under Personal Information>My Profile. See the latest version of the SOI User Manual for instructions, available at the Trimble Unity Construct PSB SOI user manual, FAQ file, and training videos link in Section 3.7 Useful Links.

3.4.5 COMMON MISTAKES

The following is a list of common mistakes found when submitting a Professional Services SOI. This list is not intended to be exhaustive and firms should make every attempt to avoid these common mistakes in their submittals. **Responsive firms will be evaluated based on the information submitted by the due date and time.**

- General
  - Failure of minimum 40% self-performance by the Prime Consultant
  - Inconsistent percentages throughout SOI submittals
  - Incorrect PSB #
  - Incorrect Contract #
  - Changing anonymous Trimble Unity Construct PSB account profile entries
  - Submitting too close to the deadline
  - Failure to save attached document in the correct item folder for that submission.
  - Failure to provide the required DBE/VOSB participation/utilization information in the SOITEAM may result in the SOI being deemed non-responsive.

- SOITEAM Data
  - Leaving blank spaces
  - Percentage does not equal 100% – this percentage should include the Prime Consultant and Subconsultants
  - Failure to include all Firms from the SOI (Prime Consultant, Team, Subconsultants etc.)

- Exhibits
  - Failure to submit Exhibit E when proposing P4G plan in the SOITEAM data
  - Unnecessarily submitting Exhibit E when not proposing P4G in SOITEAM data
  - Failure to submit correct version of Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B)
  - Failure to list all required Key Personnel on Exhibit A
  - Change of the title of Key Personnel on Exhibit A
  - Failure to list % on Terms and Conditions FEIN page
  - Percentages different than SOITEAM Grid Data

- Teams
  - Failure to include all Team members on Exhibit C (Workload)
  - Failure to include Terms and Conditions for all Team members
  - Failure to include Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B) for all Team members

3.5 DISCLOSURES AND CERTIFICATIONS

3.5.1 INSTRUCTIONS FOR SUBMITTING DISCLOSURES

The submittal shall contain either Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B). SOIs submitted without Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B) shall be deemed non-responsive. Vendor Disclosures (formerly Forms A) section shall be returned by Firm(s) that are not registered in the Illinois Procurement Gateway (IPG). Enter the BidBuy number on either Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B) when asked to supply an IPB Reference #.

IPG Active Registration Vendor Disclosures (formerly Forms B) shall be returned by Firm(s) that have a current, approved IPG registration.

Vendor Disclosures (formerly Forms A) Section

*Complete this section if you **are not using** a current, approved Illinois Procurement Gateway (IPG) Registration number.*

https://www.illinoistollway.com/doing-business/construction-engineering/forms

1. Business and Directory Information
2. Illinois Department of Human Rights Public Contracts Number
3. Authorized to Do Business in Illinois
4. Standard Certifications
5. State Board of Elections
6. Disclosure of Business Operations in Iran
7. Financial Disclosures and Conflicts of Interest
8. Taxpayer Identification Number
9. Signature

IPG Active Registration Vendor Disclosures (formerly Forms B) Section

*Complete this section only if you are **using** a current, approved IPG Registration number.*

https://www.illinoistollway.com/doing-business/construction-engineering/forms

1. Certification of Illinois Procurement Gateway Registration #
2. Certification Timely to this Solicitation
3. Disclosures of Lobbyist or Agent
4. Disclosure of Current and Pending Contracts
5. Signature

3.5.2 INSTRUCTIONS FOR SUBMITTING ILLINOIS TOLLWAY STANDARD BUSINESS TERMS AND CONDITIONS

Submit the Illinois Tollway Standard Business Terms and Conditions. This document is also available on the Illinois Tollway website and submit as a separate document on Trimble Unity Construct. Team leads must submit Illinois Tollway Standard Business Terms and Conditions for themselves and team members.

3.6 PROTEST PROCEDURE

Vendors may submit a written protest to the Protest Review Office following the requirements of the IDOT Standard Procurement Rules 44 ILL ADM 6.390 through 6.440. All protests shall be in writing and filed with the CPO within seven (7) calendar days after the protester knows or should have known of the facts giving rise to the protest. Protests filed after the seven (7) calendar day period will not be considered. In addition, protests that raise issues of fraud, corruption or illegal acts affecting specifications, special provisions, supplemental specifications and plans must be received by the CPO no later than fourteen (14) calendar days before the date set for opening of bids. The Protest Review Office information is as follows:

Chief Procurement Office for General Services
Attn: Protest Review Office

Email: cpogs.pro@illinois.gov

3.7 USEFUL LINKS

The Illinois Tollway website- https://www.illinoistollway.com/

Professional Service Bulletin- https://www.illinoistollway.com/doing-business/construction-engineering/bids-bulletins-awards

Vendor Contract Forms (required forms for submittal) - https://www.illinoistollway.com/doing-business/construction-engineering/forms

Vendor Invoicing Forms - https://www.illinoistollway.com/doing-business/construction-engineering/forms

Partnering for Growth Program - https://www.illinoistollway.com/doing-business/diversity-development/programs/partnering-for-growth

Trimble Unity Construct website- https://app.e-builder.net/

Trimble Unity Construct PSB SOI user manual, FAQ file, and training videos- https://app.e-builder.net/public/PublicFolderView.aspx?FolderID=%7bdc0355ee-4323-458e-91b5-547c6655b5f5%7d

Trimble Unity Construct PSB SOI training webinar dates and registration information- https://calendly.com/tollwaywbpm-getipass/psb-sois?back=1&month=2026-04

Bid Buy - https://www.bidbuy.illinois.gov/bso/view/login/login.xhtml

Chief Procurement Office/Illinois Procurement Gateway (IPG) – Vendor Registration - https://ipg.illinois.gov/

State Board of Elections -https://www.elections.il.gov/#News

Illinois Department of Central Management Services – Travel Reimbursement Schedule - https://www2.illinois.gov/cms/employees/travel/pages/default.aspx

National Institute of Standards and Technology - http://www.nist.gov/

Illinois Department of Transportation - http://www.idot.illinois.gov/

Illinois Department of Transportation Manual of Test Procedures for Materials https://public.powerdms.com/IDOT/documents/2732503

3.8 ILLINOIS ePROCUREMENT BidBuy NOTICE

To register in the Illinois eProcurement System, please follow these instructions:

- Go to https://www.bidbuy.illinois.gov/bso/
- Please direct questions regarding the registration process or the use of BidBuy to email address: stateuser.bidbuy@illinois.gov or the Procurement Help desk at 217-557-8992.

3.9 INFORMATION ON ACCESSING ILLINOIS TOLLWAY WEBSITE

- Go to www.illinoistollway.com
- Click on “Menu”
- Click “Doing Business”
- Click “Construction and Engineering”
- Middle of page, under “How Can We Help You? / Vendor Resources” click “Professional Services Bulletin”
- *Helpful Hint: A limited number of items are shown under “Professional Services Bulletin” on each page; click “Next” to view additional items.

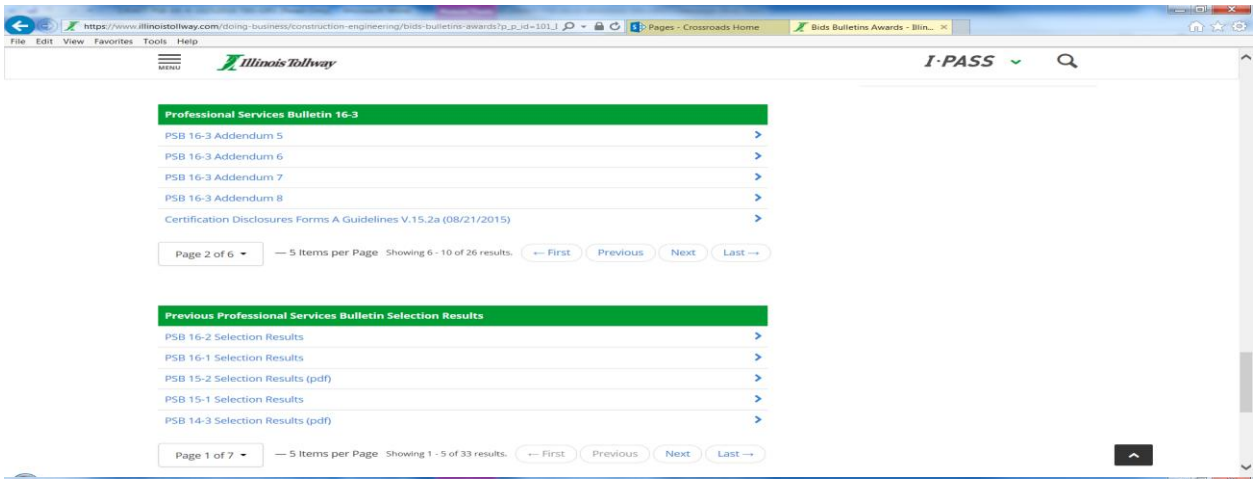

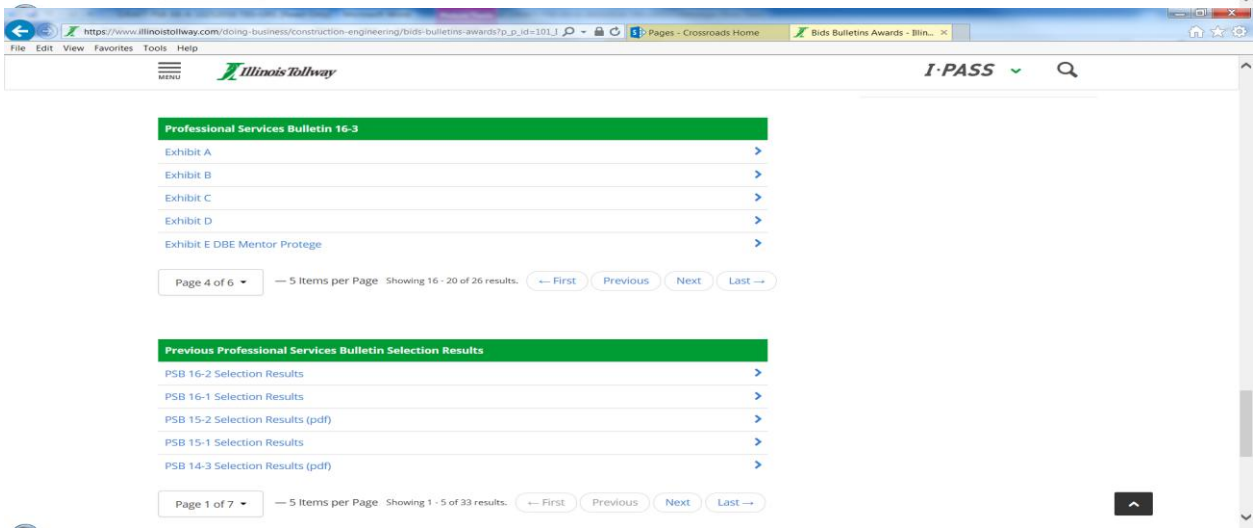

3.10 FUTURE PROFESSIONAL SERVICES BULLETIN NOTIFICATIONS

To receive notification from the Illinois Tollway that a Professional Services Bulletin has been posted, or to Unsubscribe, please email Catrice Hardwick-Giles chardwick@getipass.com or call 630-241-6800 extension 4653.

Include the following information:

Please add this contact to receive notification from the Illinois Tollway that a Professional Services Bulletin has been posted:

Name of firm _____

E-mail address _____

Contact person (corresponding with e-mail) _____

3.11 RESERVED

3.12 PSB 26-4 EXCHANGES WITH FIRMS AFTER SOI SUBMISSION

Discussions may be held with Firms to clarify certain aspects of their SOIs.

- Discussions are limited exchanges between the Tollway and Firms that may occur during the responsiveness determination. For purpose of this PSB, such discussions shall be exchanged only between the Firm and the Designated Procurement Contact for this PSB.
- Please use the e-mail address: csstaff@getipass.com
- These exchanges shall not provide an opportunity for the Firm to revise its SOI, but may only address:
    - Deficiencies
    - Errors
    - Omissions
- Responses are due to the Illinois Tollway on the due date established by the Illinois Tollway. Discussions may be initiated by the Illinois Tollway after that time. Firm's responses that are not received timely shall result in the SOI being considered non-responsive.

Certain requirements are not open for discussion and, if not met, shall render the SOI non-responsive:

- Late submissions, including omission of the required documents as stated in the PSB:
    - SOI
    - Disclosures (DS)- Vendor Disclosures (formerly Forms A) or IPG Active Registration Vendor Disclosures (formerly Forms B)
- Omission of State of Illinois requirements
- Inability to meet eligibility requirements as stated in 44 Ill. Admin. Code 625.70, Confirmation of Eligibility.

ILLINOIS TOLLWAY

PSB 26-4 Pre-Proposal Meeting

October 15, 2026



Design Corridor Management (DCM) and Phase II Engineering Services

Contract Duration: Anticipated approximately 42 months after authorization to proceed

DCM for entire corridor

(IL Route 251 to IL Route 56, nearly 38 miles)

- Design coordination with other phase II engineering consultants to provide consistency and coordinate across design sections
- Serve as Tollway's representative, along with Tollway Project Manager on coordination with outside agencies and stakeholders
- Construction coordination to identify and mitigate constructability issues and inform design
- Maintain and track corridor schedule, budget and risk register

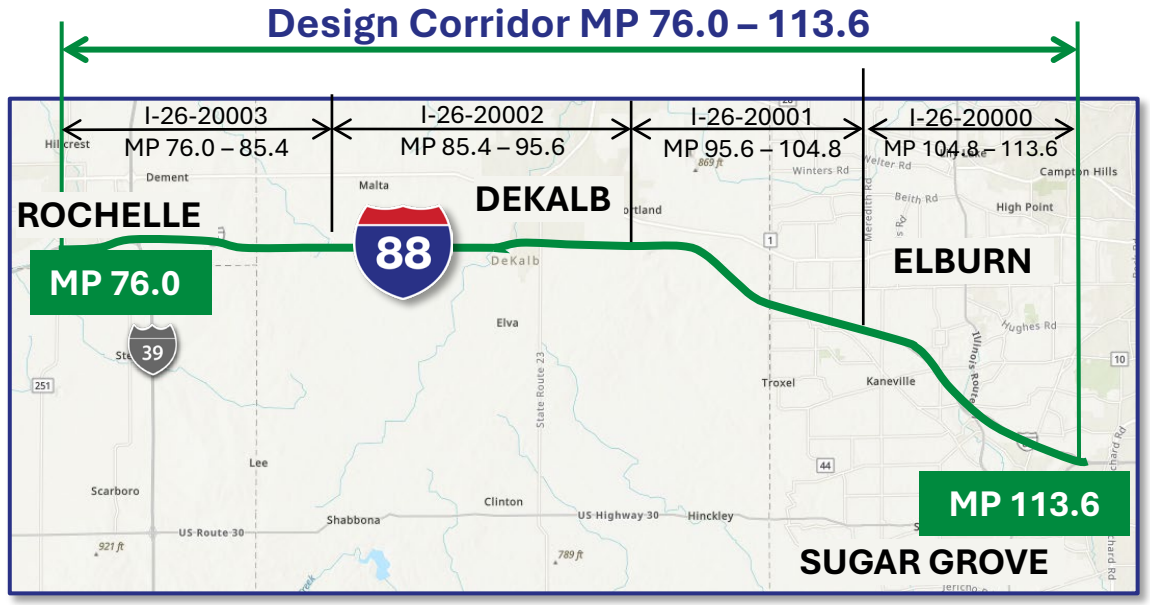

Design Corridor Management (DCM) and Phase II Engineering Services

Contract Duration: Anticipated approximately 42 months after authorization to proceed

Phase II engineering services for nearly nine miles of roadway reconstruction and bridge rehabilitation
(Dauberman Road to IL Route 56)

- May include reconstruction of structures over Blackberry Creek, requiring a hydraulic analysis
- Provide analysis of widening between IL Route 47 and IL Route 56
- Coordination with Kane County for ongoing project(s) in the area
- Evaluate repairs to seven structures

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.



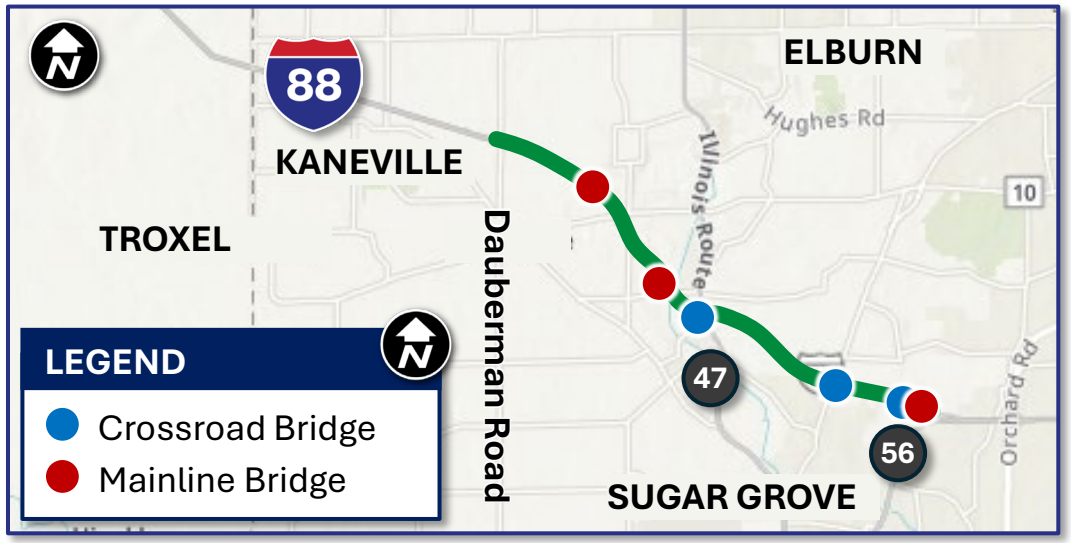

Phase II Engineering Services - Roadway Reconstruction and Bridge Rehabilitation

Contract Duration: Anticipated approximately 42 months after authorization to proceed

Phase II engineering services for more than nine miles of roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88)

(Somonauk Road to Dauberman Road)

- Requires design for culvert reconstruction
- Coordination with Kane County for ongoing project(s) in the area
- Evaluate repairs to six structures

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.



Phase II Engineering Services - Roadway Reconstruction and Bridge Rehabilitation

Contract Duration: Anticipated approximately 42 months after authorization to proceed

Phase II engineering services for more than 10 miles of roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88)

(Shabbona Road to Somonauk Road)

- Requires design for culvert reconstruction
- Evaluate repairs to fifteen structures

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

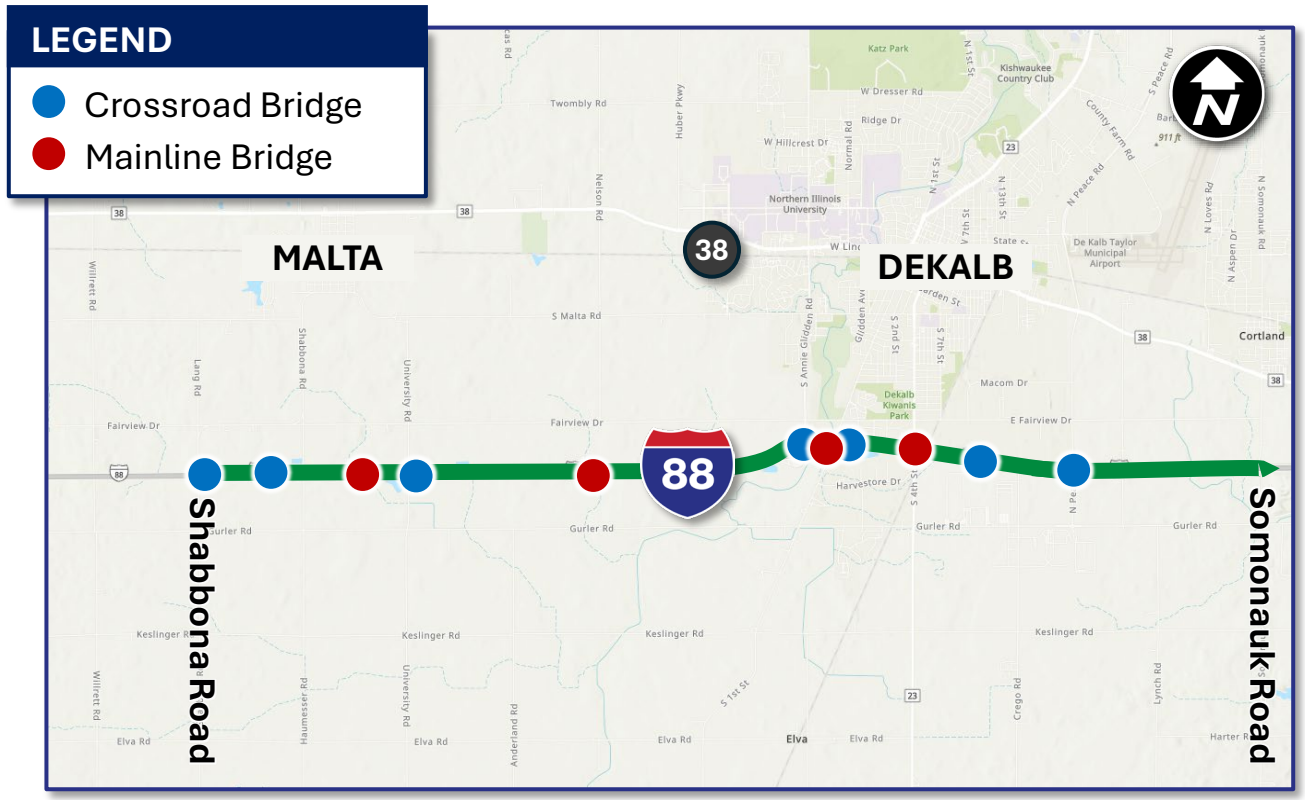

Phase II Engineering Services - Roadway Reconstruction and Bridge Rehabilitation

Contract Duration: Anticipated approximately 42 months after authorization to proceed

Phase II engineering services for more than nine miles of roadway reconstruction and bridge rehabilitation on the Reagan Memorial Tollway (I-88)

(IL Route 251 to Shabbona Road)

- Requires design for culvert reconstruction
- Evaluate repairs to twelve structures
- Includes design of bridges over BNSF railroad

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

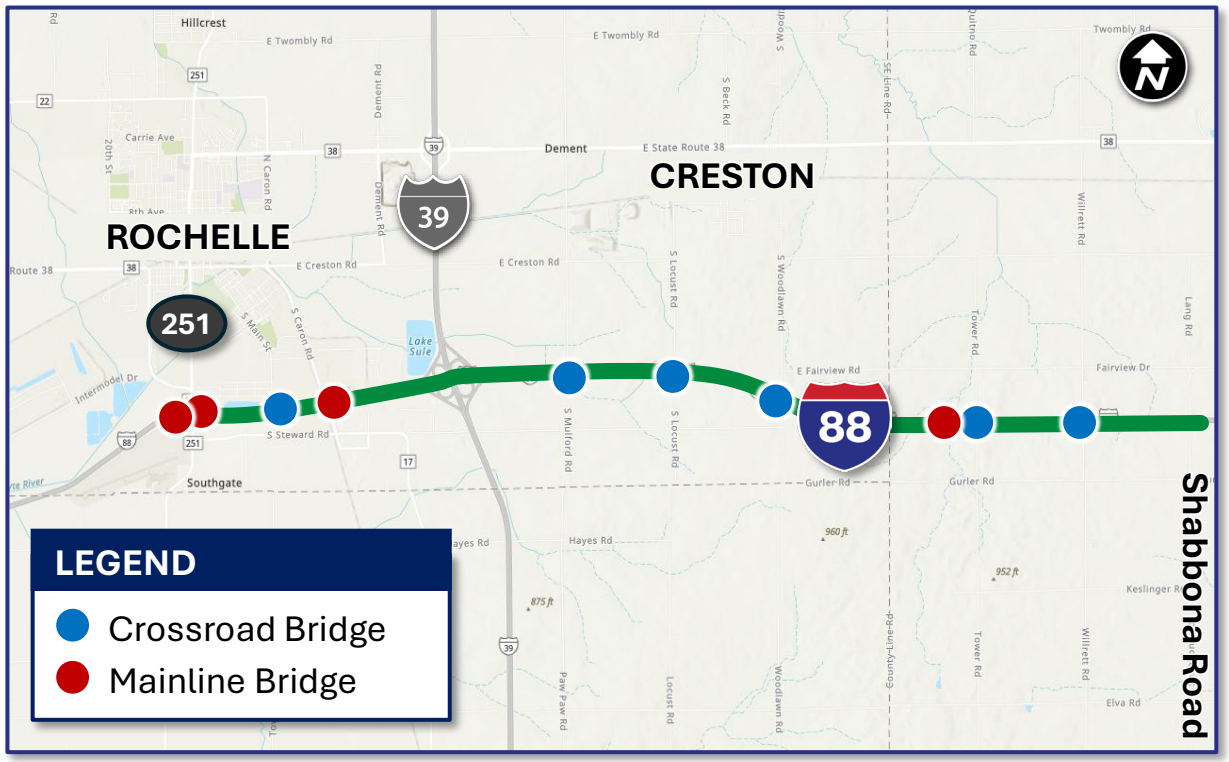

Phase II Engineering Services - Roadway and Bridge Rehabilitation

Contract Duration: Anticipated approximately 36 months after authorization to proceed

Phase II engineering services for more than one mile of roadway and bridge rehabilitation on the Tri-State Tollway (I-294)

(171st Street to 159th Street)

- Evaluate repairs to three structures
- Includes conversion of plazas 43 and 45 at I-80 to barrier free
- Study of the I-294 merge with I-80 required

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

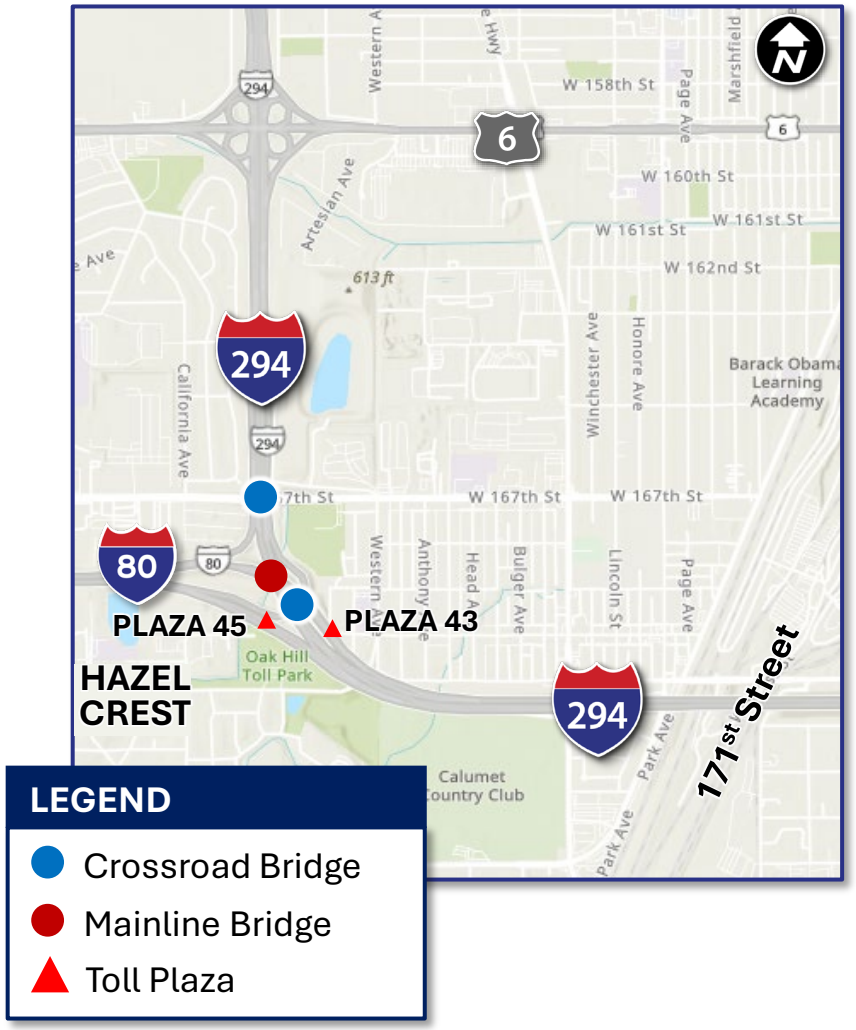

Phase II Engineering Services - Roadway Rehabilitation

Contract Duration: Anticipated approximately 36 months after authorization to proceed

Phase II engineering services for nearly five miles of roadway rehabilitation on the Tri-State Tollway (I-94)

(I-294 to the Edens Expressway)

- Includes conversion of Edens Spur Plaza 24 to barrier free
- Mill and overlay anticipated between I-294 and Pfingsten Road

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

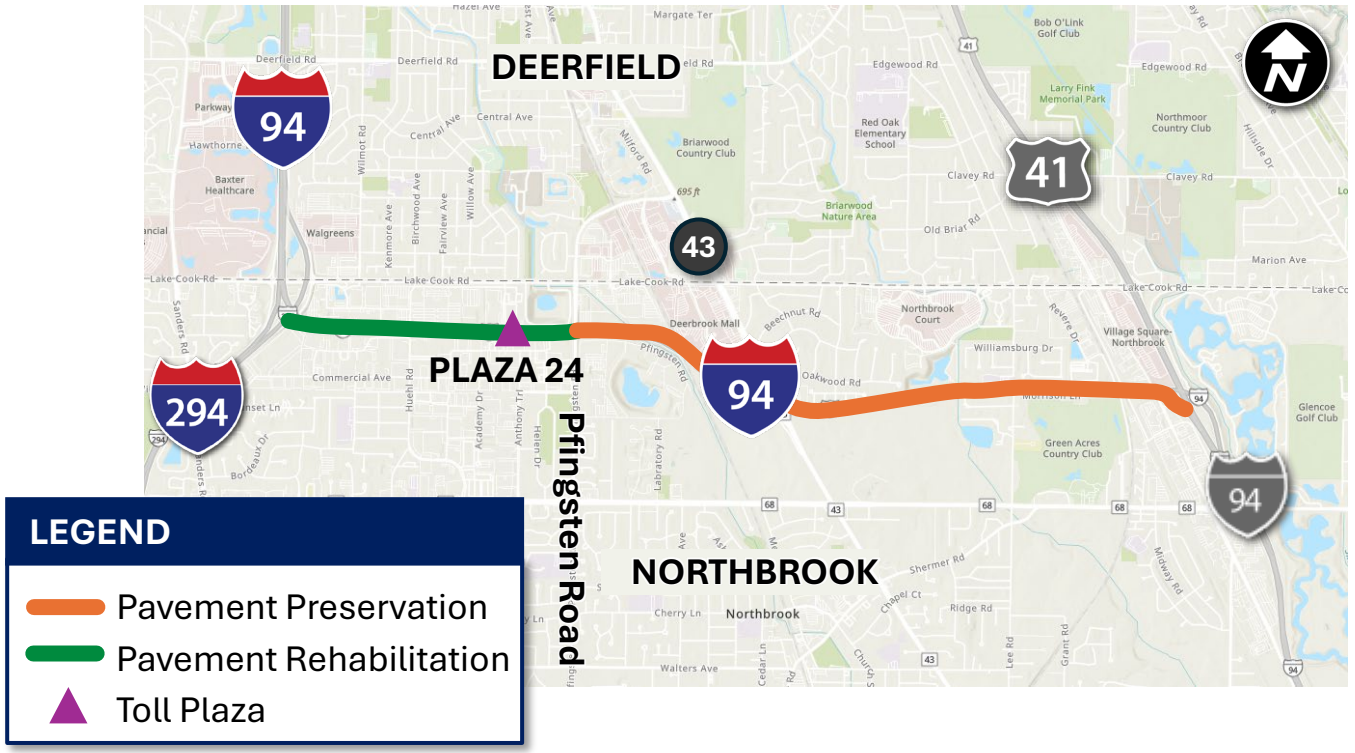

Phase II Engineering Services - Roadway Widening

Contract Duration: Anticipated approximately 36 months after authorization to proceed

Phase II engineering services for nearly three miles of roadway widening on the Reagan Memorial Tollway (I-88)

(Highland Avenue to IL Route 83)

- Widening anticipated in the westbound direction only
- Slope wall modifications anticipated at Meyers Road and Midwest Road bridges over I-88
- Incorporate potential new westbound entrance ramp from 22nd Street

Phase II design services are anticipated to be completed approximately 24 months after notice to proceed.

Phase III support during construction is required.

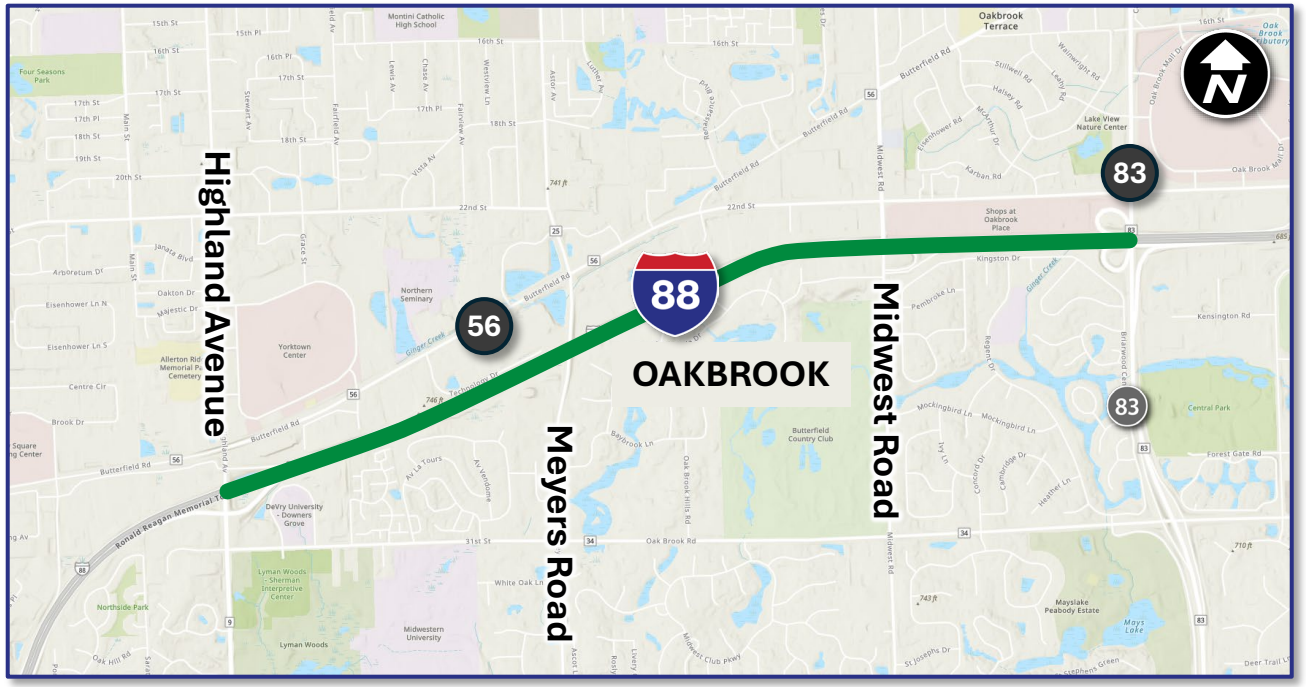

Phase II Engineering Services – Bridge Reconstruction

Contract Duration: Anticipated approximately 48 months after authorization to proceed

Phase II engineering services for reconstruction of the Roselle Road Bridge over Illinois Route 390

- Requires coordination with Cook County and Roselle
- Construction may be led by Cook County

Phase II design services are anticipated to be completed approximately 24 months after notice to proceed.

Phase III support during construction is required.



ITEM # 8 CONTRACT # I-26-70000 ILLINOIS ROUTE 390

Phase II Engineering Services – Bridge Reconstruction





Roselle Road Bridge over the Illinois Route 390 Tollway





Phase II Engineering Services – Bridge Reconstruction

Contract Duration: Anticipated to be approximately 36 months after authorization to proceed

Phase II engineering services for bridge reconstruction along the Tri-State Tollway (I-94) at Atkinson Road and Everett Road

- Requires coordination with Lake County, Lake Forest, Mettawa and Green Oaks
- Include widening for bicycle/pedestrian accommodations
- Provide standard horizontal clearance along I-94

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

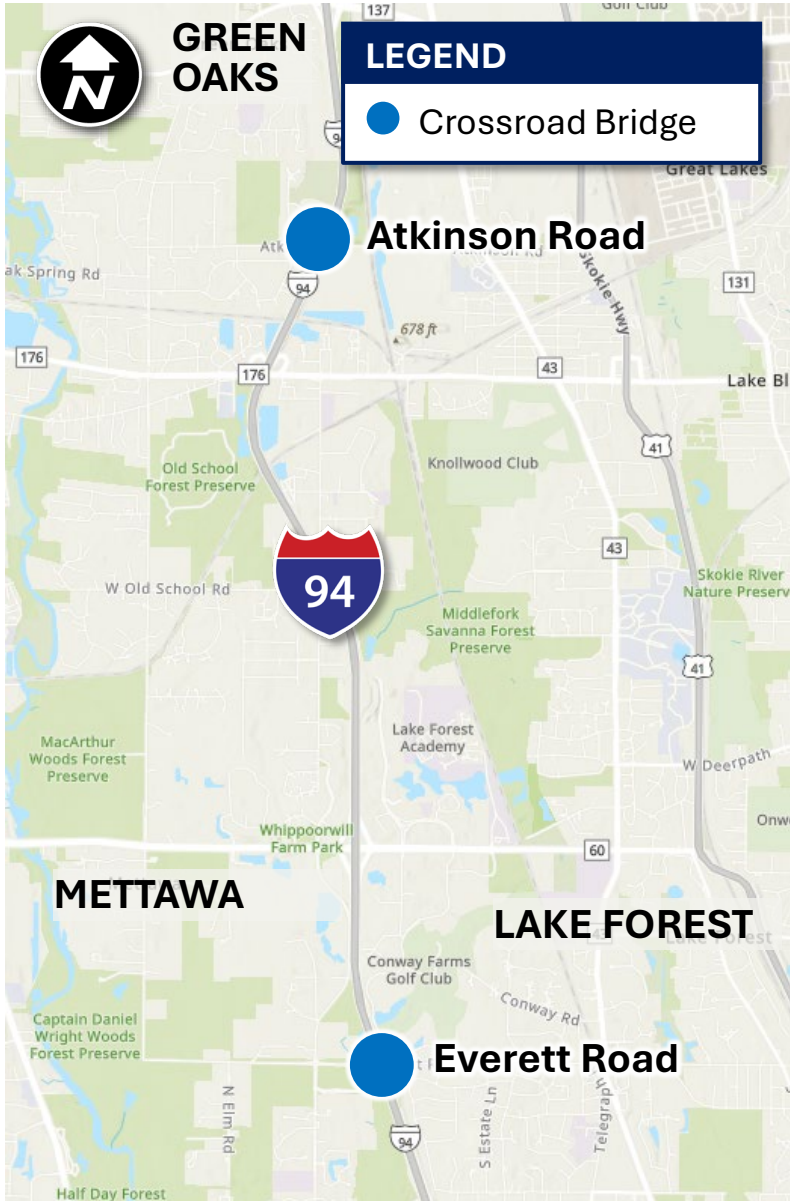

Phase II Engineering Services – Bridge Reconstruction

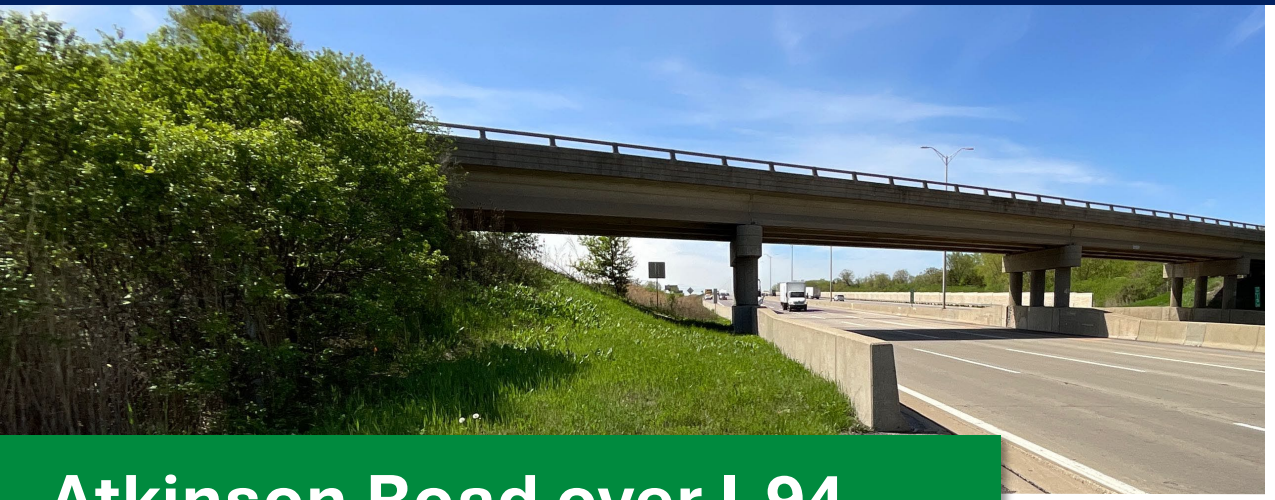

Atkinson Road over I-94

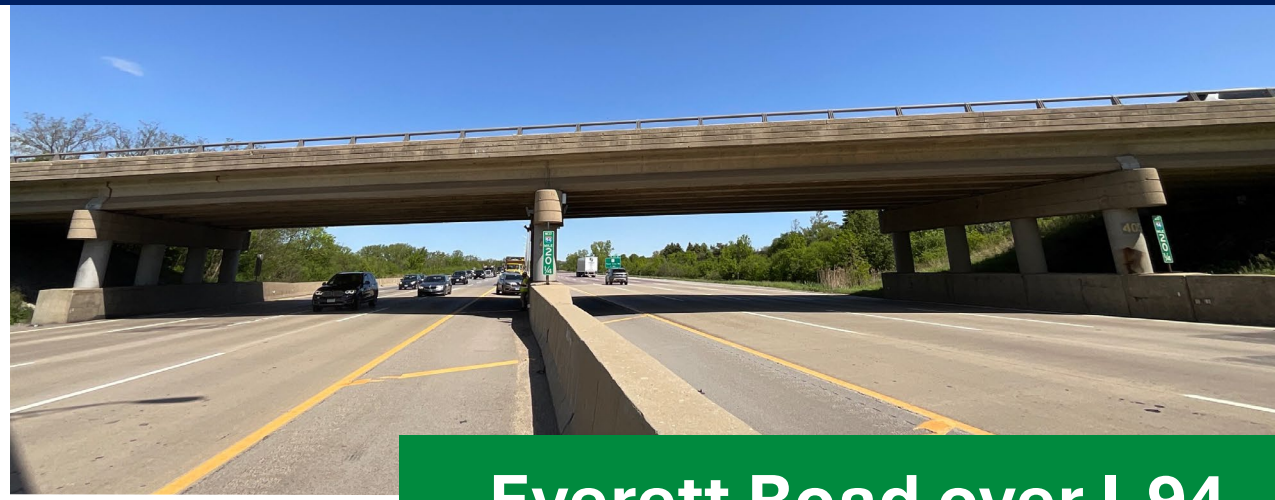

Everett Road over I-94



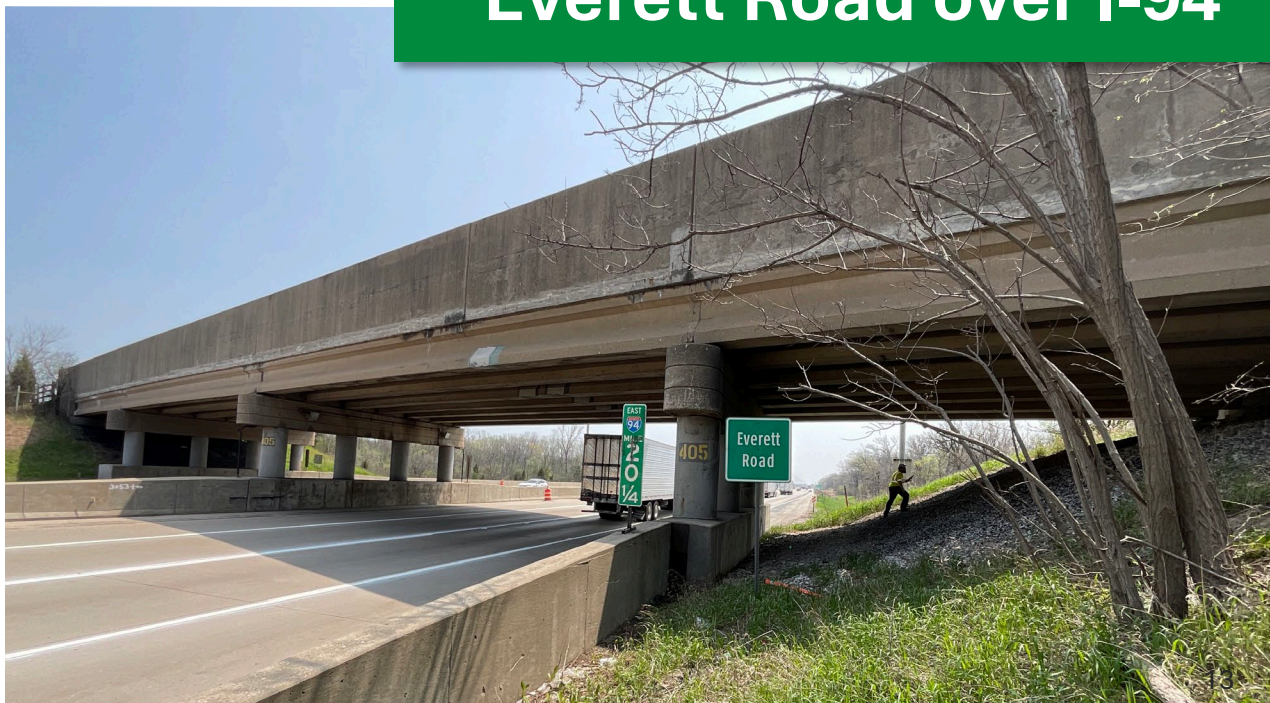

Phase II Engineering Services – Bridge Reconstruction

Contract Duration: Anticipated approximately 36 months after authorization to proceed

Phase II engineering services for bridge reconstruction along the Jane Addams Memorial Tollway (I-90)

(*Rockton Road to Rote Road)*

- Four separate structures included
- Requires coordination with Roscoe, Caledonia, Rockford and Winnebago County
- Includes widening for bicycle/pedestrian accommodations
- Provide standard horizontal clearance along I-90

Phase II design services are anticipated to be completed approximately 18 months after notice to proceed.

Phase III support during construction is required.

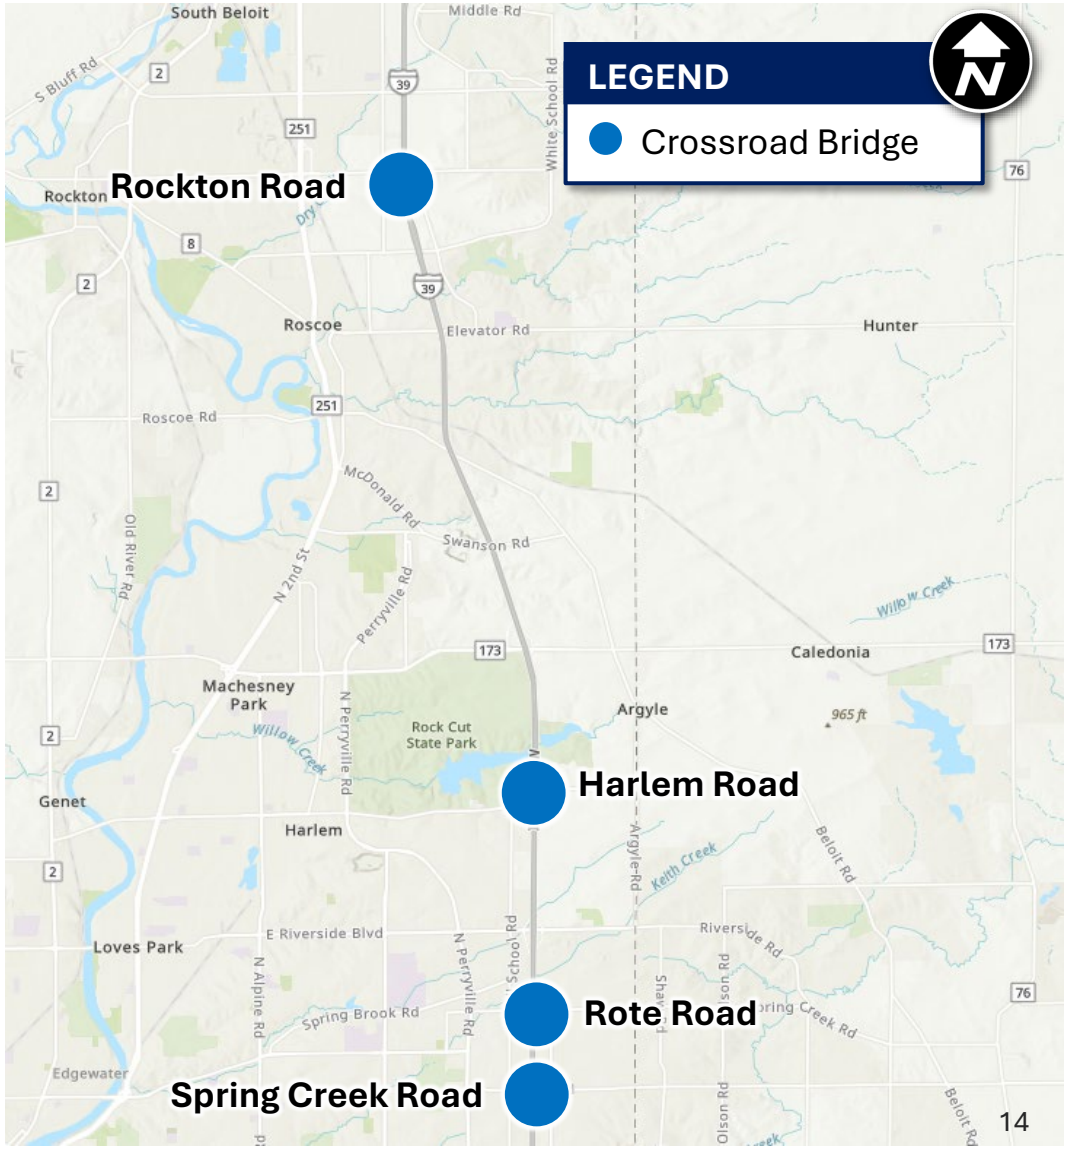

ITEM # 10 CONTRACT # I-26-50000 JANE ADDAMS MEMORIAL TOLLWAY (I-90)

Phase II Engineering Services – Bridge Reconstruction

Rockton Road



Harlem Road



Rote Road



Spring Creek Road



Phase II Engineering Services – Fiber Optic System Improvements

Contract Duration: Anticipated approximately 24 months after authorization to proceed

Limits along the Jane Addams Memorial Tollway (I-90)

(Rockton Road to Plaza 9 (Elgin Plaza))

Scope includes:

- Design of new fiber optic cables and conduit
- Design of communications equipment and systems
- Landscaping and soil erosion/sedimentation control

Phase II design services are anticipated to be completed approximately 12 months after notice to proceed.

Phase III support during construction is required.

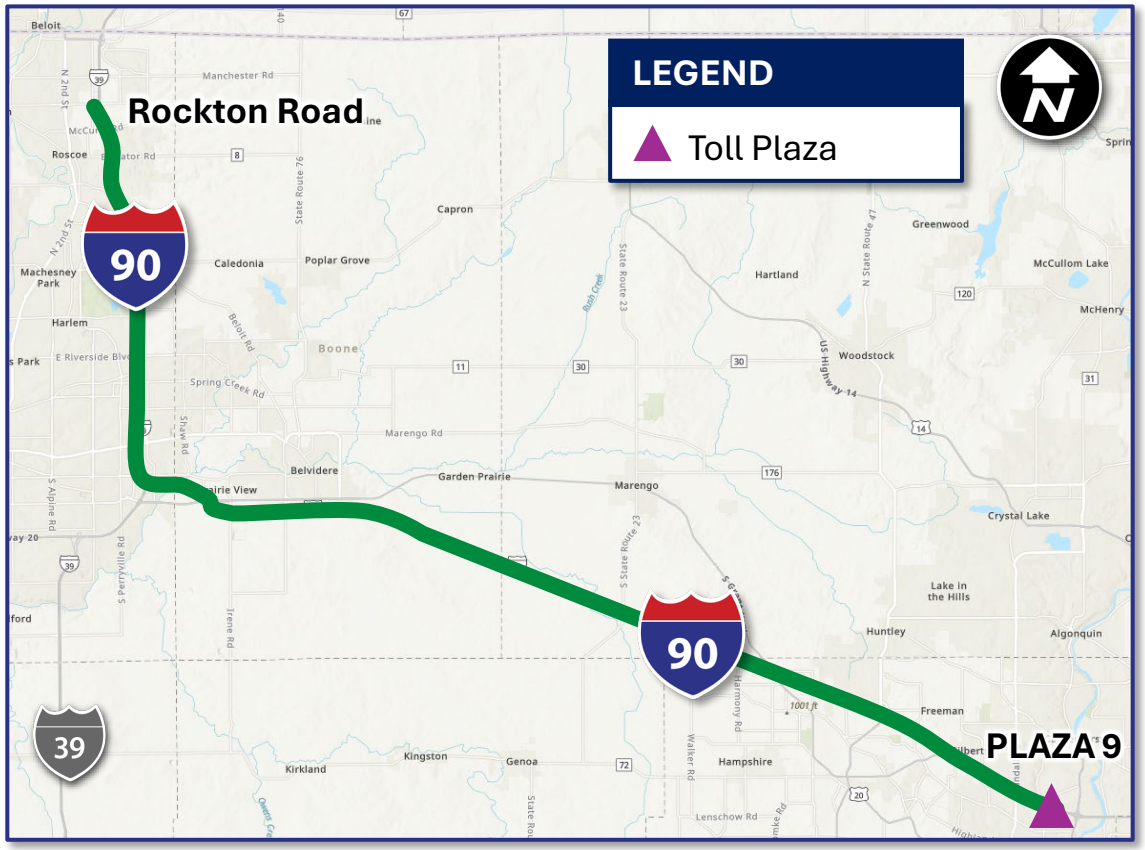

Phase II Engineering Services – Noise Abatement Wall Reconstruction

Contract Duration: Anticipated to be approximately 42 months after authorization to proceed

Limits along the Veterans Memorial Tollway (I-355)

(I-55 to Army Trail Road)

Scope includes:

- 63rd Street to Butterfield Road/IL Route 56 will be omitted from this contract
- Noise study
- Design of noise walls
- Pre-concept design services for future roadway reconstruction required
- Geotechnical services as required to support the above items

Phase II design services are anticipated to be completed approximately 24 months after notice to proceed.

Phase III support during construction is required.

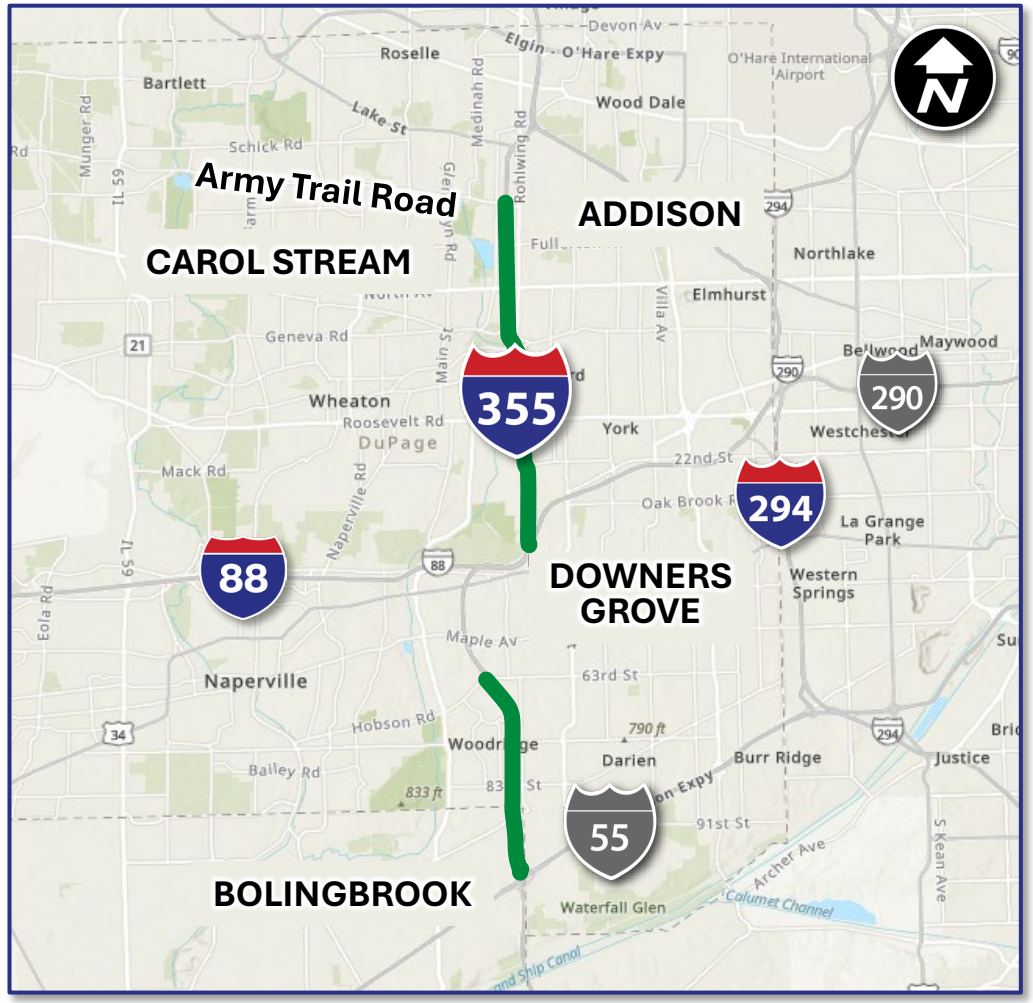

Phase II Engineering Services – Active Traffic Management System Installation

Contract Duration: Anticipated approximately 30 months after authorization to proceed

Limits along the Tri-State Tollway (I-94)

(Grand Avenue to O'Plaine Road)

Scope includes:

- Active Traffic Management System (ATMS) and ITS system design
- Signing and pavement marking design
- Landscaping and soil erosion/sedimentation control
- Geotechnical services as required to support the above items

Phase II design services are anticipated to be completed approximately 12 months after notice to proceed.

Phase III support during construction is required.

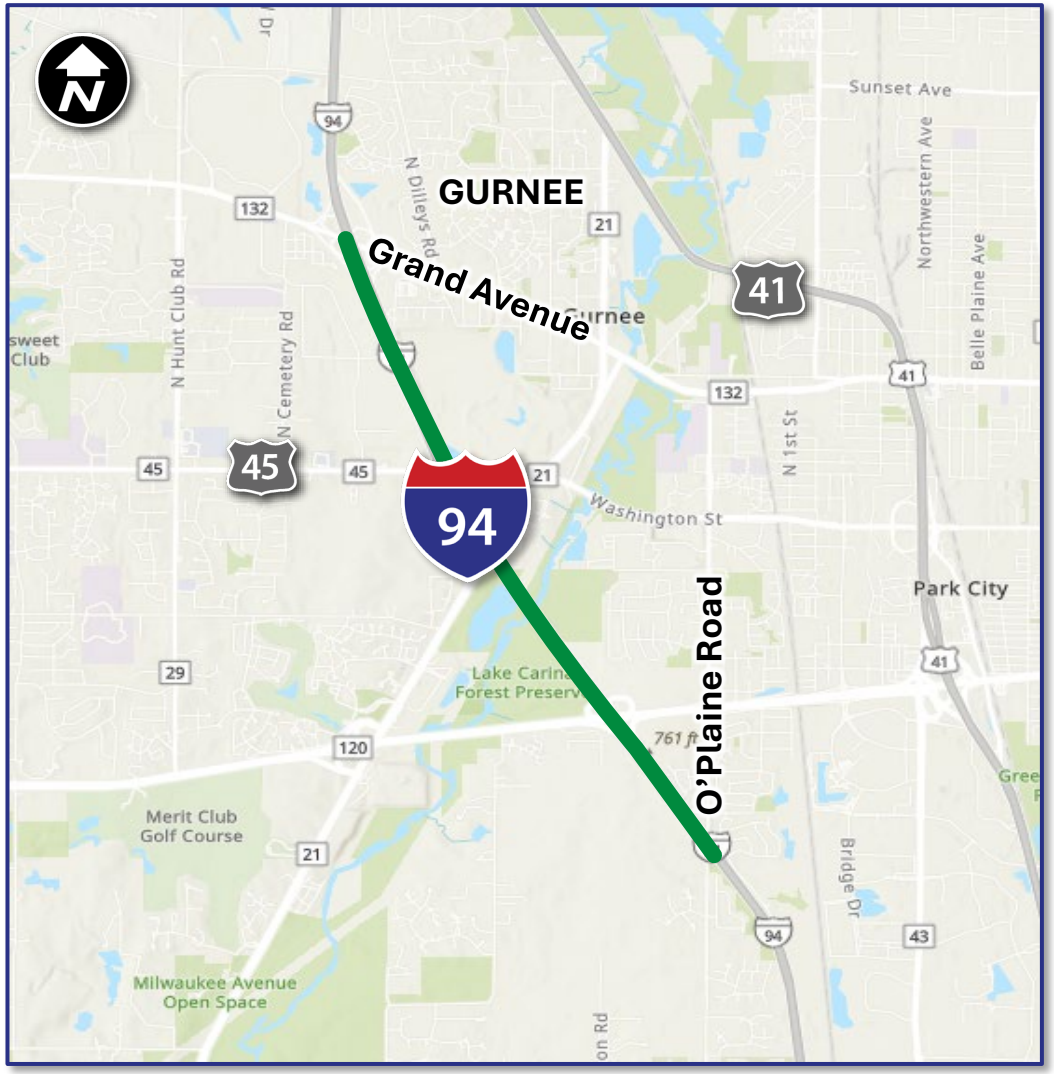

Phase II Engineering Services - Interchange Improvements at Irving Park Road

Contract Duration: Anticipated approximately 48 months after authorization to proceed

Phase II engineering services for interchange improvements along the Tri-State Tollway (I-294) at Irving Park Road

- New flyover structure over I-294 anticipated
- Requires coordination with:
  - Illinois Department of Transportation
  - Schiller Park
  - Chicago Department of Aviation
- Phase 1 being completed under a separate contract

Phase II design services are anticipated to be completed approximately 24 months after notice to proceed.

Phase III support during construction is required.



Phase II Engineering Services - Interchange Improvements at Irving Park Road

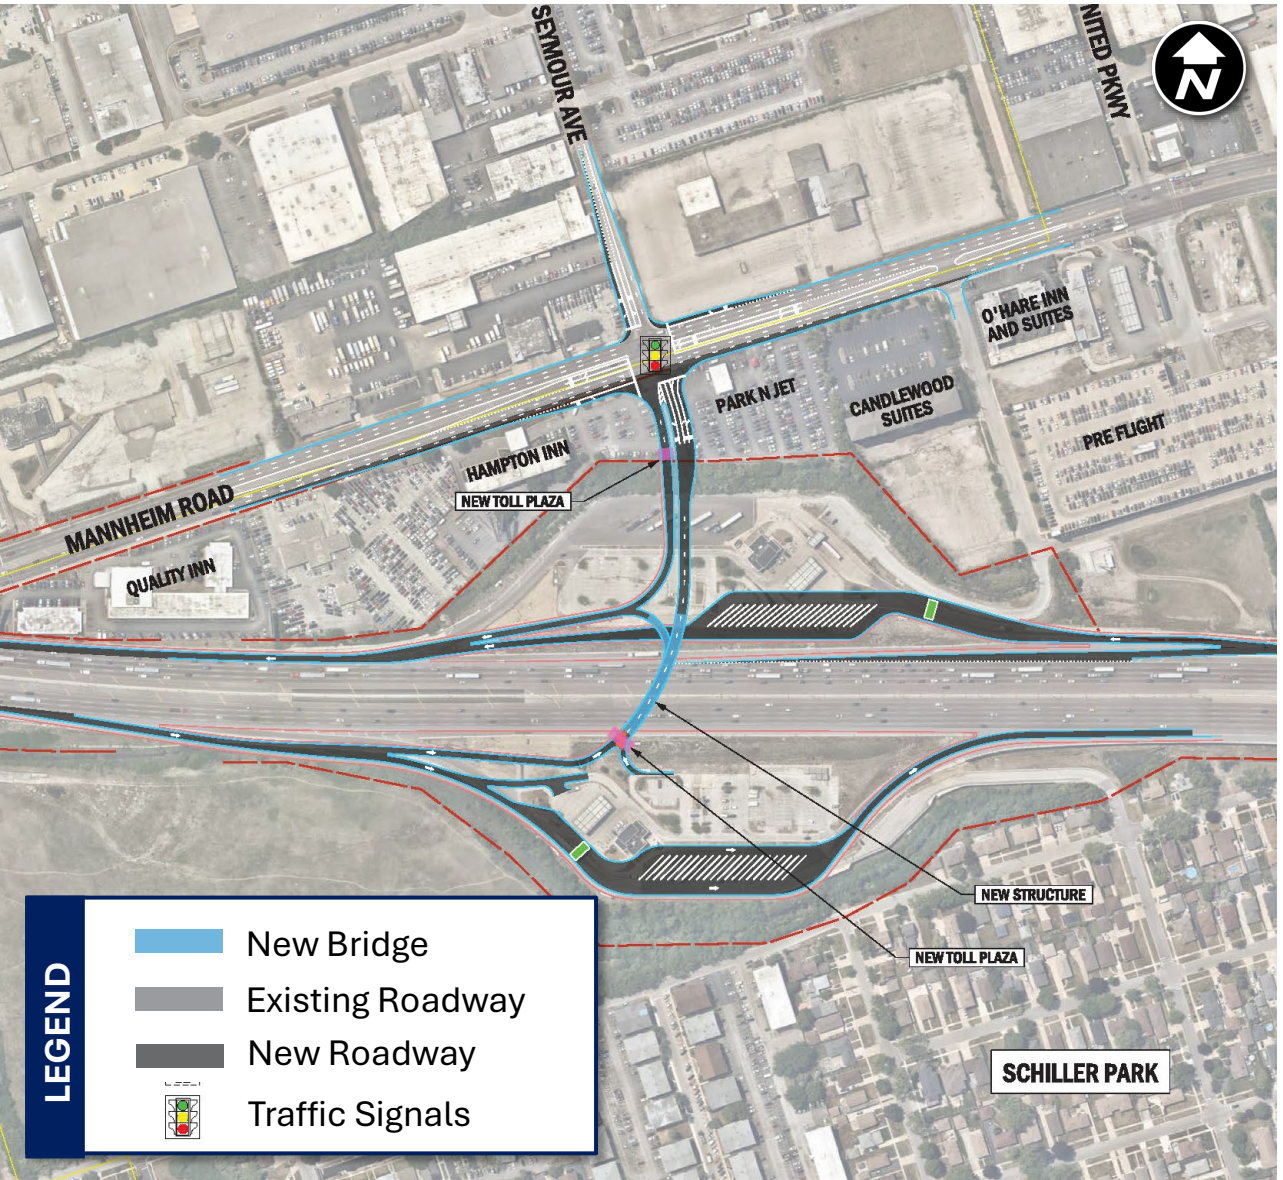

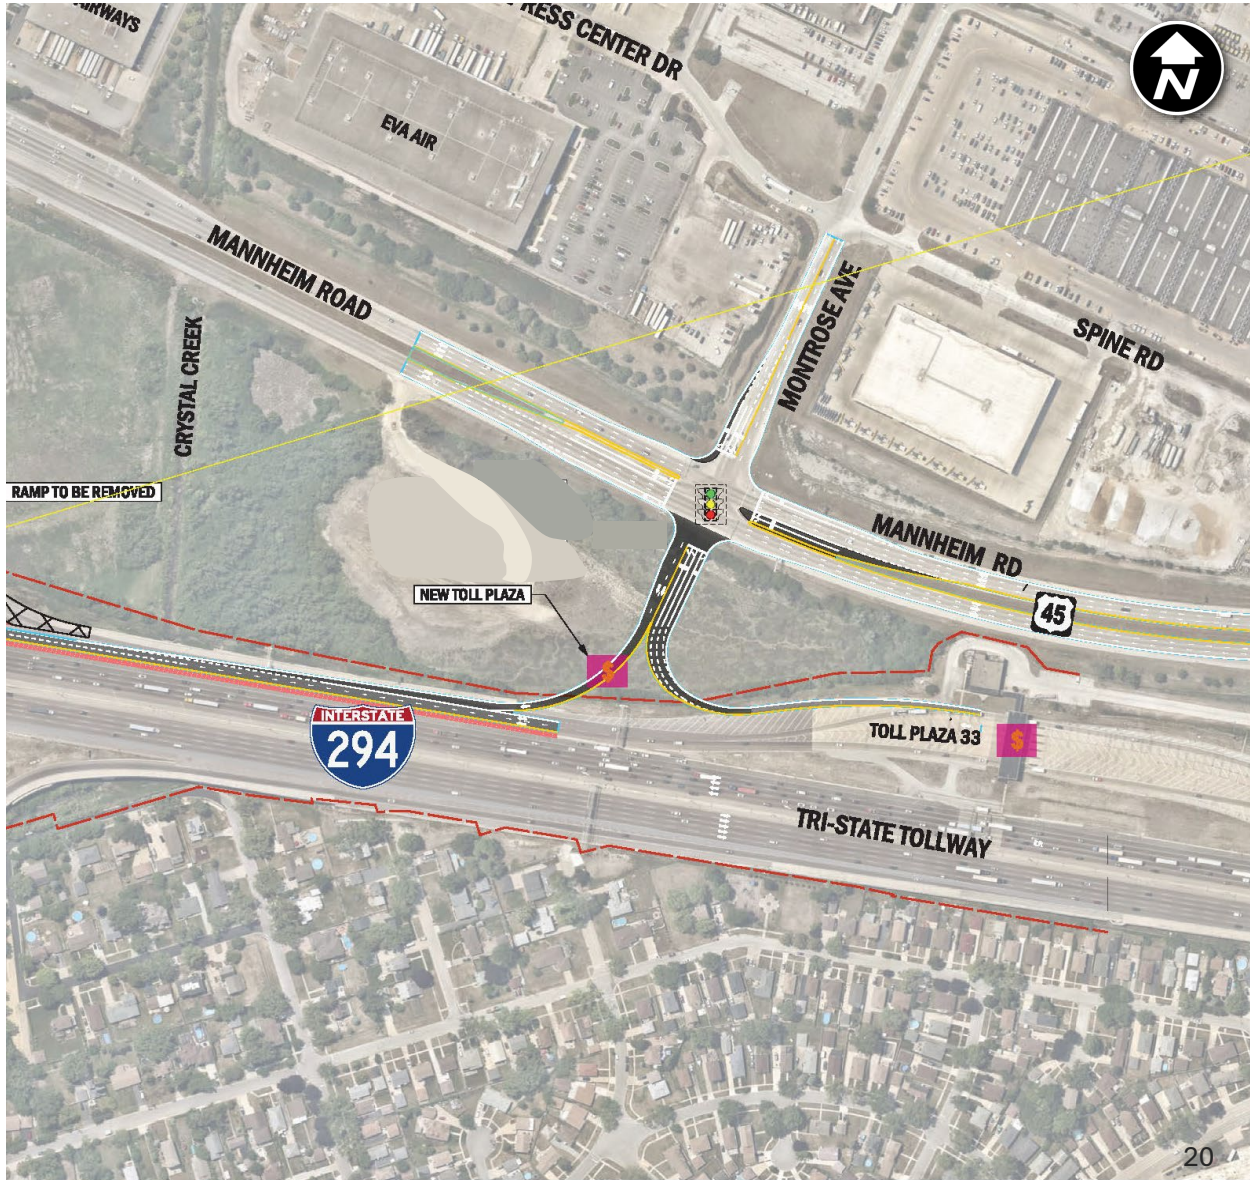

Procurement
and Submittal & Training



IN THIS SECTION

Training and system access

Required documents and forms

Schedule and deadlines

SUBMITTAL • 01

Training & System Access

AREAS OF FOCUS

- Register for PSB Submission Training webinar — October 19, 2026 or October 28, 2026
- Obtain your Unity Construct login ID
- Obtain your firm code name
- Review the SOI user manual, FAQ and videos
- Resources are posted in the public folder

Set up access early. Do not wait for the deadline.



SUBMITTAL • 02

What You Must Submit

AREAS OF FOCUS

- SOI and Team Grid — all firms total 100%
- Disclosures for the prime and team partners
- Illinois Standard Business Terms and Conditions
- Firm's Commitment and Signature Form
- Current exhibits in PDF

Late submittals and missing disclosures cannot be cured.



SUBMITTAL • 03

Schedule

KEY DATES

- Questions due — 4:30 p.m., October 21, 2026
- Statements of Interest due — 4:30 p.m., October 30, 2026
- Selections Posted — December 2026

Submit early. Late submittals cannot be cured.



Diversity
and Strategic Development



IN THIS SECTION

Mentor–protégé support

Capability building

Exhibit E

Technical assistance

DIVERSITY • 01

Support Programs

PROGRAM FOCUS

- P4G pairs primes with diverse and veteran-owned firms
- Mentor–protégé scopes build Tollway-ready capabilities
- Proposed relationships require Exhibit E with the SOI
- TA: SOI, certification and prequalification support
- Capability statements, relationship building and marketing

Build capability. Strengthen relationships.



Contract Compliance

IN THIS SECTION

- Participation goals
- Exhibits H and F
- Certifications
- Good faith efforts



COMPLIANCE • 01

What We Verify

AREAS OF FOCUS

- Participation goals —% D/M/WBE; % VOSB/SDVOSB
- Exhibits H and F — plans and letters of intent
- Current letters of certification
- Good faith efforts when goals are not met
- Defined scopes with NAICS and NIGP codes

Be specific about scope and commercially useful function.



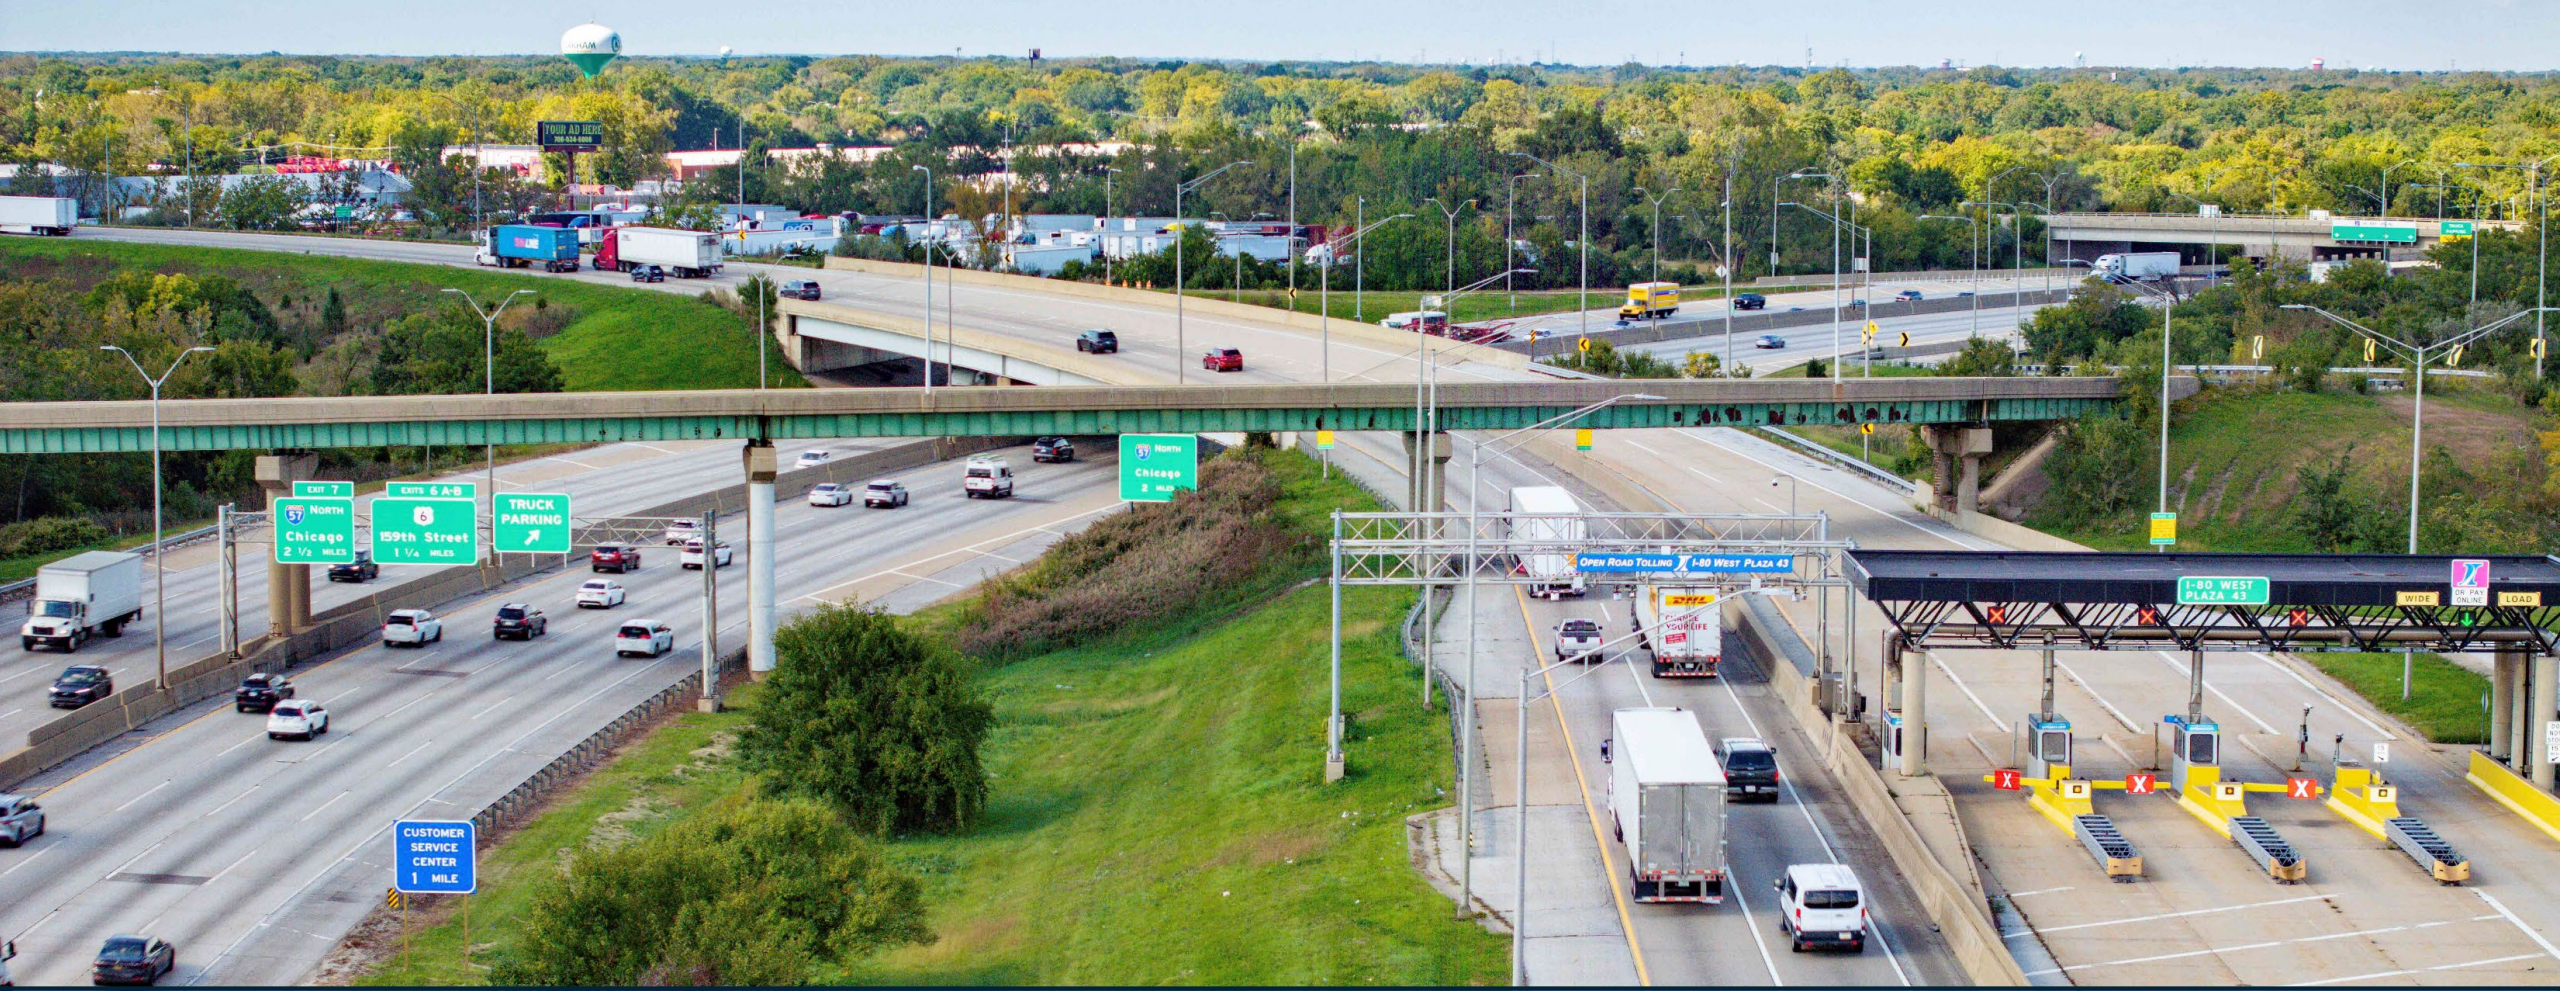
YOUR AD HERE
EXIT 7
NORTH
Chicago
2 ½ MILES
EXITS 6A-B
6
159th Street
1 ¼ MILES
TRUCK PARKING
CUSTOMER SERVICE CENTER
1 MILE
NORTH
Chicago
2 MILES
OPEN ROAD TOLLING
I-80 WEST PLAZA 43
I-80 WEST PLAZA 43
WIDE
LOAD

THANK YOU

Optional Pre-Proposal Meeting: Professional Services Bulletin 26-4 (In-Person or Virtual Option)

Name	Role	Registration First Name	Registration Last Name	Registration Email	Registration Status	Job Title	Organization	Phone Number
Williams, Cynthia	Organizer							
Hall, Danna	Organizer							
Banda, Vincent	Organizer							
Campuzano, Maria	Organizer							
Dami (Unverified)	Attendee	Damilola	Ajao	dajao@sdiengr.com	Registered	Operations	SDI ENGR Corp	3125519780
Dami (External)	Attendee	Olufemi	Oladeinde	ooladeinde@sdiengr.com	Registered	Principal Engineer	SDI ENGR Corp.	3125519780
Valentino, Michael	Presenter							
Barb Miller (External)	Attendee	Barb	Miller	bmiller@jaipc.com	Registered	Admin. Assistant	Juneau Associates, Inc., P.C.	618-877-1400
Jacob Bauer (External)	Attendee	Jacob	Bauer	jbauer@v3co.com	Registered	Project Manager	V3 Companies	8478408815
Michael Mendez (External)	Attendee	Michael	Mendez	mmendez@ihccbusiness.net	Registered	Director	Illinois Hispanic Chamber of Commerce	3124259500
Janet Wackrow (External)	Attendee	Janet	Wackrow	jwackrow@rmchin.com	Registered	Marketing Manager	R.M. Chin & Associates, Inc.	3125952000
Mondel, Jim	Attendee	Jim	Mondel	jmondel@getipass.com	Registered	Senior Contract Negotiator	Illinois Tollway CA	3316310562
MOLLER Jason	Attendee	Jason	Moller	jason.moller@egis-group.com	Registered	National Transportation Planning Practice Leader	Egis	8478945396
'+13316310562	Attendee							
Sarah Nguyen (Unverified)	Attendee	Sarah	Nguyen	snguyen@apexconsults.com	Registered	Marketing Coordinator	APEX Consulting Engineers, LLC	2624225128
Karl Wilson (External)	Attendee	Karl	Wilson	kwilson@bravocoeng.com	Registered	VP	BRAVO	8476364456
Samuel Wagner (External)	Attendee	Samuel	Wagner	swagner@osehinc.com	Registered	Marketing Coordinator	OSEH Inc.	9202685328
Harrington, Jennifer (External)	Attendee	Jennifer	Harrington	jharrington@f-w.com	Registered	Marketing Manager	Farnsworth Group, Inc.	3096638435
Galvin, Katie (External)	Attendee	Katie	Galvin	katie.galvin@aus.com	Registered	Senior Account Executive	Adesta LLC	3124931996
Malik Mattison (External)	Attendee	Malik	Mattison	mmattison@civiltechinc.com	Registered	Proposal Manager	Civiltech Engineering, Inc.	6307353582
Madison Halsne (External)	Attendee	Madison	Halsne	mhalsne@osehinc.com	Registered	Marketing Manager	OSEH Inc.	3303282337
Tiffany Chen (External)	Attendee	Tiffany	Chen	tchen@lineng.com	Registered	Technical Specialist	Lin Engineering	6303235168
Katie Self (External)	Attendee	Katie	Self	kself@descotoinc.com	Registered	Sr Marketing Proposal Specialist	d'Escoto, Inc.	773-255-1074
Edward Andrews (External)	Attendee	Edward	Andrews	edwarda@chamlin.com	Registered	Sr Project Manager	Chamlin & Associates	(815) 223-3344
Brian Pawula (External)	Attendee	Brian	Pawula	blpawula@hornershifrin.com	Registered	Associate, Regional Manager of Transportation	Horner & Shifrin, Inc.	8479226125
Arthur Nowak (External)	Attendee	Arthur	Nowak	anowak@infrastructure-eng.com	Registered	Chief Structural Engineer	IEI	8479870010
Jeffrey Ehrhart (External)	Attendee	Jeffrey	Ehrhart	jehrhart@ardmoreroderick.com	Registered	Associate Vice President	Ardmore Roderick	3127951400
Olufemi Oladeinde (External)	Attendee	Olufemi	Oladeinde	ooladeinde@sdiengr.com	Registered	Principal Engineer	SDI ENGR Corp.	3125519780
Tina Ballin (External)	Attendee	Tina	Ballin	tballin@gocos.net	Registered	Marketing Admin Manager	Gonzalez Companies, LLC	6306328462
Anita States (External)	Attendee	Anita	States	anita.states@peralte-clark.com	Registered	Marketing Coordinator	Peralte-Clark	847-466-6405
Krista Thoennes (External)	Attendee	Krista	Thoennes	kthoennes@infrastructure-eng.com	Registered	Marketing Manager	Infrastructure Engineering Inc.	312-960-1253
Clarisa Krafft (External)	Attendee	Clarisa	Krafft	ckrafft@gsg-consultants.com	Registered	Senior Marketing Coordinator	GSG Consultants, Inc.	630-994-2652
Krok, Marcin	Attendee	Marcin	Krok	marcin.krok@rsandh.com	Registered	Deputy National Discipline Leader, Bridge	RS&H	8477075993
Kelly, Sherita	Attendee	Sherita	Kelly	skelly@getipass.com	Registered	Senior Contract Negotiator	Illinois Tollway	16302416800
Scott Cain (External)	Attendee	Scott	Cain	scain@aegroupltd.com	Registered	Vice President of Transportation	Atlas Engineering Group	8472262271
Jason Martin	Attendee	Jason	Martin	jmartin@se3.us	Registered	Vice President	SE3, LLC	6306419900
Kyle Hildebrand (External)	Attendee	Kyle	Hildebrand	kyle.hildebrand@vivacitygroup.com	Registered	CRO	eX2 Technology	4028177873
Stephen Lynch (External)	Attendee	Stephen	Lynch	slynch@cerasolutions.com	Registered	Director of Operations	CERA Solutions	7089828225
LaWanda Jones (External)	Attendee	LaWanda	Jones	ljones@abnacorp.com	Registered	VP BD	ABNA	773888147
John DeRubeis (External)	Attendee	John	DeRubeis	john.derubeis@strataearth.com	Registered	Drilling Manager	Strata Earth Services	8477366199
Duane O'Laughlin (External)	Attendee	Duane	O'Laughlin	dolaughlin@ciorba.com	Registered	Chief Operating Officer	Ciorba Group	7736128157
Helander, Erin (External)	Attendee	Erin	Helander	ehelander@burnsmcd.com	Registered	Marketing Strategist	Burns & McDonnell	7085251662
Catherine Carpenter (External)	Attendee	Catherine	Carpenter	catherine.carpenter@oneatlas.com	Registered	Marketing Manager	Atlas Technical Consultants LLC	7738419912
Adenike Fasanya-Osilaja (External)	Attendee	Adenike	Fasanya-Osilaja	afosilaja@abnacorp.com	Registered	Business Development Specialist	ABNA Engineering of Illinois	7082570092
Vince DelMedico (External)	Attendee	Vincent	Del Medico	vdelmedico@v3co.com	Registered	Transportation Group Leader	V3 Companies, Ltd	7734568531
Kiernan Schock	Attendee	Kiernan	Schock	kiernan.schock@gec-group.com	Registered	Pursuit Manager	Globetrotters Engineering Corporation	8477328919
Ahmad Issa (External)	Attendee	Ahmad	Issa	ahmad.issa@hbmeng.com	Registered	Marketing	HBM Engineering Group, LLC	6308739392
Aleksandra Tadic (External)	Attendee	Aleksandra	Tadic	atadic@srfconsulting.com	Registered	Director and Office Lead	SRF Consulting Group	773-420-6695
Maria Godoy (External)	Attendee	Javier	Romero	jromero@rme-i.com	Registered	Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)	3128706607
Julia Puzio	Attendee	Julia	Puzio	julia.puzio@mottmac.com	Registered	Proposal Coordinator	Mott MacDonald	8622361172
Javier Romero (External)	Attendee	Javier	Romero	jromero@rme-i.com	Registered	Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)	3128706607
Gordon Snyder (External)	Attendee	gordon	snyder	gsnyder@rmchin.com	Registered	Director of Transportation	RM Chin	6305337041
Balka, Katie	Attendee	Katie	Balka	katie.balka@kimley-horn.com	Registered	Marketing Coordinator	Kimley-Horn and Associates, Inc.	'+1 331-234-9579
Kelli Hoeppner (External)	Attendee	Kelli	Hoeppner	khoeppner@abnacorp.com	Registered	Marketing Coordinator	ABNA Engineering	6309652949
Curtis Cornwell (External)	Attendee	Curtis	Cornwell	curtisc@thomas-engineering.com	Registered	Transportation Department Head	Thomas Engineering Group	7732517938
Daniela Salinas (External)	Attendee	Daniela	Salinas	dsalinas@hohgroup.com	Registered	Marketing	The HOH Group, Inc.	6306773733
'+16305337041 (External)	Attendee							
Lauren du Toit	Attendee	Lauren	du Toit	ldutoit@efkmoen.com	Registered	Proposal Coordinator	EFK Moen	3143943105
Liakopoulos, Stephanie (External)	Attendee	Mary Lou	Kutska	marylou.kutska@mbakerintl.com	Registered	Structural Department Manager	Michael Baker International	8475024732
Stacie Dovalovsky (External)	Attendee	Stacie	Dovalovsky	sdovalovsky@primeraeng.com	Registered	Transportation Division Manager	Primera Engineers, Ltd	2177786421
Emma Foley (External)	Attendee	Emma	Foley	efoley@descotoinc.com	Registered	Proposal Specialist	d'Escoto, Inc.	312-640-2811
Johnston, Peter (External)	Attendee	Peter	Johnston	peter.johnston@graef-usa.com	Registered	Principal	GRAEF USA Inc.	312-420-6078
Jason Schneider (External)	Attendee	Jason	Schneider	jschneider@collinsengr.com	Registered	SVP - Regional Manager	Collins Engineers, Inc.	3212365953
April Mendez (External)	Attendee	April	Mendez	amendez@greenprintpartners.com	Registered	CEO	Greenprint Partners	7739835256
Rao Doppalapudi (Unverified)	Attendee							

Perla Castro (External)	Attendee	Perla	Castro	perla@alpha-pm.com	Registered	CEO	Alpha PM	7738753750
Tom Gill (External)	Attendee	Thomas	Gill	tomg@thomas-engineering.com	Registered	President	Thomas Engineering Group, LLC	7085331700
Adholekar, Stefany	Attendee	Stefany	Adholekar	stefany.adholekar@atkinsrealis.com	Registered	Proposal Manager II	AtkinsRéalis	562.340.0700
Hayat A. Issa (External)	Attendee	Hayat	Issa	hayat.issa@hbmeng.com	Registered	President	HBM Engineering Group LLC	6308544707
Perez, Lorena	Attendee							
Omar Alsharbini	Attendee	Omar	Alsharbini	oalsharbini@alsharbinieng.com	Registered	President	Alsharbini Engineering Group, PLLC	7085430629
Pieniazek, Dave (External)	Attendee	Dave	Pieniazek	dave.pieniazek@stantec.com	Registered	Transportation Manager	Stantec	3122622245
Jose Delgado (External)	Attendee	Jose	Delgado	j.delgado@pinpointpe.com	Registered	Transportation PM	Pinpoint Precision Engineering	512-776-5591
Ruelle, Michael	Attendee	Michael	Ruelle	michael.ruelle@kimley-horn.com	Registered	Vice President	Kimley-Horn	3125904078
Christopher Snyder (External)	Attendee	Christopher	Snyder	ccsnyder@gftinc.com	Registered	Principal Project Manager	GFT	630-881-0656
Aislinn Fleming (External)	Attendee	Aislinn	Fleming	aifleming@gftinc.com	Registered	Proposal Manager	GFT Infrastructure, Inc.	3128947125
		Danna	Hall	dhall@getipass.com	Registered	Manager	Tollway	3319985448
		Ashley	Squitieri Kuffel	akuffel@geconsultllc.com	Registered	Business Development Director	Gasperec Elberts Consulting	6305233845
		Megan	Elberts	melberts@geconsultllc.com	Registered	Principal	Gasperec Elberts Consulting, LLC	847.868.1833
		Jarrod	CEBULSKI	jarrod.cebulski@rina.org	Registered	Director of Transportation Planning	RINA (Patrick Engineering)	6307957468
		Zaida	Morillo	zmorillo@v3co.com	Registered	Vice President	V3 Companies	(407) 925-4740
		Paola	Fonseca	pfonseca@v3co.com	Registered	Senior Marketing Coordinator	V3 Companies	6304783162
		Sudhakar Rao	Doppalapudi	dsrao@interraservices.com	Registered	Principal Engineer	Interra, Inc.	630-754-8700
		Rafael	Herrera	rherrera@se3.us	Registered	Vice President	SE3, LLC	630-880-8155
		Amanda	Baker	abaker@valdeseng.com	Registered	Municipal Proposal Coordinator	Valdes Architecture & Engineering	6307921886 ex1130
		Jeff	Stanko	jeff.stanko@hrgreen.com	Registered	Sr. Project Manager	HR Green, Inc.	630-354-7503
		Brian	Umbright	brian.umbright@exp.com	Registered	Vice President, Transportation	EXP	312-218-6714
		Dan	Tiltges	tiltgesd@msl-corp.com	Registered	President	Material Solutions Laboratory Corporation	8474049253
		John E.	Naughton III, P.E.	jnaughton@valdeseng.com	Registered	Director of Transportation	Valdes Architecture & Engineering	6304269898
		Benjamin	Zeman	benjamin.zeman@hdrinc.com	Registered	Project Manager	HDR	773-217-2093
		AJ	Jimenez	aj.jimenez@meadhunt.com	Registered	Client Manager	Mead & Hunt, Inc	3124047179
		Kelsey	Kidd	kelsey.kidd@exodigo.ai	Registered	Business Development	Exodigo	6306777887
		Alexander	Karahalios	akarahalios@getipass.com	Registered	Business Analyst of Diversity and Strategic Development	Illinois Tollway	6302416800
		David	Wilkinson	dwilkinson@swe-solutions.com	Registered	Principal	SWE Solutions	3125470960
		zhang	chen	askengservice@gmail.com	Registered	President	ASK Engineering	3125196614
		Joy	Schaad	jschaad@lse-eng.com	Registered	Sr. Project Manager	Lakeshore Engineering, LLC	7732308888
		Disha	Katwala	dkatwala@projecthuddlellc.com	Registered	CEO	Projecthuddle LLC	6304500886
		Ann	Seagrave	aseagrave@getipass.com	Registered	Contract Analyst	Illinois Tollway	630-743-8214
		Jorge	Galvan	jgalvan@getipass.com	Registered	Contract Analyst	TollWay	3313993495
		Valerie	Prohammer	vprohammer@getipass.com	Registered	Contract Specialist	ISTHA	331.399.3498
		Laura	Drozd	ldrozd@getipass.com	Registered	Contract Analyst	ISHTA	630-796-8652
		Takesha	Spencer	tspencer@getipass.com	Registered	Contract Analyst	Tollway	630-895-0878
		Vincent	Banda	vbanda@getipass.com	Registered	Senior Contract Admin	ISTHA	331-260-2194
		Joseph	Washington	joewashington100@gmail.com	Registered	Managing Member	PMO ERP Data	3129298640
		Fred	Lin	flin@lineng.com	Registered	President	Lin Engineering, Ltd.	6303235168
		Mohsen	Farahany	mfarahany@rme-i.com	Registered	Principal	RME	312-927-0994
		Natalia	Homedi	nhomedi@aegroupltd.com	Registered	President	Atlas Engineering Group, Ltd.	6303991052
		Kelly	Kolpak	kkolpak@hrgreen.com	Registered	Pursuit Specialist	HR Green	630-708-5054
		Nihar	Shah	nshah@rme-i.com	Registered	President	RME (Rubinos & Mesia Engineers, Inc.)	3128706600
		Patrick	Hodina	phodina@rme-i.com	Registered	Project Engineer	RME (Rubinos & Mesia Engineers, Inc.)	3128706600
		Dipak S	Shah	dshah@rme-i.com	Registered	Executive Vice President	RME (Rubinos & Mesia Engineers, Inc.)	3128706600
		Cheryl	Durante	cheryl.durante@terracon.com	Registered	Senior Client Development Specialist	Terracon Consultants, Inc.	630-814-9597
		Angela	Barak	abarak@getipass.com	Registered	Tollway PMO- Diversity	Illinois Tollway PMO	3127528161
		Akiwumi	Attawia	aattawia@osehinc.com	Registered	President	OSEH Inc.	3127762155
		Greg	Osborne	gosborne@epsteinglobal.com	Registered	Senior Project Manager	Epstein	3123308414
		William	Whitaker	wwhitaker@apexconsults.com	Registered	Vice President, Business Development	APEX Consulting Engineers	7084950044
		EG	Hessenthaler	ehessenthaler@gftinc.com	Registered	Manager - Construction Services	GFT Infrastructure, Inc.	3126176057
		Reid	Magner	rmagner@bravocoeng.com	Registered	Dir. of Design Services	Bravo Comapny Engineering	2242396346
		Julia	Garibay	julia7087333248@gmail.com	Canceled	DBE Program Manager	Illinois Tollway	7087333248
		Kathy	MacIntosh	kmacintosh@horizonworksgroup.com	Registered	VP of Business Development	HorizonWorks	6307959751
		Julia	Garibay	jgaribay@getipass.com	Registered	DBE Program Manager	Illinois Tollway	7087333248
		Gregory (Greg)	Brumm	gbrumm@dlz.com	Registered	President	DLZ Illinois, Inc.	6307451464
		Duana	Love	duana.love@contactppm.com	Registered	Vice President	Premier Project Management	708-220-9456
		Scott	VanDerAa	svanderaa@cerasolutions.com	Registered	Senior Project Manager	CERA Solutions	331-645-3948
		Corina	Farez	corina.farez@terracon.com	Registered	Principal	Terracon	6309950325
		Andri	Kurnia	andri.kurnia@terracon.com	Registered	Senior Engineer	Terracon	6308497120
		Kevin	Siksta	ksiksta@swe-solutions.com	Registered	Director of Transportation	SWE Solutions	815-258-6357
		Anna	Duff	aduff@collinsengr.com	Registered	Marketing Proposal Coordinator II	Collins Engineers, Inc.	3122367003
		Matt	Villanueva	mvillanueva@primeraeng.com	Registered	Sr. Roadway Group Manager	Primera Engineers	3122426379
		Ryan	Delves	delvesryan@stanleygroup.com	Registered	Transportation Department Manager	Stanley Consultants Inc.	7734445956
		Ryan	Smith	ryan.smith@strand.com	Registered	Project Manager	Strand Associates, Inc.	8157444200
		Joseph	Kozial	jkozial@bravocoeng.com	Registered	President	Bravo Company Engineering, Inc	6307029855
		Trent	Bruns	tbruns@bravocoeng.com	Registered	Engineer	Bravo Company Engineering	6307771340

		Lynn	Kessen	lynn.kessen@parsons.com	Registered	Capture Manager / Midwest Infrastructure	Parsons	312-930-0037
		Hamed	Mohammed	hmohammed@americanengconsultants.com	Registered	President	American Engineering Consultants, Inc	7737752050
		Adam	Woods	adam.woods@mbakerintl.com	Registered	Department Manager - Highways	Michael Baker International	6302538212
		Hemal	Patel	hemal.patel@10-4eng.com	Registered	President	10-4 Engineering, PLLC	6304403561
		Harvind	Singh	hsingh@singhinc.com	Registered	President/CEO	SINGH + Associates, Inc.	3126290240
		David	Pellizzari	dpellizzari@f-w.com	Registered	NE Illinois Transportation Manager	Farnsworth Group	708 310 9178
		Jennifer	Jones	jijones@dlz.com	Registered	Traffic Engineer	DLZ, Inc.	773-864-4835
		Robert	Brzezon	rbrzezon@efkmoen.com	Registered	Northern Illinois Regional Manager	EFK Moen, LLC	3123964065
		Arielle	Malinowski	arielle.malinowski@rsandh.com	Registered	AVP, Illinois State Leader	RS&H, Inc.	630-788-8065
		John	Yonan	jyonan@collinsengr.com	Registered	Vice President	Collins Engineers, Inc.	312/236-5119
		Lisa	Gasperec	lgasperec@geconsulttllc.com	Registered	Principal	Gasperec Elberts Consulting, LLC	847.417.4221
		Vinod	Patel	vinod.patel@10-4eng.com	Registered	Director of Engineering	10-4 Engineering, PLLC	6304403562
		Gary	Powell	gary.powell@10-4eng.com	Registered	Principal / Structural Manager	10-4 Engineering, PLLC	847-506-1986
		John	Lukowski	jlukowski@burnsmcd.com	Registered	Sr. Project Manager	Burns & McDonnell Engineering Co., Inc.	331-481-2932
		James	Robinson	jirobinson@burnsmcd.com	Registered	Operations Manager	Burns & McDonnell	6303732904
		Liviu	Iordache	liviu.iordache@terracon.com	Registered	Principal / Department Manager III	Terracon Consultants	630 786-6222
		Jennifer Allen (Jenny)	Post	japost@burnsmcd.com	Registered	Roadway Section Manager	Burns & McDonnell	630-485-1713
		Rami	Asfahani	rasfahani@f-w.com	Registered	Chicago Bridge Team Lead	Farnsworth Group	(815) 250-9383
		Ahmad	Alrousan	aalrousan4h@email.phoenix.edu	Registered	Resident Engineer	4HD INC	6302027891
		Raspal	Bajwa	rbajwa@infrastructure-eng.com	Registered	Project Manager	Infrastructure Engineering, Inc.	3129601243
		Ted	Lachus	tlachus@gocos.net	Registered	Regional Manager	Gonzalez Companies LLC	312-972-9770
		Stephanie	Liakopoulos	stephanie.liakopoulo@mbakerintl.com	Registered	Business Developer	Michael Baker International	3126603085
		Greg	Stukel	gstukel@bowman.com	Registered	Principal	Bowman	6307866733
		Tim	Seibt	tseibt@nstengr.com	Registered	Business Development Manager	NASHnal Soil Testing, LLC	331-454-8167
		Siri	Hibbler	siri@ilboc.org	Registered	CEO and Founder	Illinois Black Chamber of Commerce Inc	7735716445
		Colleen	Miller	cmiller@singhinc.com	Registered	Chief Business Development Officer	SINGH + Associates, Inc.	708.522.2686
		Dan	Filice	dfilice@singhinc.com	Registered	Director of Engineering	SINGH + Associates, Inc.	630.450.7581
		Thomas	Ngo	tngo@millennia.pro	Registered	President	Millennia Professional Services	6307812107
		Jon	Vana	jvana@civiltechinc.com	Registered	President	Civiltech	6307353382
		Ahsan	Siddiqi	ahsan.siddiqi@amesengineeringinc.com	Registered	President	AMES Engineering,Inc	6307371987
		Sam	Mittal	sam.mittal@mottmac.com	Registered	Principal Project Manager	Mott MacDonald	'+13128945367
		Gabriela	Garcia	gabi@indepchi.com	Registered	IHCCTA	INDEP Chicago	7738143636
		Nicole	Rose	nicole@pmcsconsulting.com	Registered	Senior Project Controls Manager	PMCS	7084768194
		Jeff	Reckamp	jreckamp@f-w.com	Registered	Sr Telecom Program Manager	Farnsworth Group	6306511007
		Beth	Tatro	btatro@rmchin.com	Registered	VP Marketing & Communications	CHIN	6303069469
		Andrew	Keaschall	akeaschall@benesch.com	Registered	Sr. Vice President	Benesch	773-896-8564
		John	Nelson	jnelson@hanson-inc.com	Registered	Vice President	Hanson Professional Services Inc.	630-673-1795
		Jake	Weaver	jweaver@parametrix.com	Registered	Sr. Program Manager	Parametrix	5174886027
		Mitesh	Deshpande	mdeshpande@abnacorp.com	Registered	Chief Operating Officer	ABNA	7738827693
		Robert	Bohnak	rbohnak@abnacorp.com	Registered	Senior Project Manager	ABNA Corp.	7082147518
		Amy	Frankowski	amy.frankowski@exp.com	Registered	Marketing Manager	EXP	6303732784
		Mohammed	Rashed	mrashed@dbsterlin.com	Registered	Director of Electrical Operations	DB Sterlin	7735520517
		Dan	Drew	daniel.drew@tylin.com	Registered	VP-Area/Sector Manager	TYLin	3129525340
		Vanessa	Ramos	vramos@getipass.com	Registered	Senior Contract Negotiator	Illinois Tolway	6304327737
		Melissa	McGhee	mmcghee@cbbel.com	Registered	Asst. Department Head, Phase II Engineering	Christopher B Burke Engineering	8478230500
		Torres	Ratcliff	tratcliff@kdmengineering.com	Registered	Design Manager	KDM Engineering	773-908-7619
		Kevin	Swan	kswan@kdmengineering.com	Registered	VP of Strategic Partnerships	KDM Engineering, LLC	3127632198
		Sara	Knight	sara.knight@strataearth.com	Registered	President	Strata Earth Services, LLC	8474899175
		Michael	Ross	mross@kdmengineering.com	Registered	Distribution Engineering Manager	KDM Engineering	8479750315
		Moussa	Issa	moussa.issa@hbmeng.com	Registered	Chief Engineer	HBM Engineering Group	708-717-4836
		Ken	Smorynski	ksmorynski@infrastructure-eng.com	Registered	Vice President	Infrastructure Engineering, Inc.	312-960-1260
		Josh	Lutzow	josh.lutzow@egis-group.com	Registered	Pursuit Manager	Egis USA	801-713-5249
		Ali	Ahsan	ali.ahsan@amesengineeringinc.com	Registered	Director, Business Development & Operations	Ames Engineering Inc	6304141927
		Chris	Prosperi	chris-prosperi@peralte-clark.com	Registered	Phase II Lead	Perlate-Clark	847-220-4884

PRE-SUBMISSION CONFERENCE SIGN-IN

Bid Description: PSB 26-4 Professional Services Bulletin

BidBuy Number: 27-557THA-ENGCO-B-54477 Solicitation Publication Date: Oct 8, 2026 Due Date: Oct 30, 2026

Vendor Conference Date & Time: October 15, 2026 3:15PM Conference Location: Marriott Chicago-Naperville 1801 N. Naper Blvd. Naperville, IL 60563

Attendance is: Not Mandatory

ATTENDEES

PLEASE PRINT CLEARLY

	NAME AND TITLE	COMPANY REPRESENTED	TELEPHONE	EMAIL ADDRESS
1.	Ali Ahsan Director, Business Dev	AMES Engineering INC	6304141927	Ali.Ahsan@amesengineering.c
2.	Ty Gilligan	HNTB (PMC)	630-453-9341	tgilligan@hntb.com
3.	ORHAN ULGER	MaC Kay	6303622583	oulger@2imgroup
4.	ADNAN HASHMI	JACOBS	571-612-0385	adnan.hashmi@jacobs.com
5.	Trevor Kluesel	Bereech	312-315-4033	tkluesel@bereech.com
6.	Tiffany Merrill, Senior Contract Neg. IL Tollway			TMerrill@getipass.com
7.				
8.				
9.				
10.				
11.				
12.				
13.				

PRE-SUBMISSION CONFERENCE SIGN-IN

Bid Description: PSB 26-4 Professional Services Bulletin

BidBuy Number: 27-557THA-ENGCO-B-54477 Solicitation Publication Date: Oct 8, 2026 Due Date: Oct 30, 2026

Vendor Conference Date & Time: October 15, 2026 3:15PM Conference Location: Marriott Chicago-Naperville 1801 N. Naper Blvd. Naperville, IL 60563

Attendance is: Not Mandatory

ATTENDEES

PLEASE PRINT CLEARLY

	NAME AND TITLE	COMPANY REPRESENTED	TELEPHONE	EMAIL ADDRESS
1.	Peter Stephenson	Innerdair LLC	847-554-8454	Peter.Stephenson@innerdair.com
2.	Marissa Modesto	V3 Companies	773-714-6342	mmodesto@v3co.com
3.	John O'Neill	BLA	224 217 7179	joneill@bla-inc.com
4.	Trudy Buehler	Mackie Consultants	847.818.1838	tbuehler@mackieconsult.com
5.	Arif Shaikh	Arora and Associates	312 221 5141	ashaikh@aroraae.com
6.	Zubair Haider	Baxter & Woodman	847-778-6466	zhaider@baxterwoodman.com
7.	Mike Ring	Terra Engineering	312 6083192	mring@terraengineering.com
8.	Jim Mayer	Hntb Corp	312-402-0984	jmayer@hntb.com
9.	Nicole Nutter	PMCS	708-227-6469	nikie@pmcsconsulting.com
10.				
11.				
12.				
13.				

PRE-SUBMISSION CONFERENCE SIGN-IN

Bid Description: PSB 26-4 Professional Services Bulletin

BidBuy Number: 27-557THA-ENGCO-B-54477 | Solicitation Publication Date: Oct 8, 2026 | Due Date: Oct 30, 2026

Vendor Conference Date & Time: October 15, 2026 3:15PM | Conference Location: Marriott Chicago-Naperville 1801 N. Naper Blvd. Naperville, IL 60563

Attendance is: Not Mandatory

ATTENDEES

PLEASE PRINT CLEARLY

	NAME AND TITLE	COMPANY REPRESENTED	TELEPHONE	EMAIL ADDRESS
1.	SHUJA KAZI CEO	DELTA ENGINEERING	312-291-6564	SHUJAK@DEG-AMERICA.com
2.	Rob Foster, Sr. PM	Akana	708-533-7111	robert.foster@akana.us
3.	Dan Bruchelmeyer, CEO	BLA	630-438-6400	dbruchelmeyer@bla-inc.com
4.	JEFF LANGE, DIRECTOR	CIVILTECH	630-735-3088	jlange@civiltechinc.com
5.	SAGAR SONAR, PM	KIMLEY-HORN	630-487-3469	sagar.sonar@kimley-horn.com
6.	RAYMOND KUMAPLEY	SE3	630-452-9202	rkumapley@se7.us
7.	Sis Killon	HDR	312-369-9259	Sis.Killon@hdr.com
8.	Jean-Pierre Ngoy, COO	AGANO ZURI	847 875-8860	Pierre@aganozuri.com
9.	Imtiaz A Rehman	ESG		Imtiaz@esgcorp.us
10.	Jose A. Delgado	Pinpoint Precision	312-776-5591	j.delgado@pinpointpe.com
11.	Ashley Kuffel	GEC	630-323-3845	akuffel@geconsultllc.com
12.				
13.				

PRE-SUBMISSION CONFERENCE SIGN-IN

Bid Description: PSB 26-4 Professional Services Bulletin

BidBuy Number: 27-557THA-ENGCO-B-54477 Solicitation Publication Date: Oct 8, 2026 Due Date: Oct 30, 2026

Vendor Conference Date & Time: October 15, 2026 3:15PM Conference Location: Marriott Chicago-Naperville 1801 N. Naper Blvd. Naperville, IL 60563

Attendance is: Not Mandatory

ATTENDEES

PLEASE PRINT CLEARLY

	NAME AND TITLE	COMPANY REPRESENTED	TELEPHONE	EMAIL ADDRESS
1.	Chris Prosperi	Peralta-Clark	847-220-4884	chris.prosperi@peralta-clark.com
2.	Kristen Bennett	IL Tollway	630 361 3233	KBennett@getpass.com
3.	Samina Saleem President	INNOVA	8477459353	ssaleem@innovacorp.com
4.	MICHAEL BROUCH COMSTR OP MNGR	BLA	630-742-4527	MBROUCH@BLA-INC.COM
5.	MICHAEL SCHUCH	MORREALE	708 2036784	MSCHUCH@MORREALECOMPANY.COM
6.	Jeffrey MacDonald	Gasparo Elbatt Consultants	909-907-2184	jmacdonald@gecconsultllc.com
7.	Clint Ferguson	GFT	317-698-3328	cferguson@gftinc.com
8.	Anna Dukes	Atlas Engineering Group	347 826-2135	adukes@aegroupltd.com
9.	Jamil Bou-Saab	TERRA Engineering	312-467-0123	jbousaab@terraengineering.com
10.	Renad Alrousan	4HD Inc	630-202-7892	ralrousan@4hdconsultants.com
11.	Omer A Rehman	GSG	630-745-1806	omer@esgcorp.us
12.	Michal BARTUSIEWICZ	EXP	312-616-3122	michal.bartusiewicz@exp.com
13.	THOMAS SANDERSON	AMERICAN SURVEY & ENG	312-277-2000	T.SANDERSON@AMERICANSURVEY.COM

V.20.1

PRE-SUBMISSION CONFERENCE SIGN-IN

	NAME AND TITLE	COMPANY REPRESENTED	TELEPHONE	EMAIL ADDRESS
14.	ANTHONY STANDISH, DIRECTOR OF TRANSPO	STRAND ASSOC.	815.744.4200	tony.standish@strael.com
15.				
16.				
17.				
18.				
19.				
20.				

STATE EMPLOYEES IN ATTENDANCE

1.	
2.	
3.	
4.	
5.	
6.	

Optional Pre-Proposal Meeting: Professional Services Bulletin 26-4

First Name	Last Name	Signature	Job Title	Organization
Stefany	Adholekar		Proposal Manager II	AtkinsRéalis
Damilola	Ajao		Operations	SDI ENGR Corp
Ahmad	Alrousan		Resident Engineer	4HD INC
Omar	Alsharbini		President	Alsharbini Engineering Group, PLLC
Edward	Andrews		Sr Project Manager	Chamlin & Associates
Rami	Asfahani	✓	Chicago Bridge Team Lead	Farnsworth Group
Akiwumi	Attawia	✓	President	OSEH Inc.
Raspal	Bajwa		Project Manager	Infrastructure Engineering, Inc.
Amanda	Baker		Municipal Proposal Coordinator	Valdes Architecture & Engineering
Katie	Balka		Marketing Coordinator	Kimley-Horn and Associates, Inc.
Tina	Ballin		Marketing Admin Manager	Gonzalez Companies, LLC
Vincent	Banda		Senior Contract Admin	ISTHA
Angela	Barak		Tollway PMO- Diversity	Illinois Tollway PMO
Jacob	Bauer	✓	Project Manager	V3 Companies
Robert	Bohnak	✓	Senior Project Manager	ABNA Corp.
Gregory(Greg)	Brumm		President	DLZ Illinois, Inc.
Trent	Bruns		Engineer	Bravo Company Engineering
Robert	Brzezon		Northern Illinois Regional Manager	EFK Moen, LLC
Scott	Cain		Vice President of Transportation	Atlas Engineering Group
Catherine	Carpenter		Marketing Manager	Atlas Technical Consultants LLC
Perla	Castro		CEO	Alpha PM
Jarrod	CEBULSKI	Jarrod Cebulski	Director of Transportation Planning	RINA (Patrick Engineering)
zhang	chen		President	ASK Engineering
Curtis	Cornwell		Transportation Department Head	Thomas Engineering Group
Vincent	Del Medico		Transportation Group Leader	V3 Companies, Ltd
Ryan	Delves		Transportation Department Manager	Stanley Consultants Inc.
Mitesh	Deshpande		Chief Operating Officer	ABNA
Sudhakar Rao	Doppalapudi		Principal Engineer	Interra, Inc.
Stacie	Dovalovsky		Transportation Division Manager	Primera Engineers, Ltd
Dan	Drew		VP-Area/Sector Manager	TYLin
Laura	Drozd		Contract Analyst	ISHTA
Lauren	du Toit		Proposal Coordinator	EFK Moen
Anna	Duff		Marketing Proposal Coordinator II	Collins Engineers, Inc.
Cheryl	Durante		Senior Client Development Specialist	Terracon Consultants, Inc.
Jeffrey	Ehrhart		Associate Vice President	Ardmore Roderick
Megan	Elberts		Principal	Gasperec Elberts Consulting, LLC
Mohsen	Farahany		Principal	RME
Corina	Farez		Principal	Terracon
Adenike	Fasanya-Osilaja		Business Development Specialist	ABNA Engineering of Illinois
Dan	Filice		Director of Engineering	SINGH + Associates, Inc.
Aislinn	Fleming		Proposal Manager	GFT Infrastructure, Inc.
Paola	Fonseca		Senior Marketing Coordinator	V3 Companies
Amy	Frankowski		Marketing Manager	EXP
Jorge	Galvan		Contract Analyst	TollWay

Optional Pre-Proposal Meeting: Professional Services Bulletin 26-4

First Name	Last Name	Signature	Job Title	Organization
Stefany	Adholekar		Proposal Manager II	AtkinsRéalis
Damilola	Ajao		Operations	SDI ENGR Corp
Ahmad	Alrousan		Resident Engineer	4HD INC
Omar	Alsharbini		President	Alsharbini Engineering Group, PLLC
Edward	Andrews		Sr Project Manager	Chamlin & Associates
Rami	Asfahani		Chicago Bridge Team Lead	Farnsworth Group
Akiwumi	Attawia		President	OSEH Inc.
Raspal	Bajwa	x RB	Project Manager	Infrastructure Engineering, Inc.
Amanda	Baker		Municipal Proposal Coordinator	Valdes Architecture & Engineering
Katie	Balka		Marketing Coordinator	Kimley-Horn and Associates, Inc.
Tina	Ballin		Marketing Admin Manager	Gonzalez Companies, LLC
Vincent	Banda		Senior Contract Admin	ISTHA
Angela	Barak		Tollway PMO- Diversity	Illinois Tollway PMO
Jacob	Bauer		Project Manager	V3 Companies
Robert	Bohnak		Senior Project Manager	ABNA Corp.
Gregory(Greg)	Brumm		President	DLZ Illinois, Inc.
Trent	Bruns		Engineer	Bravo Company Engineering
Robert	Brzezon		Northern Illinois Regional Manager	EFK Moen, LLC
Scott	Cain		Vice President of Transportation	Atlas Engineering Group
~~Catherine~~	~~Carpenter~~		Marketing Manager	Atlas Technical Consultants LLC
Perla	Castro		CEO	Alpha PM
Jarrod	CEBULSKI		Director of Transportation Planning	RINA (Patrick Engineering)
zhang	chen		President	ASK Engineering
Curtis	Cornwell		Transportation Department Head	Thomas Engineering Group
Vincent	Del Medico		Transportation Group Leader	V3 Companies, Ltd
Ryan	Delves	x RD.	Transportation Department Manager	Stanley Consultants Inc.
Mitesh	Deshpande		Chief Operating Officer	ABNA
Sudhakar Rao	Doppalapudi		Principal Engineer	Interra, Inc.
Stacie	Dovalovsky		Transportation Division Manager	Primera Engineers, Ltd
Dan	Drew		VP-Area/Sector Manager	TYLin
Laura	Drozd		Contract Analyst	ISHTA
Lauren	du Toit		Proposal Coordinator	EFK Moen
Anna	Duff		Marketing Proposal Coordinator II	Collins Engineers, Inc.
Cheryl	Durante		Senior Client Development Specialist	Terracon Consultants, Inc.
Jeffrey	Ehrhart		Associate Vice President	Ardmore Roderick
Megan	Elberts	x	Principal	Gasperec Elberts Consulting, LLC
Mohsen	Farahany		Principal	RME
Corina	Farez		Principal	Terracon
Adenike	Fasanya-Osilaja		Business Development Specialist	ABNA Engineering of Illinois
Dan	Filice	x	Director of Engineering	SINGH + Associates, Inc.
Aislinn	Fleming		Proposal Manager	GFT Infrastructure, Inc.
Paola	Fonseca		Senior Marketing Coordinator	V3 Companies
Amy	Frankowski		Marketing Manager	EXP
Jorge	Galvan		Contract Analyst	TollWay

Optional Pre-Proposal Meeting: Professional Services Bulletin 26-4

First Name	Last Name	Signature	Job Title	Organization
Stefany	Adholekar		Proposal Manager II	AtkinsRéalis
Damilola	Ajao		Operations	SDI ENGR Corp
Ahmad	Alrousan		Resident Engineer	4HD INC
Omar	Alsharbini		President	Alsharbini Engineering Group, PLLC
Edward	Andrews		Sr Project Manager	Chamlin & Associates
Rami	Asfahani		Chicago Bridge Team Lead	Farnsworth Group
Akiwumi	Attawia		President	OSEH Inc.
Raspal	Bajwa		Project Manager	Infrastructure Engineering, Inc.
Amanda	Baker		Municipal Proposal Coordinator	Valdes Architecture & Engineering
Katie	Balka		Marketing Coordinator	Kimley-Horn and Associates, Inc.
Tina	Ballin		Marketing Admin Manager	Gonzalez Companies, LLC
Vincent	Banda		Senior Contract Admin	ISTHA
Angela	Barak		Tollway PMO- Diversity	Illinois Tollway PMO
Jacob	Bauer		Project Manager	V3 Companies
Robert	Bohnak		Senior Project Manager	ABNA Corp.
Gregory(Greg)	Brumm		President	DLZ Illinois, Inc.
Trent	Bruns		Engineer	Bravo Company Engineering
Robert	Brzezon		Northern Illinois Regional Manager	EFK Moen, LLC
Scott	Cain		Vice President of Transportation	Atlas Engineering Group
Catherine	Carpenter		Marketing Manager	Atlas Technical Consultants LLC
Perla	Castro		CEO	Alpha PM
Jarrod	CEBULSKI		Director of Transportation Planning	RINA (Patrick Engineering)
zhang	chen		President	ASK Engineering
Curtis	Cornwell		Transportation Department Head	Thomas Engineering Group
Vincent	Del Medico		Transportation Group Leader	V3 Companies, Ltd
Ryan	Delves		Transportation Department Manager	Stanley Consultants Inc.
Mitesh	Deshpande		Chief Operating Officer	ABNA
Sudhakar Rao	Doppalapudi		Principal Engineer	Interra, Inc.
Stacie	Dovalovsky		Transportation Division Manager	Primera Engineers, Ltd
Dan	Drew		VP-Area/Sector Manager	TYLin
Laura	Drozd		Contract Analyst	ISHTA
Lauren	du Toit		Proposal Coordinator	EFK Moen
Anna	Duff		Marketing Proposal Coordinator II	Collins Engineers, Inc.
Cheryl	Durante		Senior Client Development Specialist	Terracon Consultants, Inc.
Jeffrey	Ehrhart		Associate Vice President	Ardmore Roderick
Megan	Elberts		Principal	Gasperec Elberts Consulting, LLC
Mohsen	Farahany		Principal	RME
Corina	Farez		Principal	Terracon
Adenike	Fasanya-Osilaja		Business Development Specialist	ABNA Engineering of Illinois
Dan	Filice		Director of Engineering	SINGH + Associates, Inc.
Aislinn	Fleming		Proposal Manager	GFT Infrastructure, Inc.
Paola	Fonseca		Senior Marketing Coordinator	V3 Companies
Amy	Frankowski		Marketing Manager	EXP
Jorge	Galvan		Contract Analyst	TollWay

Optional Pre-Proposal Meeting: Professional Services Bulletin 26-4

First Name	Last Name	Signature	Job Title	Organization
Stefany	Adholekar		Proposal Manager II	AtkinsRéalis
Damilola	Ajao		Operations	SDI ENGR Corp
Ahmad	Alrousan		Resident Engineer	4HD INC
Omar	Alsharbini		President	Alsharbini Engineering Group, PLLC
Edward	Andrews		Sr Project Manager	Chamlin & Associates
Rami	Asfahani	—	Chicago Bridge Team Lead	Farnsworth Group
Akiwumi	Attawia		President	OSEH Inc.
Raspal	Bajwa		Project Manager	Infrastructure Engineering, Inc.
Amanda	Baker		Municipal Proposal Coordinator	Valdes Architecture & Engineering
Katie	Balka		Marketing Coordinator	Kimley-Horn and Associates, Inc.
Tina	Ballin		Marketing Admin Manager	Gonzalez Companies, LLC
Vincent	Banda		Senior Contract Admin	ISTHA
Angela	Barak		Tollway PMO- Diversity	Illinois Tollway PMO
Jacob	Bauer		Project Manager	V3 Companies
Robert	Bohnak		Senior Project Manager	ABNA Corp.
Gregory(Greg)	Brumm		President	DLZ Illinois, Inc.
Trent	Bruns		Engineer	Bravo Company Engineering
Robert	Brzezon		Northern Illinois Regional Manager	EFK Moen, LLC
Scott	Cain		Vice President of Transportation	Atlas Engineering Group
~~Catherine~~	~~Carpenter~~		Marketing Manager	Atlas Technical Consultants LLC
Perla	Castro		CEO	Alpha PM
Jarrod	CEBULSKI		Director of Transportation Planning	RINA (Patrick Engineering)
zhang	chen		President	ASK Engineering
Curtis	Cornwell		Transportation Department Head	Thomas Engineering Group
Vincent	Del Medico		Transportation Group Leader	V3 Companies, Ltd
Ryan	Delves		Transportation Department Manager	Stanley Consultants Inc.
Mitesh	Deshpande		Chief Operating Officer	ABNA
Sudhakar Rao	Doppalapudi		Principal Engineer	Interra, Inc.
Stacie	Dovalovsky		Transportation Division Manager	Primera Engineers, Ltd
Dan	Drew		VP-Area/Sector Manager	TYLin
Laura	Drozd		Contract Analyst	ISHTA
Lauren	du Toit	—	Proposal Coordinator	EFK Moen
Anna	Duff		Marketing Proposal Coordinator II	Collins Engineers, Inc.
Cheryl	Durante		Senior Client Development Specialist	Terracon Consultants, Inc.
Jeffrey	Ehrhart		Associate Vice President	Ardmore Roderick
Megan	Elberts		Principal	Gasperec Elberts Consulting, LLC
Mohsen	Farahany		Principal	RME
Corina	Farez		Principal	Terracon
Adenike	Fasanya-Osilaja		Business Development Specialist	ABNA Engineering of Illinois
Dan	Filice		Director of Engineering	SINGH + Associates, Inc.
Aislinn	Fleming		Proposal Manager	GFT Infrastructure, Inc.
Paola	Fonseca		Senior Marketing Coordinator	V3 Companies
Amy	Frankowski		Marketing Manager	EXP
Jorge	Galvan		Contract Analyst	TollWay

Katie	Galvin		Senior Account Executive	Adesta LLC
Gabriela	Garcia		IHCCTA	INDEP Chicago
Julia	Garibay		DBE Program Manager	Illinois Tollway
Julia	Garibay		DBE Program Manager	Illinois Tollway
Lisa	Gasperec		Principal	Gasperec Elberts Consulting, LLC
Thomas	Gill		President	Thomas Engineering Group, LLC
Danna	Hall		Manager	Tollway
Madison	Halsne		Marketing Manager	OSEH Inc.
Jennifer	Harrington		Marketing Manager	Farnsworth Group, Inc.
Erin	Helander		Marketing Strategist	Burns & McDonnell
Rafael	Herrera		Vice President	SE3, LLC
EG	Hessenthaler		Manager - Construction Services	GFT Infrastructure, Inc.
Siri	Hibbler		CEO and Founder	Illinois Black Chamber of Commerce Inc
Patrick	Hodina		Project Engineer	RME (Rubinos & Mesia Engineers, Inc.)
Natalia	Homedi		President	Atlas Engineering Group, Ltd.
Liviu	Iordache		Principal / Department Manager III	Terracon Consultants
Ahmad	Issa		Marketing	HBM Engineering Group, LLC
Moussa	Issa		Chief Engineer	HBM Engineering Group
Hayat	Issa		President	HBM Engineering Group LLC
AJ	Jimenez		Client Manager	Mead & Hunt, Inc
Peter	Johnston		Principal	GRAEF USA Inc.
Jennifer	Jones		Traffic Engineer	DLZ, Inc.
Alexander	Karahalios		Business Analyst of Diversity and Strategic Development	Illinois Tollway
~~Disha~~	~~Katwala~~		CEO	Projecthuddle LLC
Andrew	Keaschall	✓	Sr. Vice President	Benesch
Sherita	Kelly		Senior Contract Negotiator	Illinois Tollway
Lynn	Kessen		Capture Manager / Midwest Infrastructure	Parsons
Kelsey	Kidd		Business Development	Exodigo
Sara	Knight		President	Strata Earth Services, LLC
Kelly	Kolpak		Pursuit Specialist	HR Green
Joseph	Kozial		President	Bravo Company Engineering, Inc
Clarisa	Krafft		Senior Marketing Coordinator	GSG Consultants, Inc.
Marcin	Krok		Deputy National Discipline Leader, Bridge	RS&H
Andri	Kurnia		Senior Engineer	Terracon
Mary Lou	Kutska		Structural Department Manager	Michael Baker International
Ted	Lachus		Regional Manager	Gonzalez Companies LLC
Stephanie	Liakopoulos		Business Developer	Michael Baker International
Fred	Lin		President	Lin Engineering, Ltd.
Duana	Love		Vice President	Premier Project Management
John	Lukowski		Sr. Project Manager	Burns & McDonnell Engineering Co., Inc.
Stephen	Lynch		Director of Operations	CERA Solutions
Kathy	MacIntosh		VP of Business Development	HorizonWorks
Reid	Magner		Dir. of Design Services	Bravo Comapny Engineering
Arielle	Malinowski		AVP, Illinois State Leader	RS&H, Inc.
Jason	Martin		Vice President	SE3, LLC
Malik	Mattison		Proposal Manager	Civiltech Engineering, Inc.
Melissa	McGhee		Asst. Department Head, Phase II Engineering	Christopher B Burke Engineering
April	Mendez		CEO	Greenprint Partners

Katie	Galvin		Senior Account Executive	Adesta LLC
Gabriela	Garcia		IHCCTA	INDEP Chicago
Julia	Garibay		DBE Program Manager	Illinois Tollway
Julia	Garibay		DBE Program Manager	Illinois Tollway
Lisa	Gasperec		Principal	Gasperec Elberts Consulting, LLC
Thomas	Gill		President	Thomas Engineering Group, LLC
Danna	Hall		Manager	Tollway
Madison	Halsne		Marketing Manager	OSEH Inc.
Jennifer	Harrington		Marketing Manager	Farnsworth Group, Inc.
Erin	Helander		Marketing Strategist	Burns & McDonnell
Rafael	Herrera		Vice President	SE3, LLC
EG	Hessenthaler		Manager - Construction Services	GFT Infrastructure, Inc.
Siri	Hibbler		CEO and Founder	Illinois Black Chamber of Commerce Inc
Patrick	Hodina		Project Engineer	RME (Rubinos & Mesia Engineers, Inc.)
Natalia	Homedi		President	Atlas Engineering Group, Ltd.
Liviu	Iordache		Principal / Department Manager III	Terracon Consultants
Ahmad	Issa		Marketing	HBM Engineering Group, LLC
Moussa	Issa		Chief Engineer	HBM Engineering Group
Hayat	Issa		President	HBM Engineering Group LLC
AJ	Jimenez		Client Manager	Mead & Hunt, Inc
Peter	Johnston		Principal	GRAEF USA Inc.
Jennifer	Jones		Traffic Engineer	DLZ, Inc.
Alexander	Karahalios		Business Analyst of Diversity and Strategic Development	Illinois Tollway
Disha	Katwala		CEO	Projecthuddle LLC
Andrew	Keaschall		Sr. Vice President	Benesch
Sherita	Kelly		Senior Contract Negotiator	Illinois Tollway
Lynn	Kessen		Capture Manager / Midwest Infrastructure	Parsons
Kelsey	Kidd		Business Development	Exodigo
Sara	Knight		President	Strata Earth Services, LLC
Kelly	Kolpak		Pursuit Specialist	HR Green
Joseph	Kozial		President	Bravo Company Engineering, Inc
Clarisa	Krafft		Senior Marketing Coordinator	GSG Consultants, Inc.
Marcin	Krok		Deputy National Discipline Leader, Bridge	RS&H
Andri	Kurnia		Senior Engineer	Terracon
Mary Lou	Kutska		Structural Department Manager	Michael Baker International
Ted	Lachus		Regional Manager	Gonzalez Companies LLC
Stephanie	Liakopoulos		Business Developer	Michael Baker International
Fred	Lin		President	Lin Engineering, Ltd.
Duana	Love		Vice President	Premier Project Management
John	Lukowski		Sr. Project Manager	Burns & McDonnell Engineering Co., Inc.
Stephen	Lynch		Director of Operations	CERA Solutions
Kathy	MacIntosh		VP of Business Development	HorizonWorks
Reid	Magner		Dir. of Design Services	Bravo Comapny Engineering
Arielle	Malinowski		AVP, Illinois State Leader	RS&H, Inc.
Jason	Martin		Vice President	SE3, LLC
Malik	Mattison		Proposal Manager	Civiltech Engineering, Inc.
Melissa	McGhee		Asst. Department Head, Phase II Engineering	Christopher B Burke Engineering
April	Mendez		CEO	Greenprint Partners

Katie	Galvin		Senior Account Executive	Adesta LLC
Gabriela	Garcia		IHCCTA	INDEP Chicago
Julia	Garibay		DBE Program Manager	Illinois Tollway
Julia	Garibay		DBE Program Manager	Illinois Tollway
Lisa	Gasperec		Principal	Gasperec Elberts Consulting, LLC
Thomas	Gill		President	Thomas Engineering Group, LLC
Danna	Hall		Manager	Tollway
Madison	Halsne		Marketing Manager	OSEH Inc.
Jennifer	Harrington		Marketing Manager	Farnsworth Group, Inc.
Erin	Helander		Marketing Strategist	Burns & McDonnell
Rafael	Herrera		Vice President	SE3, LLC
EG	Hessenthaler		Manager - Construction Services	GFT Infrastructure, Inc.
Siri	Hibbler		CEO and Founder	Illinois Black Chamber of Commerce Inc
Patrick	Hodina		Project Engineer	RME (Rubinos & Mesia Engineers, Inc.)
Natalia	Homedi		President	Atlas Engineering Group, Ltd.
Liviu	Iordache		Principal / Department Manager III	Terracon Consultants
Ahmad	Issa		Marketing	HBM Engineering Group, LLC
Moussa	Issa		Chief Engineer	HBM Engineering Group
Hayat	Issa		President	HBM Engineering Group LLC
AJ	Jimenez		Client Manager	Mead & Hunt, Inc
Peter	Johnston		Principal	GRAEF USA Inc.
Jennifer	Jones		Traffic Engineer	DLZ, Inc.
Alexander	Karahalios		Business Analyst of Diversity and Strategic Development	Illinois Tollway
Disha	Katwala		CEO	Projecthuddle LLC
Andrew	Keaschall		Sr. Vice President	Benesch
Sherita	Kelly		Senior Contract Negotiator	Illinois Tollway
Lynn	Kessen		Capture Manager / Midwest Infrastructure	Parsons
Kelsey	Kidd		Business Development	Exodigo
Sara	Knight		President	Strata Earth Services, LLC
Kelly	Kolpak		Pursuit Specialist	HR Green
Joseph	Kozial		President	Bravo Company Engineering, Inc
Clarisa	Krafft		Senior Marketing Coordinator	GSG Consultants, Inc.
Marcin	Krok		Deputy National Discipline Leader, Bridge	RS&H
Andri	Kurnia		Senior Engineer	Terracon
Mary Lou	Kutska		Structural Department Manager	Michael Baker International
Ted	Lachus		Regional Manager	Gonzalez Companies LLC
Stephanie	Liakopoulos		Business Developer	Michael Baker International
Fred	Lin		President	Lin Engineering, Ltd.
Duana	Love		Vice President	Premier Project Management
John	Lukowski		Sr. Project Manager	Burns & McDonnell Engineering Co., Inc.
Stephen	Lynch		Director of Operations	CERA Solutions
Kathy	MacIntosh		VP of Business Development	HorizonWorks
Reid	Magner		Dir. of Design Services	Bravo Comapny Engineering
Arielle	Malinowski		AVP, Illinois State Leader	RS&H, Inc.
Jason	Martin		Vice President	SE3, LLC
Malik	Mattison		Proposal Manager	Civiltech Engineering, Inc.
Melissa	McGhee		Asst. Department Head, Phase II Engineering	Christopher B Burke Engineering
April	Mendez		CEO	Greenprint Partners

Katie	Galvin		Senior Account Executive	Adesta LLC
Gabriela	Garcia		IHCCTA	INDEP Chicago
Julia	Garibay		DBE Program Manager	Illinois Tollway
Julia	Garibay		DBE Program Manager	Illinois Tollway
Lisa	Gasperec		Principal	Gasperec Elberts Consulting, LLC
Thomas	Gill		President	Thomas Engineering Group, LLC
Danna	Hall		Manager	Tollway
Madison	Halsne		Marketing Manager	OSEH Inc.
Jennifer	Harrington		Marketing Manager	Farnsworth Group, Inc.
Erin	Helander		Marketing Strategist	Burns & McDonnell
Rafael	Herrera		Vice President	SE3, LLC
EG	Hessenthaler		Manager - Construction Services	GFT Infrastructure, Inc.
Siri	Hibbler		CEO and Founder	Illinois Black Chamber of Commerce Inc
Patrick	Hodina		Project Engineer	RME (Rubinos & Mesia Engineers, Inc.)
Natalia	Homedi		President	Atlas Engineering Group, Ltd.
Liviu	Iordache		Principal / Department Manager III	Terracon Consultants
Ahmad	Issa		Marketing	HBM Engineering Group, LLC
Moussa	Issa		Chief Engineer	HBM Engineering Group
Hayat	Issa		President	HBM Engineering Group LLC
AJ	Jimenez		Client Manager	Mead & Hunt, Inc
Peter	Johnston		Principal	GRAEF USA Inc.
Jennifer	Jones		Traffic Engineer	DLZ, Inc.
Alexander	Karahalios		Business Analyst of Diversity and Strategic Development	Illinois Tollway
Disha	Katwala		CEO	Projecthuddle LLC
Andrew	Keaschall		Sr. Vice President	Benesch
Sherita	Kelly		Senior Contract Negotiator	Illinois Tollway
Lynn	Kessen		Capture Manager / Midwest Infrastructure	Parsons
Kelsey	Kidd		Business Development	Exodigo
Sara	Knight		President	Strata Earth Services, LLC
Kelly	Kolpak		Pursuit Specialist	HR Green
Joseph	Kozial		President	Bravo Company Engineering, Inc
Clarisa	Krafft		Senior Marketing Coordinator	GSG Consultants, Inc.
Marcin	Krok		Deputy National Discipline Leader, Bridge	RS&H
Andri	Kurnia		Senior Engineer	Terracon
Mary Lou	Kutska		Structural Department Manager	Michael Baker International
Ted	Lachus		Regional Manager	Gonzalez Companies LLC
Stephanie	Liakopoulos		Business Developer	Michael Baker International
Fred	Lin		President	Lin Engineering, Ltd.
Duana	Love		Vice President	Premier Project Management
John	Lukowski		Sr. Project Manager	Burns & McDonnell Engineering Co., Inc.
Stephen	Lynch		Director of Operations	CERA Solutions
Kathy	MacIntosh		VP of Business Development	HorizonWorks
Reid	Magner		Dir. of Design Services	Bravo Comapny Engineering
Arielle	Malinowski		AVP, Illinois State Leader	RS&H, Inc.
Jason	Martin		Vice President	SE3, LLC
Malik	Mattison		Proposal Manager	Civiltech Engineering, Inc.
Melissa	McGhee		Asst. Department Head, Phase II Engineering	Christopher B Burke Engineering
April	Mendez		CEO	Greenprint Partners

Michael	Mendez		Director	Illinois Hispanic Chamber of Commerce
Colleen	Miller	✓	Chief Business Development Officer	SINGH + Associates, Inc.
Sam	Mittal		Principal Project Manager	Mott MacDonald
Hamed	Mohammed		President	American Engineering Consultants, Inc
Jim	Mondel		Senior Contract Negotiator	Illinois Tollway CA
Zaida	Morillo	✓	Vice President	V3 Companies
John E.	Naughton III, P.E.		Director of Transportation	Valdes Architecture & Engineering
John	Nelson	✓	Vice President	Hanson Professional Services Inc.
Thomas	Ngo	✓	President	Millennia Professional Services
Sarah	Nguyen		Marketing Coordinator	APEX Consulting Engineers, LLC
Duane	O'Laughlin		Chief Operating Officer	Ciorba Group
Olufemi	Oladeinde		Principal Engineer	SDI ENGR Corp.
Greg	Osborne		Senior Project Manager	Epstein
Hemal	Patel		President	10-4 Engineering, PLLC
Vinod	Patel		Director of Engineering	10-4 Engineering, PLLC
Brian	Pawula		Associate, Regional Manager of Transportation	Horner & Shifrin, Inc.
David	Pellizzari		NE Illinois Transportation Manager	Farnsworth Group
Dave	Pieniazek		Transportation Manager	Stantec
Jennifer Allen (Jenny)	Post		Roadway Section Manager	Burns & McDonnell
Gary	Powell		Principal / Structural Manager	10-4 Engineering, PLLC
Valerie	Prohammer		Contract Specialist	ISTHA
Julia	Puzio		Proposal Coordinator	Mott MacDonald
Vanessa	Ramos		Senior Contract Negotiator	Illinois Tolway
Mohammed	Rashed		Director of Electrical Operations	DB Sterlin
Torres	Ratcliff		Design Manager	KDM Engineering
Jeff	Reckamp		Sr Telecom Program Manager	Farnsworth Group
James	Robinson		Operations Manager	Burns & McDonnell
Javier	Romero		Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)
Nicole	Rose		Senior Project Controls Manager	PMCS
Michael	Ross		Distribution Engineering Manager	KDM Engineering
Michael	Ruelle		Vice President	Kimley-Horn
Daniela	Salinas		Marketing	The HOH Group, Inc.
Joy	Schaad		Sr. Project Manager	Lakeshore Engineering, LLC
Jason	Schneider		SVP - Regional Manager	Collins Engineers, Inc.
Kiernan	Schock		Pursuit Manager	Globetrotters Engineering Corporation
Ann	Seagrave		Contract Analyst	Illinois Tollway
Tim	Seibt		Business Development Manager	NASHnal Soil Testing, LLC
Nihar	Shah		President	RME (Rubinos & Mesia Engineers, Inc.)
Dipak S	Shah		Executive Vice President	RME (Rubinos & Mesia Engineers, Inc.)
Ahsan	Siddiqi		President	AMES Engineering,Inc
Kevin	Siksta		Director of Transportation	SWE Solutions
Harvind	Singh		President/CEO	SINGH + Associates, Inc.
Ryan	Smith		Project Manager	Strand Associates, Inc.
Christopher	Snyder		Principal Project Manager	GFT
gordon	snyder		Director of Transportation	RM Chin
Takesha	Spencer		Contract Analyst	Tollway
Ashley	Squitieri Kuffel		Business Development Director	Gasperec Elberts Consulting
Jeff	Stanko		Sr. Project Manager	HR Green, Inc.

Michael	Mendez		Director	Illinois Hispanic Chamber of Commerce
Colleen	Miller		Chief Business Development Officer	SINGH + Associates, Inc.
Sam	Mittal		Principal Project Manager	Mott MacDonald
Hamed	Mohammed		President	American Engineering Consultants, Inc
Jim	Mondel		Senior Contract Negotiator	Illinois Tollway CA
Zaida	Morillo		Vice President	V3 Companies
John E.	Naughton III, P.E.		Director of Transportation	Valdes Architecture & Engineering
John	Nelson		Vice President	Hanson Professional Services Inc.
Thomas	Ngo		President	Millennia Professional Services
Sarah	Nguyen		Marketing Coordinator	APEX Consulting Engineers, LLC
Duane	O'Laughlin		Chief Operating Officer	Ciorba Group
Olufemi	Oladeinde		Principal Engineer	SDI ENGR Corp.
Greg	Osborne		Senior Project Manager	Epstein
Hemal	Patel		President	10-4 Engineering, PLLC
Vinod	Patel		Director of Engineering	10-4 Engineering, PLLC
Brian	Pawula		Associate, Regional Manager of Transportation	Horner & Shifrin, Inc.
David	Pellizzari		NE Illinois Transportation Manager	Farnsworth Group
Dave	Pieniazek		Transportation Manager	Stantec
Jennifer Allen (Jenny)	Post		Roadway Section Manager	Burns & McDonnell
Gary	Powell	—	Principal / Structural Manager	10-4 Engineering, PLLC
Valerie	Prohammer		Contract Specialist	ISTHA
Julia	Puzio		Proposal Coordinator	Mott MacDonald
Vanessa	Ramos		Senior Contract Negotiator	Illinois Tolway
Mohammed	Rashed		Director of Electrical Operations	DB Sterlin
Torres	Ratcliff		Design Manager	KDM Engineering
Jeff	Reckamp		Sr Telecom Program Manager	Farnsworth Group
James	Robinson		Operations Manager	Burns & McDonnell
Javier	Romero		Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)
Nicole	Rose		Senior Project Controls Manager	PMCS
Michael	Ross		Distribution Engineering Manager	KDM Engineering
Michael	Ruelle		Vice President	Kimley-Horn
Daniela	Salinas		Marketing	The HOH Group, Inc.
Joy	Schaad		Sr. Project Manager	Lakeshore Engineering, LLC
Jason	Schneider		SVP - Regional Manager	Collins Engineers, Inc.
Kiernan	Schock		Pursuit Manager	Globetrotters Engineering Corporation
Ann	Seagrave		Contract Analyst	Illinois Tollway
Tim	Seibt		Business Development Manager	NASHnal Soil Testing, LLC
Nihar	Shah		President	RME (Rubinos & Mesia Engineers, Inc.)
Dipak S	Shah		Executive Vice President	RME (Rubinos & Mesia Engineers, Inc.)
Ahsan	Siddiqi		President	AMES Engineering,Inc
Kevin	Siksta		Director of Transportation	SWE Solutions
Harvind	Singh		President/CEO	SINGH + Associates, Inc.
Ryan	Smith		Project Manager	Strand Associates, Inc.
Christopher	Snyder		Principal Project Manager	GFT
gordon	snyder		Director of Transportation	RM Chin
Takesha	Spencer	—	Contract Analyst	Tollway
Ashley	Squitieri Kuffel		Business Development Director	Gasperec Elberts Consulting
Jeff	Stanko		Sr. Project Manager	HR Green, Inc.

Michael	Mendez		Director	Illinois Hispanic Chamber of Commerce
Colleen	Miller		Chief Business Development Officer	SINGH + Associates, Inc.
Sam	Mittal		Principal Project Manager	Mott MacDonald
Hamed	Mohammed		President	American Engineering Consultants, Inc
Jim	Mondel		Senior Contract Negotiator	Illinois Tollway CA
Zaida	Morillo		Vice President	V3 Companies
John E.	Naughton III, P.E.		Director of Transportation	Valdes Architecture & Engineering
John	Nelson		Vice President	Hanson Professional Services Inc.
Thomas	Ngo		President	Millennia Professional Services
Sarah	Nguyen		Marketing Coordinator	APEX Consulting Engineers, LLC
Duane	O'Laughlin		Chief Operating Officer	Ciorba Group
Olufemi	Oladeinde		Principal Engineer	SDI ENGR Corp.
Greg	Osborne		Senior Project Manager	Epstein
Hemal	Patel		President	10-4 Engineering, PLLC
Vinod	Patel		Director of Engineering	10-4 Engineering, PLLC
Brian	Pawula		Associate, Regional Manager of Transportation	Horner & Shifrin, Inc.
David	Pellizzari		NE Illinois Transportation Manager	Farnsworth Group
Dave	Pieniazek		Transportation Manager	Stantec
JenniferAllen (Jenny)	Post	—	Roadway Section Manager	Burns & McDonnell
Gary	Powell		Principal / Structural Manager	10-4 Engineering, PLLC
Valerie	Prohammer		Contract Specialist	ISTHA
Julia	Puzio		Proposal Coordinator	Mott MacDonald
Vanessa	Ramos		Senior Contract Negotiator	Illinois Tolway
Mohammed	Rashed		Director of Electrical Operations	DB Sterlin
Torres	Ratcliff		Design Manager	KDM Engineering
Jeff	Reckamp		Sr Telecom Program Manager	Farnsworth Group
James	Robinson		Operations Manager	Burns & McDonnell
Javier	Romero		Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)
Nicole	Rose		Senior Project Controls Manager	PMCS
Michael	Ross		Distribution Engineering Manager	KDM Engineering
Michael	Ruelle		Vice President	Kimley-Horn
Daniela	Salinas		Marketing	The HOH Group, Inc.
Joy	Schaad		Sr. Project Manager	Lakeshore Engineering, LLC
Jason	Schneider		SVP - Regional Manager	Collins Engineers, Inc.
Kiernan	Schock		Pursuit Manager	Globetrotters Engineering Corporation
Ann	Seagrave		Contract Analyst	Illinois Tollway
Tim	Seibt		Business Development Manager	NASHnal Soil Testing, LLC
Nihar	Shah		President	RME (Rubinos & Mesia Engineers, Inc.)
Dipak S	Shah		Executive Vice President	RME (Rubinos & Mesia Engineers, Inc.)
Ahsan	Siddiqi		President	AMES Engineering,Inc
Kevin	Siksta		Director of Transportation	SWE Solutions
Harvind	Singh		President/CEO	SINGH + Associates, Inc.
Ryan	Smith		Project Manager	Strand Associates, Inc.
Christopher	Snyder		Principal Project Manager	GFT
gordon	snyder	—	Director of Transportation	RM Chin
Takesha	Spencer		Contract Analyst	Tollway
Ashley	Squitieri Kuffel		Business Development Director	Gasperec Elberts Consulting
Jeff	Stanko		Sr. Project Manager	HR Green, Inc.

Michael	Mendez		Director	Illinois Hispanic Chamber of Commerce
Colleen	Miller		Chief Business Development Officer	SINGH + Associates, Inc.
Sam	Mittal		Principal Project Manager	Mott MacDonald
Hamed	Mohammed		President	American Engineering Consultants, Inc
Jim	Mondel		Senior Contract Negotiator	Illinois Tollway CA
Zaida	Morillo		Vice President	V3 Companies
John E.	Naughton III, P.E.		Director of Transportation	Valdes Architecture & Engineering
John	Nelson		Vice President	Hanson Professional Services Inc.
Thomas	Ngo		President	Millennia Professional Services
Sarah	Nguyen		Marketing Coordinator	APEX Consulting Engineers, LLC
Duane	O'Laughlin		Chief Operating Officer	Ciorba Group
Olufemi	Oladeinde		Principal Engineer	SDI ENGR Corp.
Greg	Osborne		Senior Project Manager	Epstein
Hemal	Patel		President	10-4 Engineering, PLLC
Vinod	Patel		Director of Engineering	10-4 Engineering, PLLC
Brian	Pawula		Associate, Regional Manager of Transportation	Horner & Shifrin, Inc.
David	Pellizzari		NE Illinois Transportation Manager	Farnsworth Group
Dave	Pieniazek		Transportation Manager	Stantec
Jennifer Allen (Jenny)	Post		Roadway Section Manager	Burns & McDonnell
Gary	Powell		Principal / Structural Manager	10-4 Engineering, PLLC
Valerie	Prohammer		Contract Specialist	ISTHA
Julia	Puzio		Proposal Coordinator	Mott MacDonald
Vanessa	Ramos		Senior Contract Negotiator	Illinois Tolway
~~Mohammed~~	~~Rashed~~		Director of Electrical Operations	DB Sterlin
Torres	Ratcliff		Design Manager	KDM Engineering
Jeff	Reckamp		Sr Telecom Program Manager	Farnsworth Group
James	Robinson		Operations Manager	Burns & McDonnell
Javier	Romero		Marketing Coordinator	RME (Rubinos & Mesia Engineers, Inc.)
Nicole	Rose		Senior Project Controls Manager	PMCS
Michael	Ross		Distribution Engineering Manager	KDM Engineering
Michael	Ruelle		Vice President	Kimley-Horn
Daniela	Salinas		Marketing	The HOH Group, Inc.
Joy	Schaad		Sr. Project Manager	Lakeshore Engineering, LLC
Jason	Schneider		SVP - Regional Manager	Collins Engineers, Inc.
Kiernan	Schock		Pursuit Manager	Globetrotters Engineering Corporation
Ann	Seagrave		Contract Analyst	Illinois Tollway
Tim	Seibt		Business Development Manager	NASHnal Soil Testing, LLC
Nihar	Shah		President	RME (Rubinos & Mesia Engineers, Inc.)
Dipak S	Shah		Executive Vice President	RME (Rubinos & Mesia Engineers, Inc.)
Ahsan	Siddiqi		President	AMES Engineering,Inc
Kevin	Siksta		Director of Transportation	SWE Solutions
Harvind	Singh		President/CEO	SINGH + Associates, Inc.
Ryan	Smith		Project Manager	Strand Associates, Inc.
Christopher	Snyder		Principal Project Manager	GFT
gordon	snyder		Director of Transportation	RM Chin
Takesha	Spencer		Contract Analyst	Tollway
Ashley	Squitieri Kuffel		Business Development Director	Gasperec Elberts Consulting
Jeff	Stanko		Sr. Project Manager	HR Green, Inc.

Anita	States		Marketing Coordinator	Peralte-Clark
Greg	Stukel		Principal	Bowman
Kevin	Swan		VP of Strategic Partnerships	KDM Engineering, LLC
Aleksandra	Tadic		Director and Office Lead	SRF Consulting Group
Beth	Tatro		VP Marketing & Communications	CHIN
Krista	Thoennes		Marketing Manager	Infrastructure Engineering Inc.
Dan	Tiltges		President	Material Solutions Laboratory Corporation
Brian	Umbright		Vice President, Transportation	EXP
Jon	Vana		President	Civiltech
Scott	VanDerAa		Senior Project Manager	CERA Solutions
Matt	Villanueva		Sr. Roadway Group Manager	Primera Engineers
Janet	Wackrow		Marketing Manager	R.M. Chin & Associates, Inc.
Samuel	Wagner		Marketing Coordinator	OSEH Inc.
Joseph	Washington		Managing Member	PMO ERP Data
Jake	Weaver		Sr. Program Manager	Parametrix
William	Whitaker		Vice President, Business Development	APEX Consulting Engineers
David	Wilkinson		Principal	SWE Solutions
Karl	Wilson		VP	BRAVO
Adam	Woods		Department Manager - Highways	Michael Baker International
John	Yonan		Vice President	Collins Engineers, Inc.
Benjamin	Zeman		Project Manager	HDR

Anita	States		Marketing Coordinator	Peralte-Clark
Greg	Stukel		Principal	Bowman
Kevin	Swan		VP of Strategic Partnerships	KDM Engineering, LLC
Aleksandra	Tadic		Director and Office Lead	SRF Consulting Group
Beth	Tatro		VP Marketing & Communications	CHIN
Krista	Thoennes		Marketing Manager	Infrastructure Engineering Inc.
Dan	Tiltges		President	Material Solutions Laboratory Corporation
Brian	Umbright		Vice President, Transportation	EXP
Jon	Vana		President	Civiltech
Scott	VanDerAa		Senior Project Manager	CERA Solutions
Matt	Villanueva		Sr. Roadway Group Manager	Primera Engineers
Janet	Wackrow		Marketing Manager	R.M. Chin & Associates, Inc.
Samuel	Wagner		Marketing Coordinator	OSEH Inc.
Joseph	Washington		Managing Member	PMO ERP Data
Jake	Weaver		Sr. Program Manager	Parametrix
William	Whitaker		Vice President, Business Development	APEX Consulting Engineers
David	Wilkinson		Principal	SWE Solutions
Karl	Wilson		VP	BRAVO
Adam	Woods		Department Manager - Highways	Michael Baker International
John	Yonan		Vice President	Collins Engineers, Inc.
Benjamin	Zeman		Project Manager	HDR

Anita	States		Marketing Coordinator	Peralte-Clark
Greg	Stukel		Principal	Bowman
Kevin	Swan		VP of Strategic Partnerships	KDM Engineering, LLC
Aleksandra	Tadic		Director and Office Lead	SRF Consulting Group
Beth	Tatro		VP Marketing & Communications	CHIN
Krista	Thoennes		Marketing Manager	Infrastructure Engineering Inc.
Dan	Tiltges		President	Material Solutions Laboratory Corporation
Brian	Umbright	✓	Vice President, Transportation	EXP
Jon	Vana		President	Civiltech
Scott	VanDerAa		Senior Project Manager	CERA Solutions
Matt	Villanueva	—	Sr. Roadway Group Manager	Primera Engineers
Janet	Wackrow		Marketing Manager	R.M. Chin & Associates, Inc.
Samuel	Wagner		Marketing Coordinator	OSEH Inc.
Joseph	Washington		Managing Member	PMO ERP Data
Jake	Weaver		Sr. Program Manager	Parametrix
William	Whitaker		Vice President, Business Development	APEX Consulting Engineers
David	Wilkinson		Principal	SWE Solutions
Karl	Wilson		VP	BRAVO
Adam	Woods		Department Manager - Highways	Michael Baker International
John	Yonan		Vice President	Collins Engineers, Inc.
Benjamin	Zeman	✓	Project Manager	HDR

—

Anita	States		Marketing Coordinator	Peralte-Clark
Greg	Stukel		Principal	Bowman
Kevin	Swan		VP of Strategic Partnerships	KDM Engineering, LLC
Aleksandra	Tadic		Director and Office Lead	SRF Consulting Group
Beth	Tatro		VP Marketing & Communications	CHIN
Krista	Thoennes		Marketing Manager	Infrastructure Engineering Inc.
Dan	Tiltges		President	Material Solutions Laboratory Corporation
Brian	Umbright		Vice President, Transportation	EXP
Jon	Vana		President	Civiltech
Scott	VanDerAa		Senior Project Manager	CERA Solutions
Matt	Villanueva		Sr. Roadway Group Manager	Primera Engineers
Janet	Wackrow		Marketing Manager	R.M. Chin & Associates, Inc.
Samuel	Wagner		Marketing Coordinator	OSEH Inc.
Joseph	Washington		Managing Member	PMO ERP Data
Jake	Weaver		Sr. Program Manager	Parametrix
William	Whitaker		Vice President, Business Development	APEX Consulting Engineers
David	Wilkinson		Principal	SWE Solutions
Karl	Wilson		VP	BRAVO
Adam	Woods		Department Manager - Highways	Michael Baker International
John	Yonan		Vice President	Collins Engineers, Inc.
Benjamin	Zeman		Project Manager	HDR
